

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:14 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 179 Const Calendar Day: 737 Date: 15-Sep-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70
Precipitation None **Condition** Partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- ABF crews continuing the installation of the UHMWP plates on the frames between the two saddles per Detail 20 on the drawing sheets No. DE419OT of the submittal ABF-SUB-2171R01.
- ABF crew put in position the winch and bolted the winch end steel channel of the bottom frame, welding of the cut end plate beam is required.
- The ABF crews completed installation of 22 the HSS 76x76 galvanized posts with respect to drawing sheet No.DE419PT of the submittal ABF-SUB-2171R01. The crew also removed two mistakenly welded posts on the sides of the jacking saddle.
- The ABF crew started installing the three bottom 48 mm Diameter horizontal rollers which are located on each PWS Hauling System frame at the W-Line saddle. Drawing sheet No. DE419GT, Detail 3 and Section D of The submittal ABF-SUB-2171R01.

SCAFFOLDING:

- ABF crews continuing the assembly of the scaffolding at the E-line saddle, at the South side of pier W2.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in Secondary hauling system

Installation crew:

- Jerry Kubala (FOR.- Installation)
- Walter Hernandez
- Melgar Fleix
- Rigovento Garcia
- Ian Murphy
- Rick Clayborn
- Victor Hernandez



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 179 **Date:** 15-Sep-2011 **Thursday**

ABF crew involved in the assembly of the scaffolding:

- Obra Paulk (FOR.)
- Michael Balwinski
- Ryan Nash
- Dusten Clayborn
- Barry Rothman
- pablo Ramirez
- Carlos Bustomante

Equipments

- Lincoln Welding Machine (ABF-002082)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	IAN MURPHY	1.50	0.00	0.00	1.50		<input type="checkbox"/>
Ironworker	FOR	OBRA PAULK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CARLOS BUSTAMANTE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	PABLO RAMIREZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DUSTEN CLAYBORN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RYAN NASH	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL BALWINSKI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	1.50	0.00	0.00	1.50		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	1.50	0.00	0.00	0.00	No		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday

Attachment

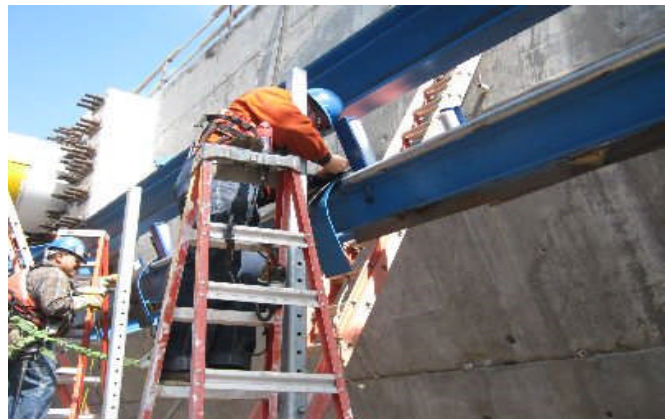

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday

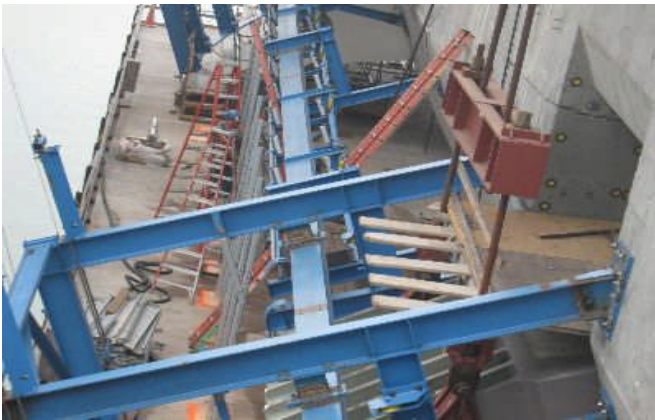

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 179

Date: 15-Sep-2011

Thursday

