

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:13 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 180 Const Calendar Day: 738 Date: 16-Sep-2011 Friday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:30 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 70**Precipitation** None**Condition** Partly CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- ABF crews continuing the installation of the UHMWP plates on the frames between the two saddles per Detail 20 on the drawing sheets No. DE419OT of the submittal ABF-SUB-2171R01.
- The ABF crew completed the installation the bottom 48 mm diameter horizontal rollers which are located on each PWS Hauling System frame at the W-Line saddle and the frames between the two saddles. Drawing sheet No. DE419GT, Detail 3 and Section D, sheets No. DE419BT & No. DE419CT of The submittal ABF-SUB-2171R01.
- ABF crew supported the tip of guide cable bracket (Bracket that the top catwalk strands are going to be anchored to) by a cable connected to an angle secured at the Pier W2 as shown in the picture.

SCAFFOLDING:

- ABF crews almost completed the assembly of the scaffolding at the E-line saddle, at the South side of pier W2, only minor work needs to be done.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Walter Hernandez
- Melgar Fleix
- Rigoverta Garcia
- Ian Murphy
- Rick Clayborn

ABF crew involved in the assembly of the scaffolding:



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 180 **Date:** 16-Sep-2011 **Friday**

-Obra Paulk (FOR.)
 -Michael Balwinski
 -Ryan Nash
 -Dusten Clayborn
 -Barry Rothman
 -Pablo Ramirez
 -Carlos Bustomante

Equipments
 -Miller Welding Machine (ABF-002303)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	IAN MURPHY	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	FOR	OBRA PAULK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CARLOS BUSTAMANTE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	PABLO RAMIREZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DUSTEN CLAYBORN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RYAN NASH	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL BALWINSKI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0220406	WELDING EQUIPMENT					No		
		3.00	0.00	0.00	0.00			<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



ddrRptbyBidItem

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 180

Date: 16-Sep-2011

Friday

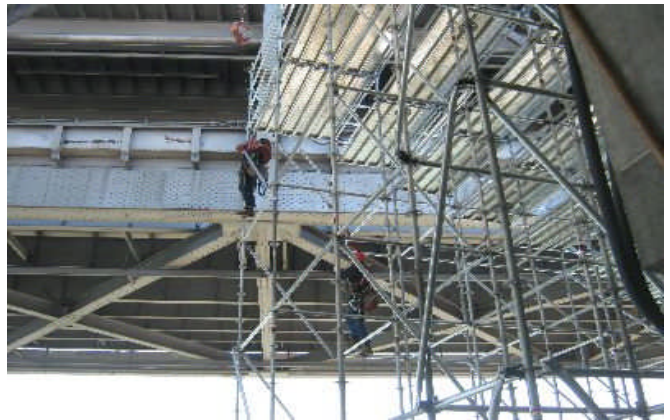

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 180

Date: 16-Sep-2011

Friday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 180

Date: 16-Sep-2011

Friday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 180

Date: 16-Sep-2011

Friday

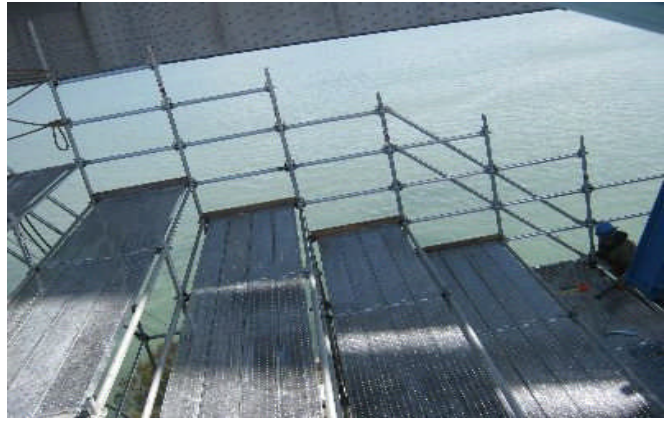

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 180

Date: 16-Sep-2011

Friday

