

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:12 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 182 Const Calendar Day: 742 Date: 20-Sep-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 4PM 70 - 80**Precipitation** None **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- ABF crews completed the installation of the UHMWP (Ultra High Molecular Weight Polyethylene) 6 mm thick Plates using ¼" countersunk screw on the on the W-Line and E-Line saddle frames and the framing system between the two saddles per Detail 20 on the drawing sheets No. DE419OT of the submittal ABF-SUB-2171R01.
- The ABF completed putting in place the horizontal rollers of the E-line frames and thus the horizontal rollers of the PWS hauling system are completed. Also all the vertical rollers are in place which can be concluded are rollers of the PWS hauling system are in place.
- Some of the PWS hauling system pieces are not still delivered to the job site, by connecting those pieces and the haul roping, the PWS system will be completed.
- The ABF crew completed cleaning the added steel pieces which were added to stabilize the PWS framing system and all the welds. The added pieces might be painted.
- ABF crew made a platform for the Tramway Anchorage Frame at Pier W2 (South).

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Walter Hernandez
- Melgar Fleix
- Rigovertto Garcia

- PWS Frames cleaning:

-John Power



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 182 **Date:** 20-Sep-2011 **Tuesday**

-Tramway Anchorage Platform
-Rigoberto Campos
-Victor Hernandez

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	RIGOBERTO CAMPOS	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	JOHN POWER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0220406	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No		<input type="checkbox"/>


04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment

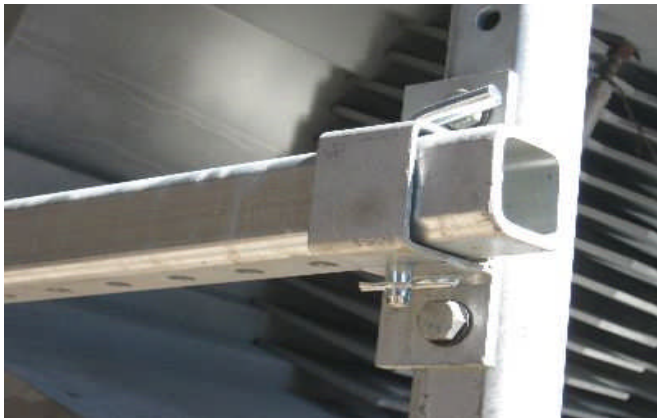

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 182

Date: 20-Sep-2011

Tuesday

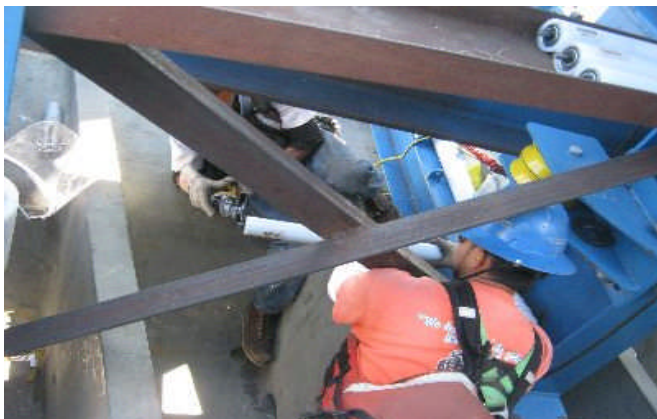

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 182

Date: 20-Sep-2011

Tuesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 182

Date: 20-Sep-2011

Tuesday

