

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:08 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 186 Const Calendar Day: 748 Date: 26-Sep-2011 Monday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 4PM 70 - 80**Precipitation** None **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- Adding the steel channel sections at the lower part of the saddles frames in order to install the hydraulic jack pressure gage. For each hydraulic jack a pressure gage is being installed.
- The bracket of the horizontal arms of the vertical HSS 76x76x9.5 posts were rotated 180 degree in order to eliminate the sharp edge while the PWS is lowered from the roller system to be positioned in its final position. The pictures for both conditions are attached.
- The PWS transition brackets for both the North and South side of the pier W2 have been brought on the pier W2 for installation.
- The pictures of all the out-haul sheaves which are located between the W-Line and E-line saddles are attached to show the position of the wire rope. The sheaves with both in-Haul and out-haul wire rope are located on the frames adjacent to the W-Line and E-Line saddles.
- The only sheave which the wire rope doesn't touch the sheaves, is the first sheave of the first frame at the W-line which ABF might leave it as it is.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Melgar Fleix
- Rigovento Garcia
- Walter Hernandez
- Eulises Torres

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 186 **Date:** 26-Sep-2011 **Monday**

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Operator	APP	EULISES TORRES	6.00	0.00	0.00	6.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday

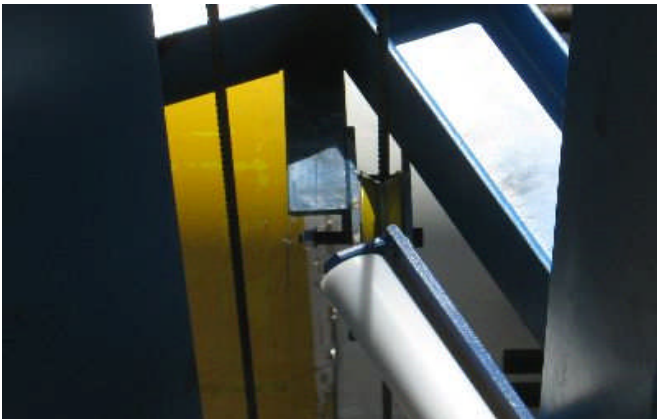

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday

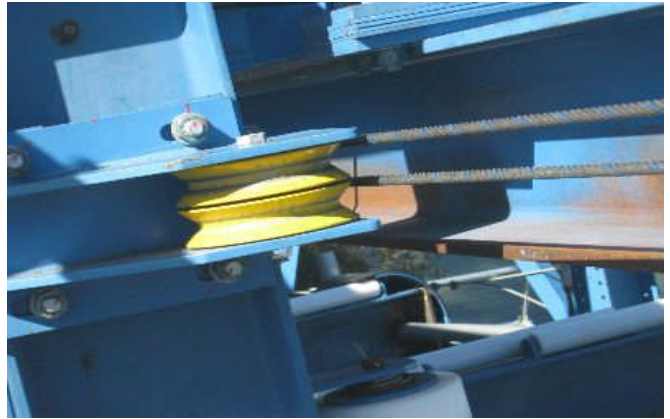

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 186

Date: 26-Sep-2011

Monday

