



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:03 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 191 Const Calendar Day: 755 Date: 03-Oct-2011 Monday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70

Precipitation None

Condition Mostly cloudy, light rain

Working Day ☒ If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-2171R01, "PWS Restraint System at Pier W2".
- ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".

INSTALLATION:

- ABF crews are continuing the work on connecting of the hydraulic hoses between the hydraulic jacks of all the steel frames.
- ABF crew started filling up the caps of Macalloy rods with grease which its specification is shown on the pictures.
- ABF crews completed installing the Transfer Arms at the South side of Pier W2 after leveling the concrete surface either with shims or combination of shims and underneath plate.
- ABF crews welded the thick washer of the anchor bolts used in the Transfer Arms at the North side of Pier W2 to the plate of the bottom plate of the Transfer arm, since the connecting holes were oversized by torch.
- ABF Engineers, Mr. Levi Gatsos has been present in the installation process.

2-The attached pictures show the detail of the performed activities.

NOTE: The crane and the operator work overtime for the primary hauling system which is not included here.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Melgar Fleix
- Rigovertto Garcia
- Walter Hernandez
- Scott Ross (Crane Op.)

Installing the hydraulic jacks and hoses



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 191 **Date:** 03-Oct-2011 **Monday**

-Gene Pratt
-Eulises Torres

ABF Surveyors:
-James Allen
-Stephen Smith

Welding crews:
-Eric Sparks
-Paul Fambrini

Filling up the cap of Macalloy Rods with grease
-Victor Hernandez

Equipments:
-TEREX RT160 crane
- Lincoln welding machine
-Torch

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	PAUL FAMBRINI	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Surveyor	APP	STEPHEN SMITH	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Surveyor	OTH	JAMES ALLEN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	EULISES TORRES	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	3.00	0.00	0.00	0.00	No		<input type="checkbox"/>
*E0260406		5.00	0.00	0.00	0.00	No		<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton	5.00	0.00	0.00	0.00	No		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item





Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

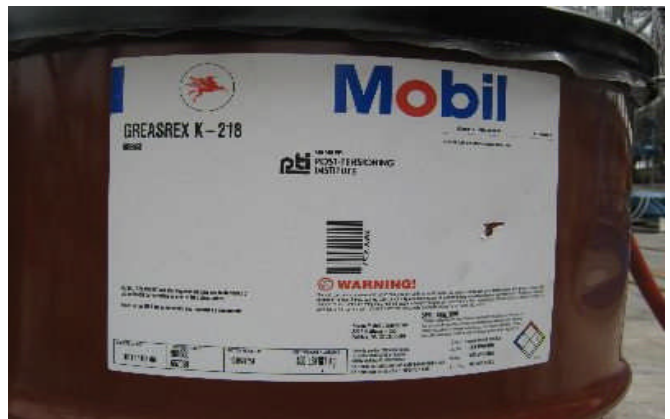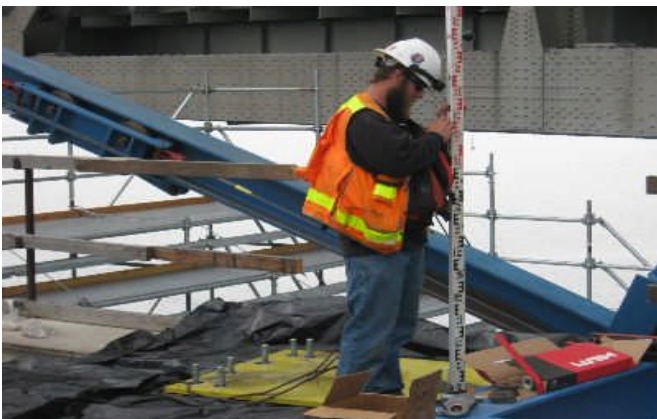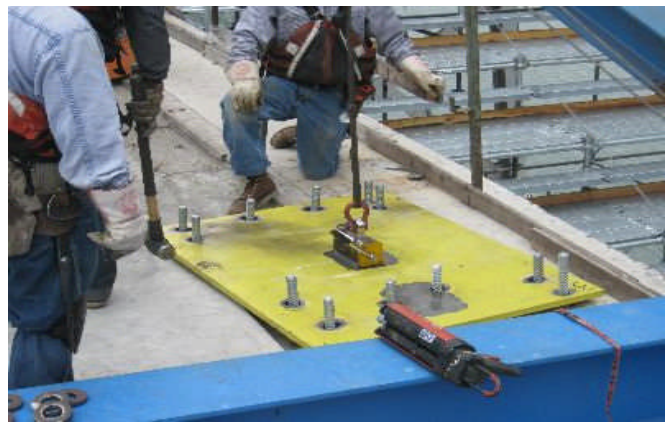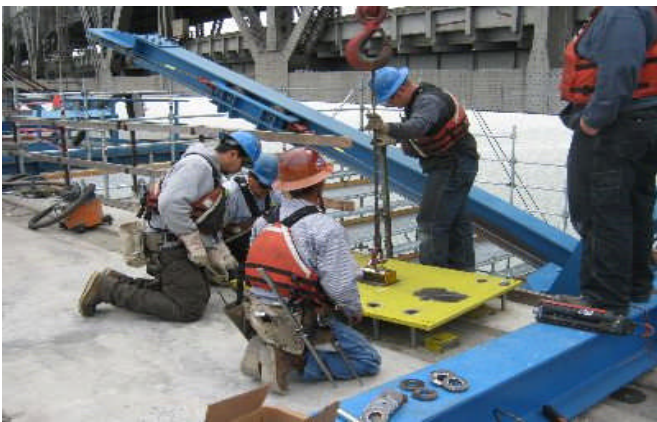

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

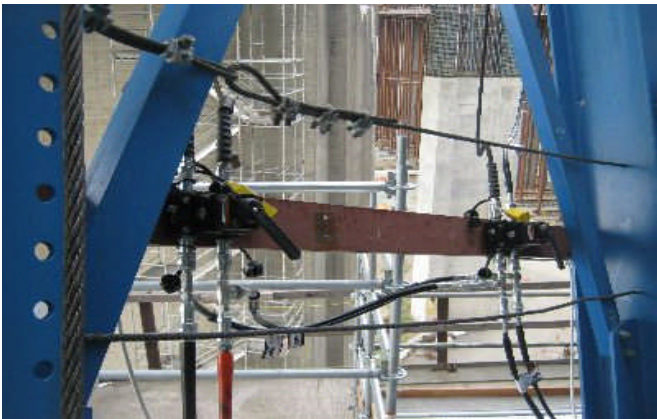

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

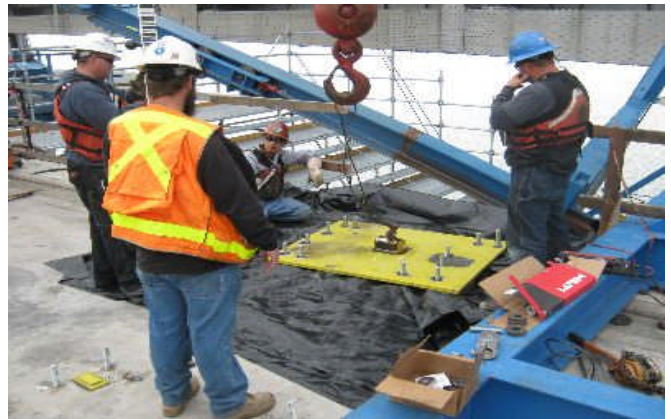

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

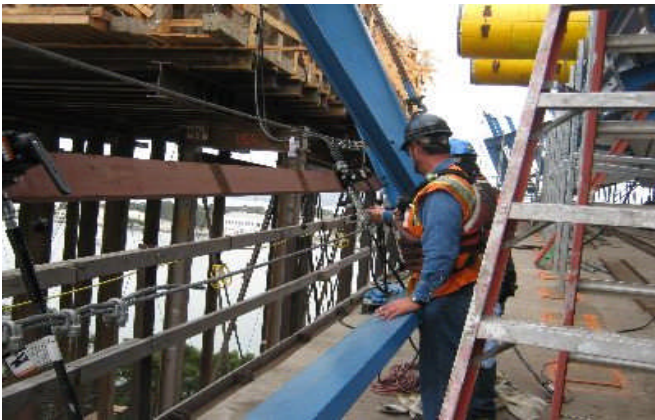

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 191

Date: 03-Oct-2011

Monday

