

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:00 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 194 Const Calendar Day: 758 Date: 06-Oct-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 70**Precipitation** None**Condition** Mostly cloudy, rain in the morning until 9:30Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-2171R01, "PWS Restraint System at Pier W2".
- ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".

INSTALLATION:

- ABF crews completed assembling the scaffolding in front of the vertical posts between the W and E line saddles. The scaffolding makes possible for the ABF crews to have access to the PWS in the hauling and positioning process.
- ABF crew transferred the winch electrical control panel from the pierW2 surface to the lower level on the deck of the pier W2 falsework under the W2 pier. By this repositioning, the control panel is protected against the rain.
- The ABF crews continued to work on the forms around the supporting plates of the transfer Arm and Tramway Anchorage Frame located at the North side of pier W2.
- The ABF mechanic, Mr. Gene Pratt, and the General Superintendent, Mr. Jerry Kent, tested different variation of Hydraulic hose arrangement to activate both Hydraulic jacks at the Jacking saddle, however only one jack was activated by the pump.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Melgar Fleix
- Rigovertto Garcia
- Walter Hernandez
- Scott Ross (Crane Op.)

Hydraulic Jack system:

- Jerry Kent
- Gene Pratt



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 194 **Date:** 06-Oct-2011 **Thursday**

-Eulises Torres

Forms for grouting under the Transfer Arm & Tramway Anchorage Frame

-Jose Prado

-Froylan Ruiz

Equipments:

-TEREX RT 160 crane ABF002154

- Generator ABF000009

-Cutting saw for forms

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Operator	APP	SCOTT ROSS	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Operator	JNM	EULISES TORRES	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FROYLAN RUIZ-AYALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	JOSE PRADO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002154	Equipment, Crane, 60 Ton	2.00	0.00	0.00	0.00		No	<input type="checkbox"/>
*E0270406		8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
9	GENERATOR, 7000 WATT	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



ddrRptbyBidItem

Page 2 of 4

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 194

Date: 06-Oct-2011

Thursday

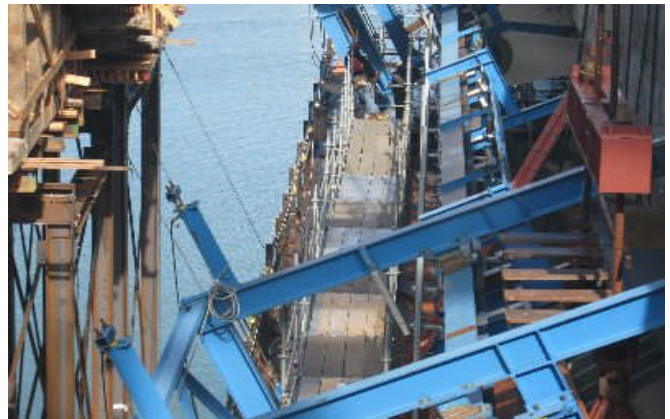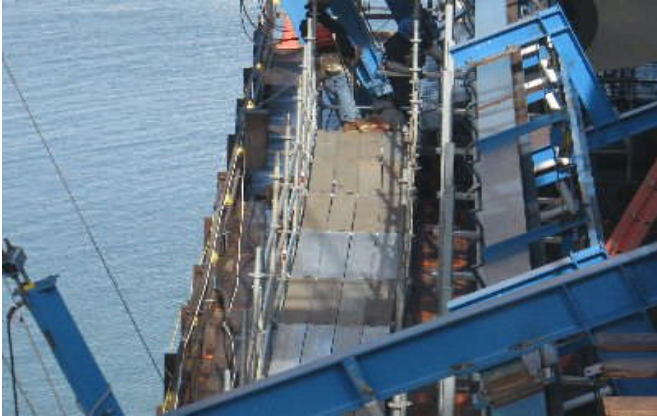

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 194

Date: 06-Oct-2011

Thursday

