

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:58 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 197 Const Calendar Day: 763 Date: 11-Oct-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 70**Precipitation** None**Condition** Partly cloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

**Work description.**

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-2171R01, "PWS Restraint System at Pier W2".
- ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".

**INSTALLATION:**

- The ABF crews completed the entrance from Pier W2 to the scaffolding located at the south side of Pier W2.
- The ABF crews replaced all the new valves, Manual 4-Way 3 Position Closed Center, with the old ones, The ENERPAC representative, Mr. Michael Sheehan, was present in the morning for 3 hours. The new and old valves are shown in the pictures. More work is done on the hydraulic jack system hoses and secured to the framing system at different locations.
- The Electrical work is being continued, two shut off limit switches are installed at both ends of the trolley rail beam ends, the wiring is connected to the control panel. As the trolley reaches these switches, the PWS hauling system is shut down. The ABF electrician is setting up a remote control key for operation of the hauling rope winch.
- The ABF crews removed the scaffolding of one of the K-Hinges of the E-line and transferred it to the South side Hinge-K of the W-line. The scaffolding makes possible for the ABF crews to install the Macalloy rod caps.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Hydraulic Jack system:

- Gene Pratt
- Eulises Torres
- Johnaton Canites
- Michael Sheehan (from ENERPAC)

Electric wiring and installing switches

- Ron Knarr



## Daily Diary Report by Bid Item

Job Name: 04-0120F4    Inspector Name Iranmanesh, Abbas    Diary #: 197    Date: 11-Oct-2011    Tuesday

-Michael Ford

Entrance to the Scaffolding:

-Froylan Ruiz

-Jose Prado

-Pedro Garcia (Scaffolding)

Replacing the scaffolding of the Macalloy rods:

-Kevin Karber

-Eduardo Jimenez

-Mike Draper

- Kevin Alger (Crane Op.)

Equipment:

-Crane Grove RT 890E

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**

AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Operator	OTH	KEVIN ALGER	3.00	2.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL DRAPER	0.50	2.00	0.00	2.50		<input type="checkbox"/>
Ironworker	JNM	EDUARDO JIMENEZ-PADILLA	2.50	0.00	0.00	2.50		<input type="checkbox"/>
Ironworker	FOR	KEVIN KARBER	3.00	2.00	0.00	5.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	JOSE PRADO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FROYLAN RUIZ-AYALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Mechanic	JNM	MICHAEL FORD	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	EULISES TORRES	7.00	0.00	0.00	7.00		<input type="checkbox"/>
		RON KNARR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	7.00	2.00	0.00	9.00		<input type="checkbox"/>

### Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0280406						No		
		4.00	0.00	0.00	0.00			<input type="checkbox"/>

**04-0120F4      Bid Item: 060      W-W2C-WDS.060      W Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      X-W2C-JKS.060      E-W Line Cross Over W2 Cap Jacking Saddle**

AMERICAN BRIDGE/FLUOR, A JV



## Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name Iranmanesh, Abbas

Diary #: 197

Date: 11-Oct-2011

Tuesday

### Attachment

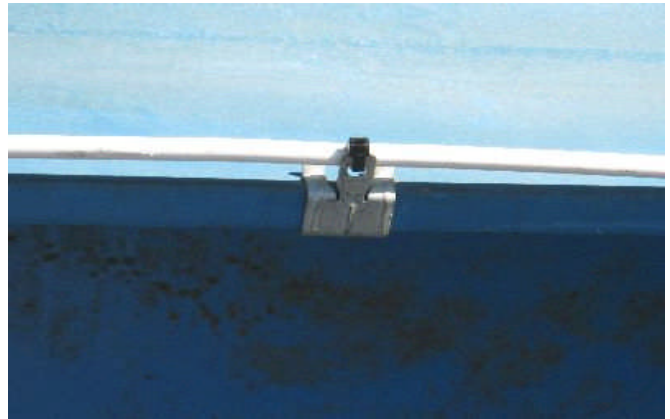



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 197

Date: 11-Oct-2011

Tuesday



## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 197

Date: 11-Oct-2011

Tuesday

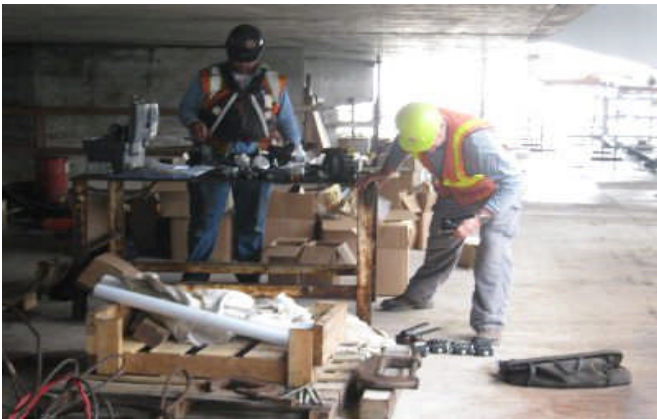



## Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 197

Date: 11-Oct-2011

Tuesday

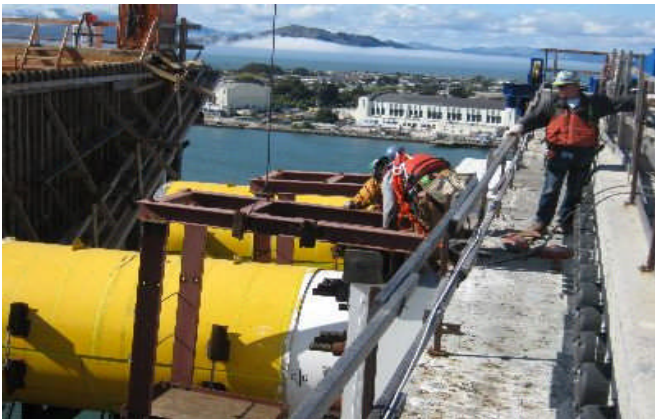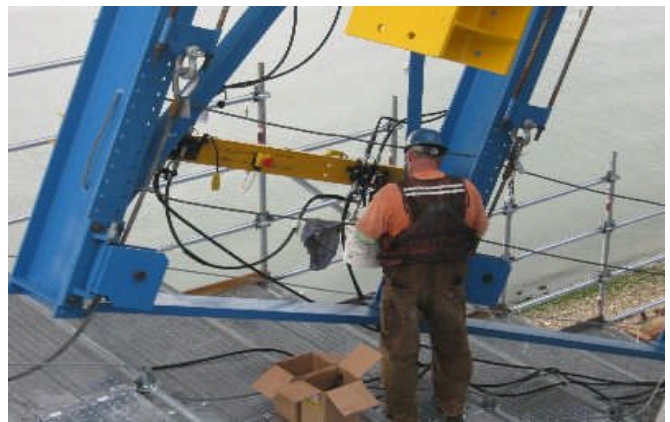

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 197

Date: 11-Oct-2011

Tuesday

