

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:56 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 199 Const Calendar Day: 765 Date: 13-Oct-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 2:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 4PM 80 - 86**Precipitation** None **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

**Work description.**

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-2171R01, "PWS Restraint System at Pier W2".
- ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".

**INSTALLATION:**

- The ABF crews continue installing the grease cap of the Macalloy rods at Hinge-K with neoprene seal washer plates with bolts at the South side of the W-line after cleaning and removing the rust.
- The ABF crew started to put in the place the final piece of the Secondary Hauling System, the plate shown as Details 10 and 11 on sheets No. DE419HT, DEDE419IT of the submittal ABF-SUB-2171R01. This plate will transfer the PWS into the slots of the saddles. Some repair is being done on these plates.
- The ABF crew completed securing the hoses and electrical wiring system by using clamps, checked and repaired and hydraulic oil leakage from the connections of hoses under 4500psi pump pressure. The operational pressure will be slightly less than 4500psi.
- The Electrical work is being continued. The ABF electrician is working on the remote control key for operation of the hauling rope winch. Six more switch limits and necessary wiring need to be done.
- The ABF crews started assembly of the scaffolding in front of the jacking saddle.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Hydraulic Jack system:

- Gene Pratt
- Eulises Torres
- Michael Ford

Jacking Saddle Scaffolding:

- Froylan Ruiz
- Jose Prado



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Iranmanesh, Abbas    **Diary #:** 199    **Date:** 13-Oct-2011    **Thursday**

Installing the grease cap of the Macalloy rods:

-Kevin Karber  
-Luis Plancarte  
-Pablo Ramirez

Assembly Plate of the Hauling System

-Jerry Kubala  
-Rigovert Garcia  
-Jose Torres

Securing the W-line Scaffolding platform

-Carlos Montejano

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**

AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	3.00	2.00	0.00	5.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	3.50	2.00	0.00	5.50		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	3.50	2.00	0.00	5.50		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	1.00	2.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	PABLO RAMIREZ	2.50	2.00	0.00	4.50		<input type="checkbox"/>
Ironworker	APP	LUIS PLANCARTE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	KEVIN KARBER	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	JOSE PRADO	4.50	2.00	0.00	6.50		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FROYLAN RUIZ-AYALA	4.50	2.00	0.00	6.50		<input type="checkbox"/>
Mechanic	JNM	MICHAEL FORD	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	EULISES TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	8.00	0.00	0.00	8.00		<input type="checkbox"/>

**04-0120F4      Bid Item: 060      W-W2C-WDS.060      W Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      X-W2C-JKS.060      E-W Line Cross Over W2 Cap Jacking Saddle**

AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 199

Date: 13-Oct-2011

Thursday

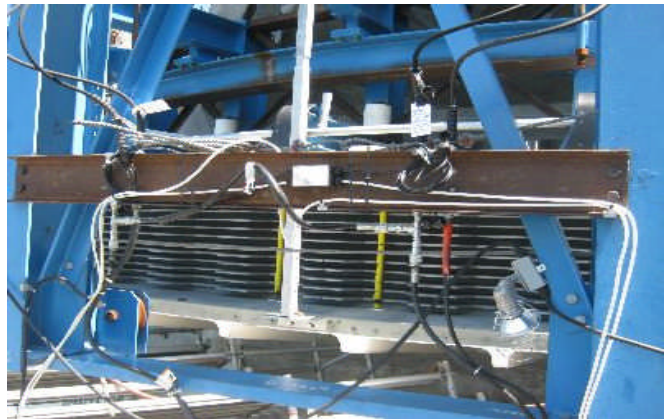



## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 199

Date: 13-Oct-2011

Thursday

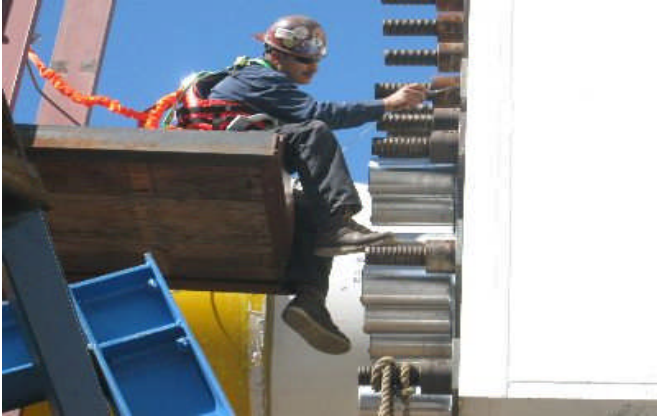



## Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 199

Date: 13-Oct-2011

Thursday

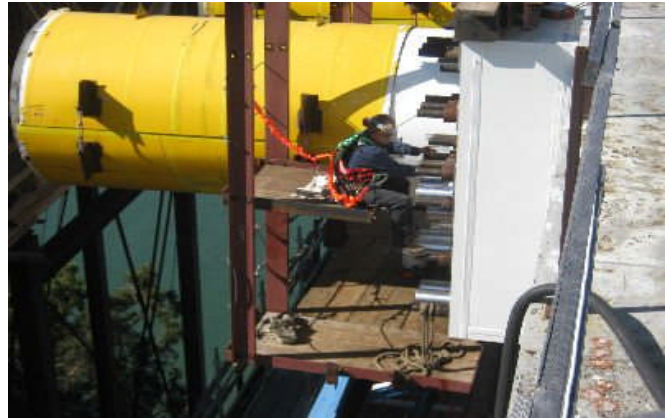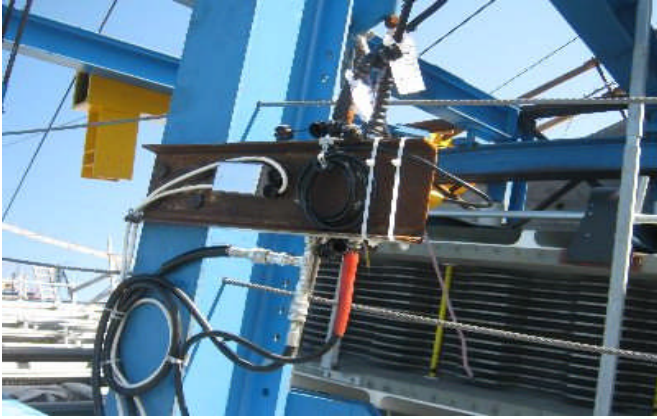

---

## ***Daily Diary Report by Bid Item***

**Job Name:** 04-0120F4

**Inspector Name** Iranmanesh, Abbas

**Diary #:** 199

**Date:** 13-Oct-2011

**Thursday**

---

