

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:44 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 214 Const Calendar Day: 784 Date: 01-Nov-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 4PM 60 - 74**Precipitation** None **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

**Work description.**

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
- ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002416R00, "West Floating Arms".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".
- ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

**INSTALLATION:**

1. The Activity at the Secondary Hauling system is as follows:

- The ABF crews organized all the Secondary Hauling System accessories and other existing pieces on the deck of the falsework at Pier W2.
- The ABF welder crews fixed the PWS sliding surface and replaced the horizontal roller bracket at four (4) locations.

2. The selected attached pictures show the detail of the performed activities.

ABF crews involved in the Secondary hauling system

PWS cross section re-construction and sliding into the saddles slot:

- Jerry Kubala
- Rigoverto Garcia
- Waler Hernandez
- Jose Torres
- Fleix Melgar

Welding crews:

- Todd Jackson
- Jayson Smith

Equipment:

Lincoln Welding Machine (ABF002082)



## Daily Diary Report by Bid Item

Job Name: 04-0120F4    Inspector Name: Iranmanesh, Abbas    Diary #: 214    Date: 01-Nov-2011    Tuesday

**04-0120F4    Bid Item: 051    0-000-000.051    ERECT STRUCTURAL STEEL (BRIDGE)**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4    Bid Item: 060    E-W2C-WDS.060    E Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	TODD JACKSON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JAYSON SMITH	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>


### Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	4.00	0.00	0.00	0.00		No	<input type="checkbox"/>

**04-0120F4    Bid Item: 060    W-W2C-WDS.060    W Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4    Bid Item: 060    X-W2C-JKS.060    E-W Line Cross Over W2 Cap Jacking Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

### Attachment

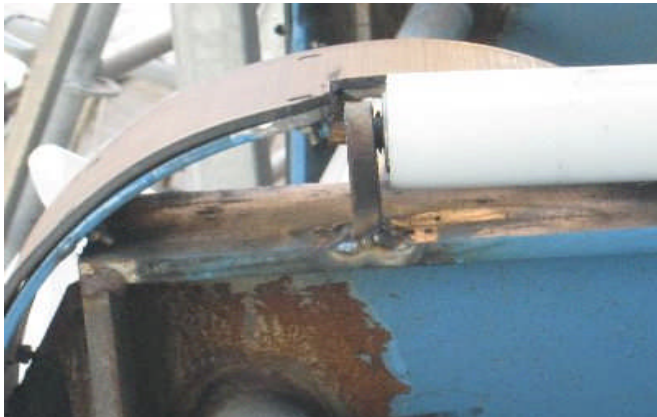

---

## *Daily Diary Report by Bid Item*

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 214

Date: 01-Nov-2011 Tuesday

---

