

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:42 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 217 Const Calendar Day: 787 Date: 04-Nov-2011 Friday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 4PM 50 - 60**Precipitation** None**Condition** Mostly CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
- ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002416R00, "West Floating Arms".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".
- ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

INSTALLATION:

1. The ABF crews set up the counterweight assembly for the primary hauling system as shown in the pictures.
2. The frame holding the counterweights was braced by the ABF welders.
3. The ABF crews installed a piece of plate as a stopper for the hydraulic jacking system. The hydraulic jack system pulls the PWS until a certain limit. The original limit was reduced by these plates.
4. The selected attached pictures show the detail of the performed activities.

ABF crews involved in the Primary Hauling System counterweight assembly:

- David Lucero (FOR.)
- Jack Hunter
- Jeff Stewart
- Roger Ruiz
- Gene Paulk

ABF welder crews:

- Earl Clayborn
- Ian Murphy

ABF crews involved in installing stoppers for the Secondary Hydraulic jacking system:

- Jerry Kubala
- Rigoerto Garcia
- Felix Melgar



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Iranmanesh, Abbas Diary #: 217 Date: 04-Nov-2011 Friday

- Kevin Alger (crane OP)

Equipments:

-Crane Grove 890E RT

-Miller welding Machine (ABF002243)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	EARL CLAYBORN	2.00	0.00	0.00	2.00		<input type="checkbox"/>
		JULIAN PAUL	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	APP	JEFFERY STEWART	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	JACK HUNTER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	DAVID LUCERO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	ROGELIO RUIZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	5.00	0.00	0.00	5.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002243	WELDING EQUIPMENT	2.00	0.00	0.00	0.00		No	<input type="checkbox"/>
*E0010583		4.00	0.00	0.00	0.00		No	<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 217

Date: 04-Nov-2011

Friday

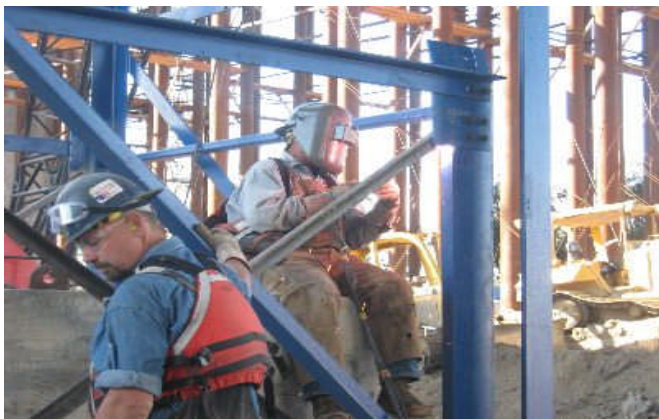

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 217

Date: 04-Nov-2011

Friday

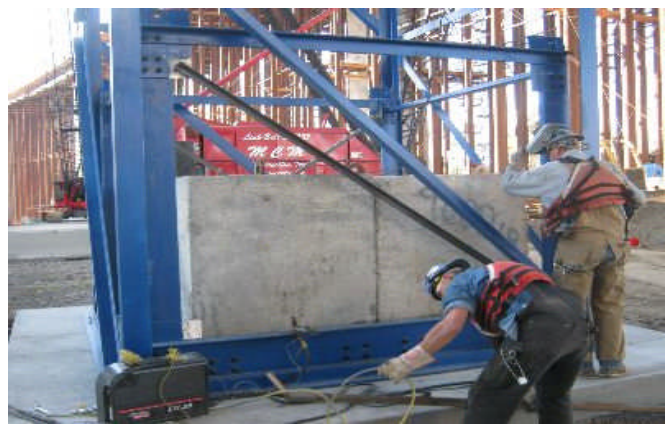

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 217

Date: 04-Nov-2011

Friday

