



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:39 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 221 Const Calendar Day: 793 Date: 10-Nov-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 60

Precipitation None Condition Clear

Working Day ☒ If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:

- 1- The crews continued working At Pier W2 with respect to some of the following submittals
 - ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
 - ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
 - ABF-SUB-002019R02, "West End Tramway".
 - ABF-SUB-002416R00, "West Floating Arms".
 - ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
 - ABF-SUB-002393R00, "Pier W2 Access Platform".
 - ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

ACTIVITIES:

1. The ABF crew continued caulking the contact edges of the Hinge-K frame with W2 concrete surface.
2. The ABF crews started assembly of different pieces of the Floating arms which were brought to the job site. At one location the holes of the hydraulic jack system and the supporting frame didn't match. It is not clear yet, what ABF will decide for correction.
3. ABF crews continued making forms for pouring counter weight concrete of the SAS deck.
4. The selected attached pictures show the detail of the performed activities.

ABF crews involved in assembly of the floating arms:

- Jerry Kubala
- Filex Melgar
- Rigoverto Garcia
- Scott Ross (Crane Op.)
- Todd Jackson
- Jose Torres
- Michael Pratt

Hinge-K frame caulking:

- Luis Diaz

Concrete Forms:

- Guillermo Limon
- Jose Avalos



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Iranmanesh, Abbas Diary #: 221 Date: 10-Nov-2011 Thursday

Equipments:

- Crane TERX RT160 (ABF002154)
- Miller Welding Machine (ABF002242)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	JOSE AVALOS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	APP	TODD JACKSON	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS DIAZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002154	Equipment, Crane, 60 Ton	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002242	WELDING EQUIPMENT	2.00	0.00	0.00	0.00		No	<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 221

Date: 10-Nov-2011

Thursday

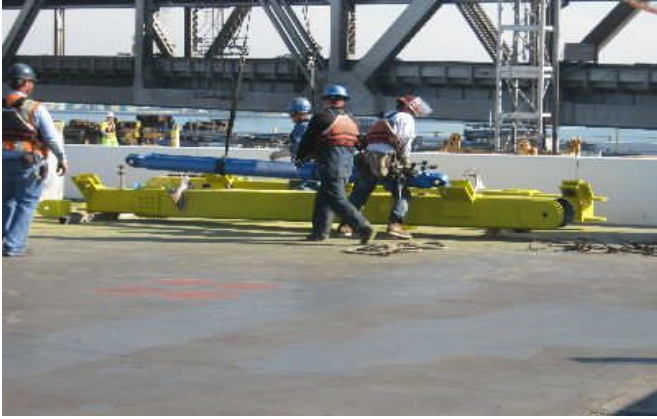

Daily Diary Report by Bid Item




Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 221

Date: 10-Nov-2011

Thursday

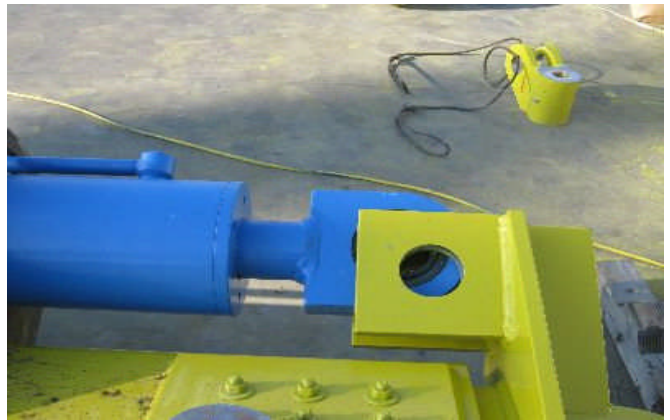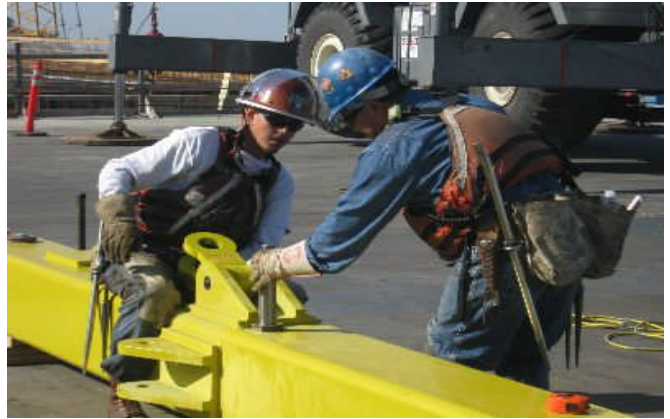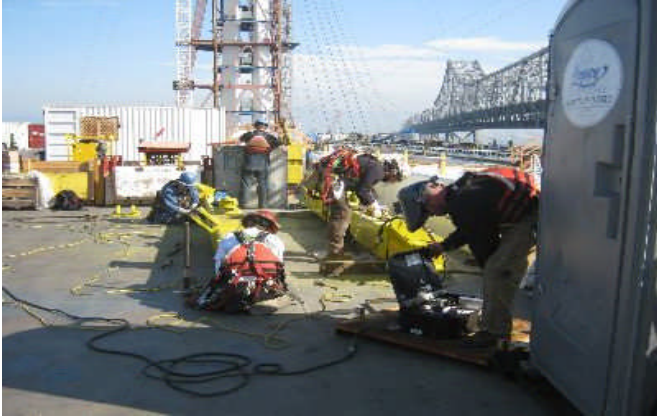

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 221

Date: 10-Nov-2011

Thursday

