

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:37 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 224 Const Calendar Day: 798 Date: 15-Nov-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 4PM 50 - 68**Precipitation** None**Condition** Partly CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

**Work description.**

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
- ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002416R00, "West Floating Arms".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".
- ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

**ACTIVITIES:**

1. The ABF crews completed the North side Transfer Arm by installing the hydraulic jack which rotates the tip of the Transfer Arm and completed bolting of the main bracket.

2. The ABF crew started installing the South side Transfer Arm at Pier W2; the holes of the bottom base plate of the main bracket didn't match the drilled holes on the deck. ABF decided to drill new holes on the bottom base plate rather than drilling new holes on the Pier W2 deck. The ABF surveyor, James Allen, transferred the location of the drilled holes on the bottom base plate. After drilling the new holes and putting in place the HILTI anchor bolts the main bracket was installed. After installation of the smaller bracket which supports the transfer arm, the extension of the main bracket center-line didn't match the center-line of the supporting bracket (smaller bracket was twisted). It is expected that ABF comes with some idea to solve the issue. The remaining work of the installation was left for the next day.

3. The selected attached pictures show the detail of the performed activities.

ABF crews involved in assembly of the South side Transfer Arm:

- Jerry Kubala
- Filex Melgar
- Rigoverto Garcia
- Scott Ross (Crane Op.)
- Enrique Robles
- Andrew Meade
- Jonathan Canites



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Iranmanesh, Abbas    **Diary #:** 224    **Date:** 15-Nov-2011    **Tuesday**

Surveyors:  
-James Allen  
-Stephen Smith

Equipments:  
-Crane TERX RT160 (ABF002154)  
-Torch

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Surveyor	APP	STEPHEN SMITH	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Surveyor	OTH	JAMES ALLEN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	6.00	0.00	0.00	6.00		<input type="checkbox"/>
Ironworker	JNM	ANDREW MEADE	6.00	0.00	0.00	6.00		<input type="checkbox"/>
Ironworker	FOR	ENRIQUE ROBLES	6.00	0.00	0.00	6.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>

### Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0320406						No		<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton	3.00	0.00	0.00	0.00	No		<input type="checkbox"/>
		8.00	0.00	0.00	0.00			<input type="checkbox"/>

**04-0120F4      Bid Item: 060      W-W2C-WDS.060      W Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      X-W2C-JKS.060      E-W Line Cross Over W2 Cap Jacking Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 224

Date: 15-Nov-2011

Tuesday

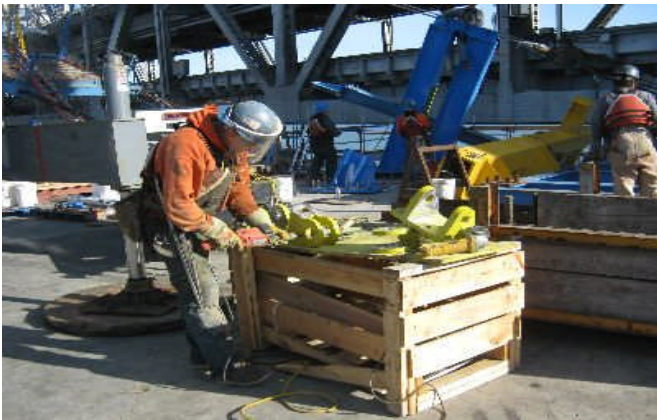



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 224

Date: 15-Nov-2011

Tuesday





## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 224

Date: 15-Nov-2011

Tuesday

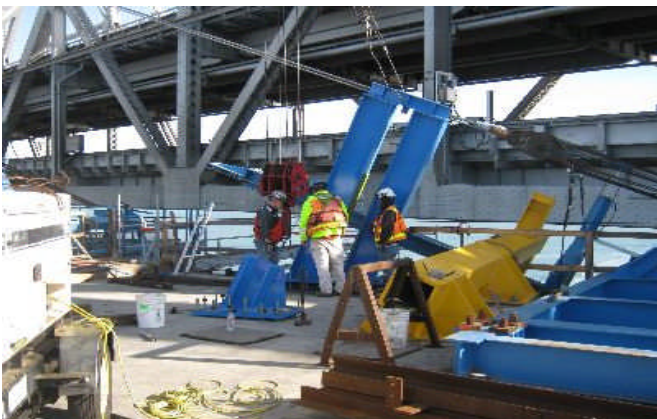

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 224

Date: 15-Nov-2011 Tuesday

