

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:31 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 230 Const Calendar Day: 805 Date: 22-Nov-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 60
Precipitation None **Condition** partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

- 1- The crews continued working At Pier W2 with respect to some of the following submittals
- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
- ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002416R00, "West Floating Arms".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".
- ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

ACTIVITIES:

1. The ABF crews adjusted the PWS catwalk roller by either extending the bracket legs by welding angles or cutting the legs in order to make it shorter. The ABF crews installed two rollers on the extension of the North catwalk and two rollers on the extension of the South catwalk so that PWS is guided to the deviation saddles.
2. The ABF crews increased the weight of the Primary Hauling System. The four 10,000 lbs concrete blocks (Total 40,000lbs) has been increased by adding four pieces of a heavy plate girder, no evaluation on the weight is performed.
3. ABF crew started caulking the circular connection boundary between the Hinge-K pipe and the frame as shown in the picture.
4. The ABF crews increased the size hole provided on the counterweight sheave bracket in order to attach a hoist to the bracket.
5. ABF crews continued painting of added steel pieces to the Secondary Hauling System. These pieces were added as bracing to stabilize the system. The connection of the framing system to the Pier W2 also was painted. All steel surfaces which might rust are being painted.
6. The selected attached pictures show the detail of the performed activities.

ABF crews involved in pier W2 activities:

- Jerry Kubala
- Rigoverto Garcia
- Filex Melgar
- Joseph Stone
- Enrique Robles
- Jonathon Canate



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 230 **Date:** 22-Nov-2011 **Tuesday**

-Scott Ross (Crane Op.)
-Victor Hernandez

Welding:
-Rick Clayborn
-Ian Murphy

Painting:
-Marc Mackey
Agustin Alenzuela
Rubin Soto
Equipments:

-Miller welding Machine (ABF002243)
-Lincoln Welding machine (ABF00074)
-Crane TEREX RT160 (ABF002154)
-Fork Lift Genie GTH 1056

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Operator	APP	SCOTT ROSS	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	3.00	1.00	0.00	4.00		<input type="checkbox"/>
		RUBIN SOTO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		AGUSTIN ALENZUELA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		MARC MACKEY	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	ENRIQUE ROBLES	3.00	1.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	6.50	2.00	0.00	8.50		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0330406							No	<input type="checkbox"/>
		0.00	1.00	0.00	0.00			
002154	Equipment, Crane, 60 Ton						No	<input type="checkbox"/>
		0.00	1.00	0.00	0.00			
000074	WELDER, LINCOLN 500-549 AMP DSL/TOW						No	<input type="checkbox"/>
		0.00	1.00	0.00	0.00			
002243	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00			




Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 230 Date: 22-Nov-2011 Tuesday

04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			

Attachment

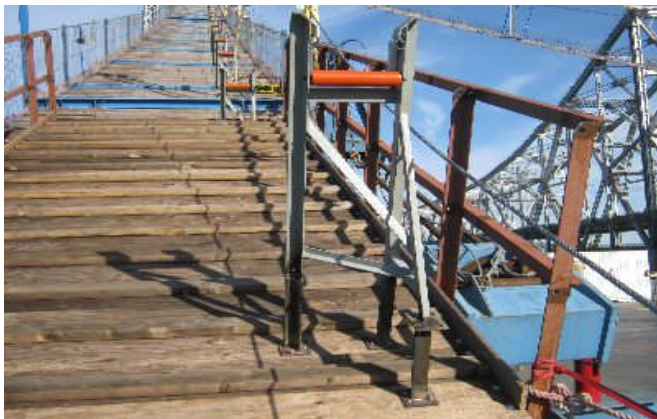

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 230

Date: 22-Nov-2011

Tuesday

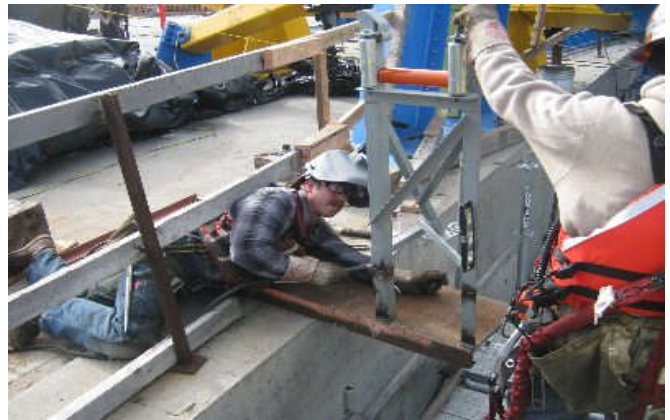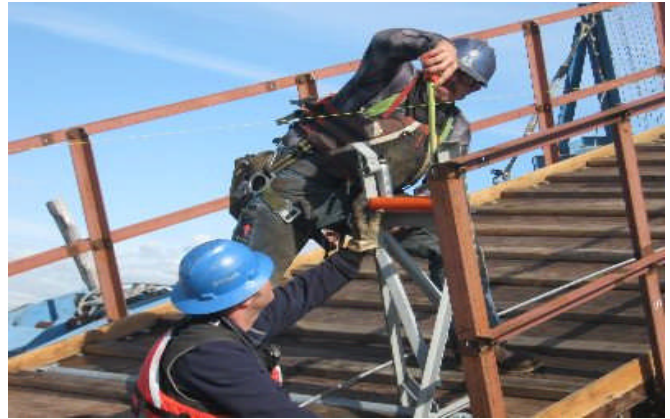

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 230

Date: 22-Nov-2011

Tuesday

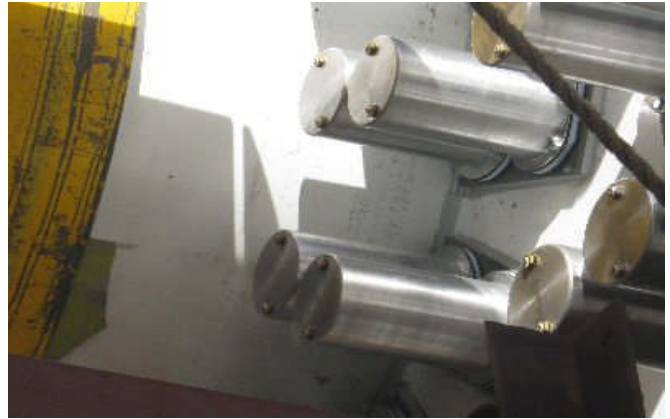

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 230

Date: 22-Nov-2011 Tuesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 230

Date: 22-Nov-2011 Tuesday

