

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:30 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 231 Const Calendar Day: 806 Date: 23-Nov-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am Break: Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 60
Precipitation None **Condition** partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

- 1- The crews continued working At Pier W2 with respect to some of the following submittals
- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
 - ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
 - ABF-SUB-002019R02, "West End Tramway".
 - ABF-SUB-002416R00, "West Floating Arms".
 - ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
 - ABF-SUB-002393R00, "Pier W2 Access Platform".
 - ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

ACTIVITIES:

1. The main activity of the ABF crews was doing some modifications on the Primary Hauling System counterweight sheave bracket. The front portion of the bracket was removed from its position and the crews welded stiffening plates at the pulley block connection. The work was supervised by Mr. Jerry Kent, the General Superintendent; the pulley block was put in place for testing after all necessary modifications were done.
2. The ABF crews repositioned one of the two Hinge-K scaffolding of the E-line; still ABF is caulking the circular connection boundary between the Hinge-K pipe and the frame as shown in the pictures.
3. ABF crews continued painting of added steel pieces to the Secondary Hauling System. These pieces were added as bracing to stabilize the system. The connection of the framing system to the Pier W2 also was painted. All steel surfaces which might rust are being painted.
4. The selected attached pictures show the detail of the performed activities.

NOTES:

- Jerry Kubala, The Foreman, hurt his finger which was caught under a thick plate around 9:00AM; he left the job site for the hospital for a check.
- ABF Engineers Mr. Adam Reeve and Mr. Scott Yeager were present at the job site.
- ABF General Superintendent, Mr. Jerry Kent and Mr. Aaron Kent supervised the work.
- The activity was stopped at 11:30 because of the holidays.

ABF crews involved in pier W2 activities:



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 231 **Date:** 23-Nov-2011 **Wednesday**

-Jerry Kubala
-Rigoverto Garcia
-Filex Melgar
-Joseph Stone
-Enrique Robles
-Jonathon Canate
-Scott Ross (Crane Op.)

Welding:
-Rick Clayborn
-Ian Murphy

Painting:
-Rubin Soto
-Javier Alcala
-Manny Berrios

Equipments:
-Miller welding Machine (ABF002243)
-Lincoln Welding machine (ABF00074)
-Crane TEREX RT160 (ABF002154)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
		MANNY BERRIOS	1.00	0.00	0.00	1.00		<input type="checkbox"/>
		JAVIER ALCALA	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	4.50	0.00	0.00	4.50		<input type="checkbox"/>
		RUBIN SOTO	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	FOR	ENRIQUE ROBLES	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	4.50	0.00	0.00	4.50		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	4.50	0.00	0.00	4.50		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002154	Equipment, Crane, 60 Ton					No		<input type="checkbox"/>
		4.50	0.00	0.00	0.00			
002243	WELDING EQUIPMENT					No		<input type="checkbox"/>
		3.00	0.00	0.00	0.00			
000074	WELDER, LINCOLN 500-549 AMP DSL/TOW					No		<input type="checkbox"/>
		1.00	0.00	0.00	0.00			



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 231 Date: 23-Nov-2011 Wednesday

04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 231

Date: 23-Nov-2011

Wednesday

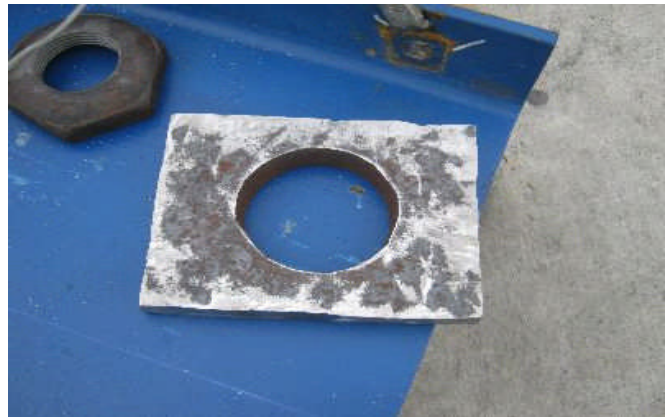

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 231

Date: 23-Nov-2011

Wednesday

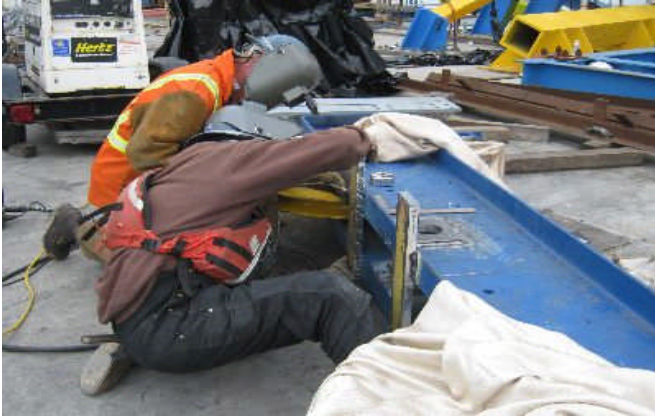

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 231

Date: 23-Nov-2011

Wednesday



Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 231

Date: 23-Nov-2011

Wednesday

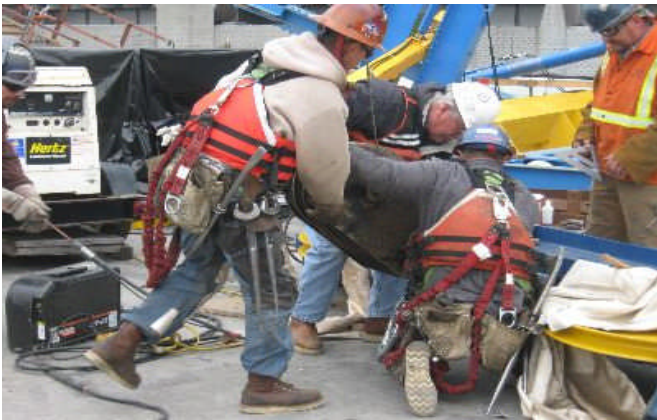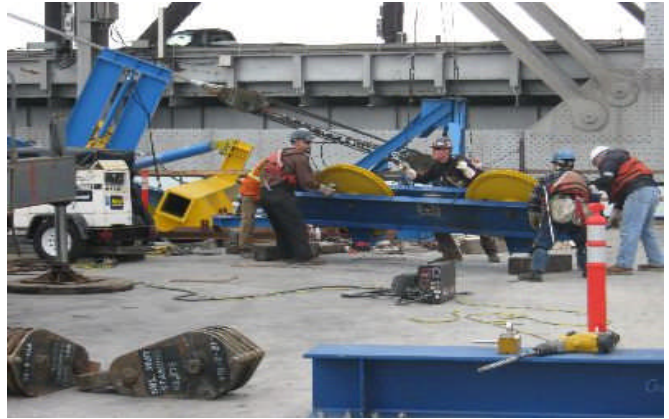

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 231

Date: 23-Nov-2011

Wednesday

