

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:26 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 236 Const Calendar Day: 815 Date: 02-Dec-2011 Friday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 4PM 60 - 70**Precipitation** None **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities:

- 1- The crews continued working At Pier W2 with respect to some of the following submittals
- ABF-SUB-002171R01, "PWS Restraint System at Pier W2".
- ABF-SUB-002283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002416R00, "West Floating Arms".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".
- ABF-SUB-002447R01, "Erection Plan (Cable)-Main Cable Strand (PWS) Erection plan".

ACTIVITIES:

1. The ABF crew installed six alarming lights; as long as the bells ring the alarming lights will be on.
2. The ABF crews cleaned the frame of Hinges K at both the W-line and E-line with the help of man gasket and crane.
3. The ABF Engineers, Mr. Levi Gatsos, measures the maximum extension of the all the Transfer Arms Hydraulic jacks and it was decided to limit the lowering of the Transfer Arm by welding a steel arm to stop it from going down further as shown in the pictures.
4. The ABF mechanics checked the hydraulic power unit and pump at the North side of Pier W2 and a powerful light (1000Watts) was installed at the corner of the North scaffolding.
5. The ABF crews continued painting of the added steel sections to the Secondary Hauling System and unpainted surfaces.
6. The selected attached pictures show the detail of the performed activities.

NOTE: The ABF Engineer Mr. Levi Gatsos was present during testing of the Transfer Arm in the morning and he measured the maximum extension of the Hydraulic jacks.

ABF crews involved in pier W2 activities:

- Jerry Kubala
- Rigoverto Garcia
- Filex Melgar
- Todd Jackson
- Eulises Torres
- Gene Pratt



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 236 **Date:** 02-Dec-2011 **Friday**

-Michael Ford
-Ron Knarr
Jose Avils
-Luis Diaz
- Bill Alger (Crane Op.)

Painting:
-Javier Alcala
-Edilberto Leon

Equipments:
-Crane Grove (890E RT)-ABF002321

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Operator	OTH	WILLIAM ALGER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
		EDILBERTO LEON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		JAVIER ALCALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		RON KNARR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS DIAZ	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	JOSE AVILA	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Mechanic	JNM	MICHAEL FORD	5.50	0.00	0.00	5.50		<input type="checkbox"/>
Operator	JNM	EULISES TORRES	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	5.50	0.00	0.00	5.50		<input type="checkbox"/>
Ironworker	APP	TODD JACKSON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002321	Equipment, Crane, 90 Ton Rough Terrain	4.00	0.00	0.00	0.00	No		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name Iranmanesh, Abbas

Diary #: 236

Date: 02-Dec-2011

Friday

Attachment

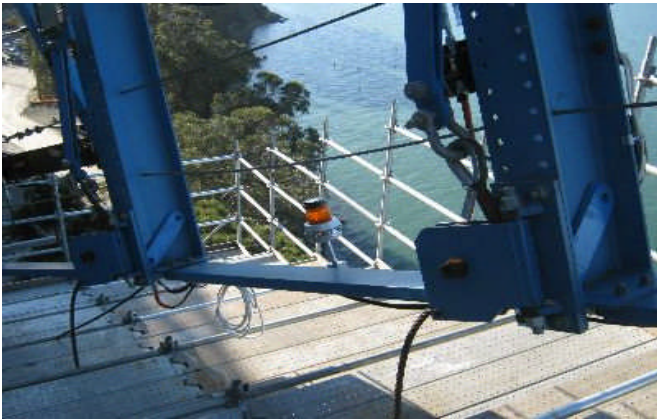

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 236

Date: 02-Dec-2011

Friday

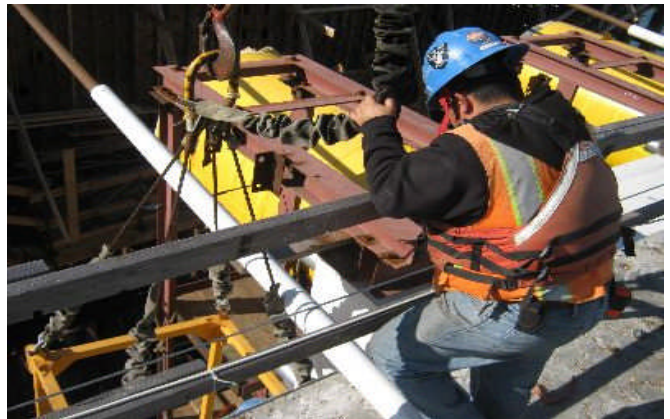

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 236

Date: 02-Dec-2011

Friday

