

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:16 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 250 Const Calendar Day: 835 Date: 22-Dec-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 58

Precipitation None Condition Clear

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

INSTALLING THE FIRST PWS



The ABF crews activities are as follow:

- The ABF crews hauled the PWS by the Hauling Arm to the East end of SAS after fixing the rollers located at the Tower.
- The ABF crews removed the twist at west loop and still they need to remove the twist on the South catwalk.
-
- The ABF crews created a slack of almost 3.0 meters (more the allowed value of 2.6 meters) by the Floating Arm at the North deviation saddle in order to side down the PWS from the rollers. The slack created by South deviation saddle was much smaller than 3.0 meters causing the center-line of the hexagonal clap moves to the North of the Jacking saddle center-line.
- The ABF crews lowered down the PWS from the rollers in front of the lower saddle slot where the first PWS is located.
- The ABF crews started forming the rectangular cross section of PWS at the Jacking saddle.
- ABF is planning to position the first PWS in position at the Jacking and deviation saddles.
- One of the brackets holding the rollers of Primary Hauling system beginning of the catwalk at the North side of pier W2 was adjusted in height.

NOTE: The ABF Engineers Mr. K. Baltezer, Mr. Scott Yeager, Mr. Levi Gatsos and the superintendent Mr. Scott Smith were present.

ABF Crews active at Pier W2:

- Jerry Kubala
- Rigoverto Garcia
- Ryan Nash
- Ryan Evanchik
- Jonathan Canites
- Joseph Stone
- Mike portillo
- Kevin Karber
- Luis Plancarte
- James Wilkerson
- Lance Carlson
- Mike Draper



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 250 Date: 22-Dec-2011 Thursday

-Tony Miranda
-Victor Hernandez
-Jose Avila

Equipments:
-Lincoln Welding Machine (ABF002082)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV


04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment

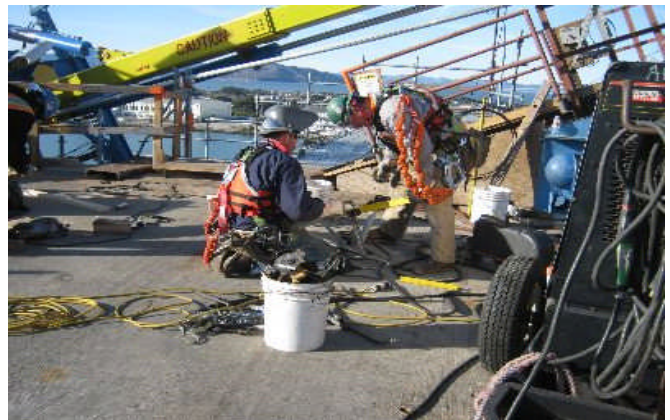

Daily Diary Report by Bid Item




Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 250

Date: 22-Dec-2011

Thursday

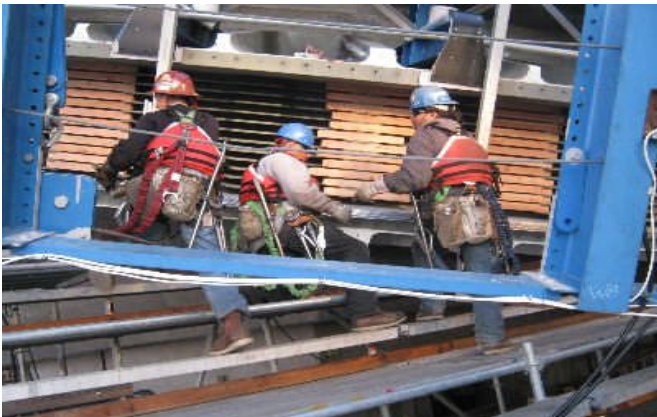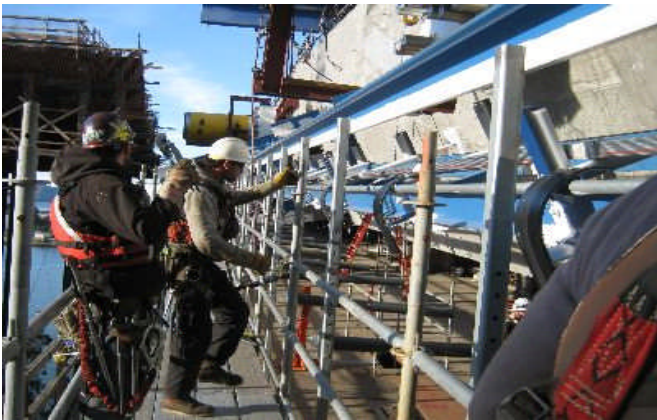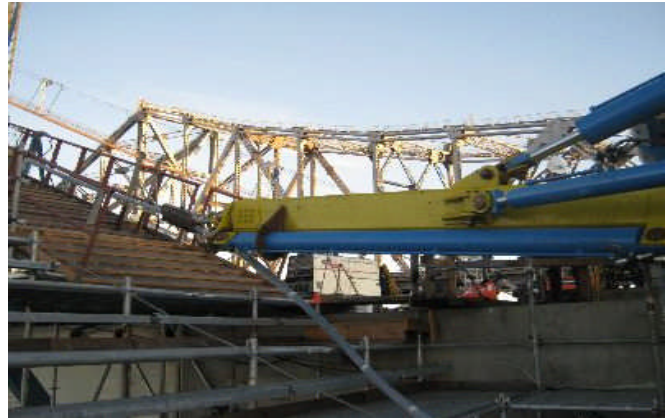

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 250

Date: 22-Dec-2011

Thursday

