

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:15 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 251 Const Calendar Day: 836 Date: 23-Dec-2011 Friday
Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer
Inspection Type: Intermittent
Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:
Federal ID:
Location:
Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 58
Precipitation None Condition Clear

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

INSTALLING THE FIRST PWS



The ABF crew's activities are as follows:

- Sliding the PWS inside the saddles was done with the help of both the Floating arms and the Hydraulic jacking systems provided at the frames of the saddles.
- The ABF crews formed the first PWS in the jacking saddle position and put it in place inside the saddle slot with the correct position of all the PWS wire, the red and blue wires in the correct position.
- The ABF crews started to put in place the PWS inside the slot of the North and South deviation saddles, in two different groups of crews.
- For the North deviation saddle all the wires of the PWS put in the correct position inside the saddle slot starting from the South up to the North, except the last five feet. The crews left the correction since it was the end of working day.
- For the South deviation saddle the wires of the PWS put in place inside the saddle slot starting from the North. Wire crossing of the red wire exists up to about four feet and after that all the wires are in the correct position. The work is not complete yet, the last five feet remained to be done.
- Successive pictures are taken from the wires position for both Deviation saddles. However, PMIV might not show them on order.

Note: ABF Engineers, Mr. K. Baltezer, Mr. K. Smith and Mr. L. Gatsos and the ABF General Superintendent Mr. Jerry Kent were present.

ABF Crews involved:

-Jerry Kubala
-Rigoverto Garcia
-Mike portillo
-Mike Draper
-Tony Miranda
-Ryan Nash
-James Wilkerson
Joseph Stone
-Jonathan Canites
-Luis Plancarte
-Lance Carlson
-Kevin Karber
-Ryan Evanchick



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 251 Date: 23-Dec-2011 Friday

-Gener Pratt
-Aaron Kent

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV


04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment

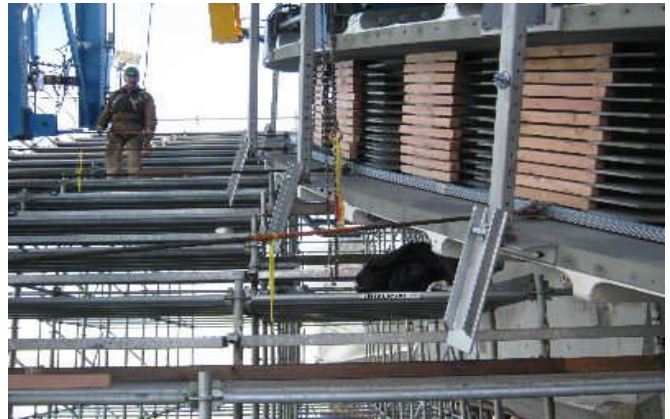

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 251

Date: 23-Dec-2011

Friday

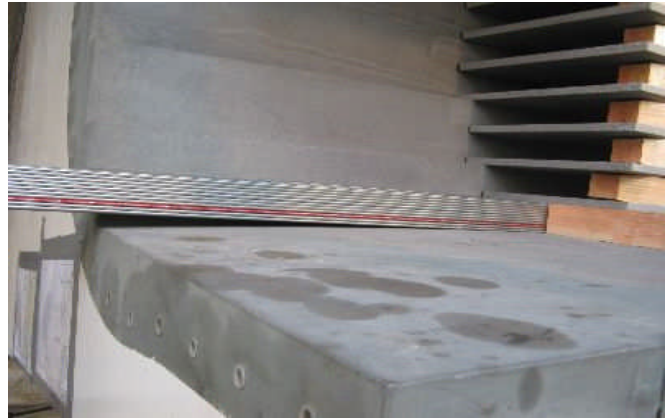

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 251

Date: 23-Dec-2011

Friday

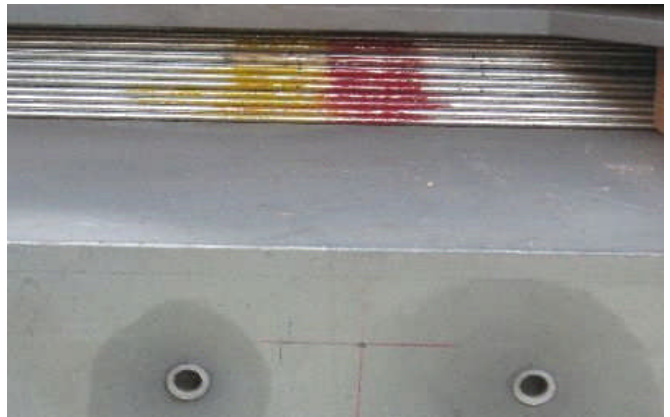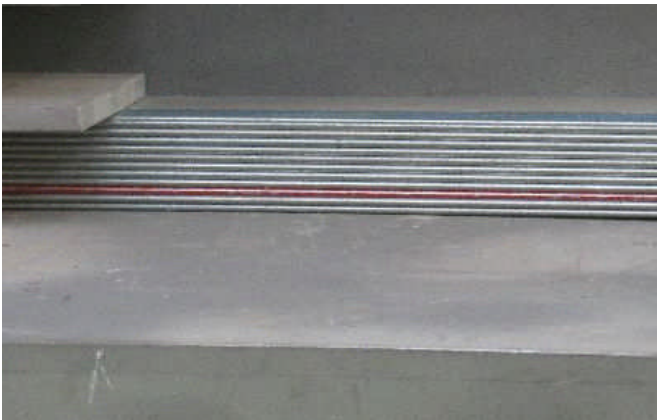

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 251

Date: 23-Dec-2011

Friday

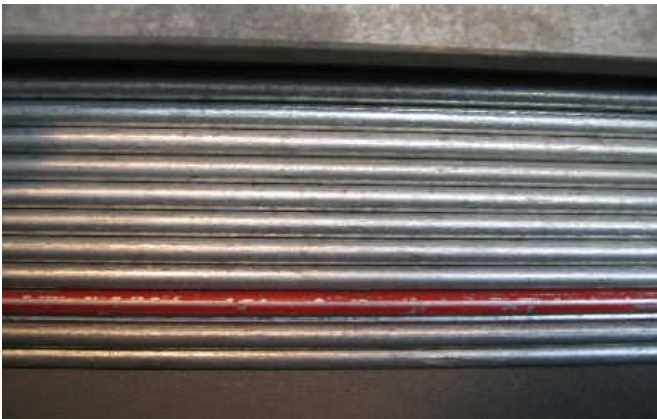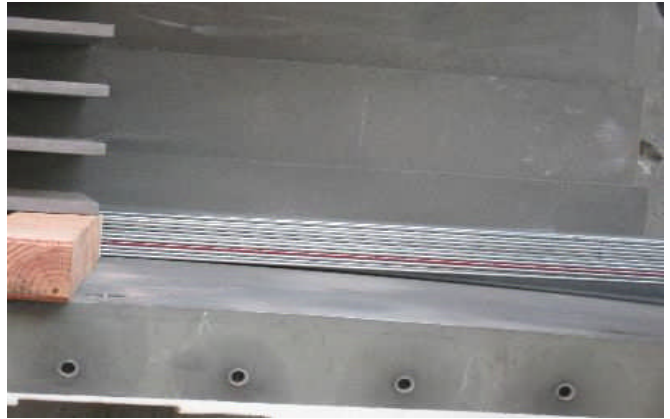

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 251

Date: 23-Dec-2011

Friday

