



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:14 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 253 Const Calendar Day: 841 Date: 28-Dec-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 58

Precipitation None Condition Clear

Working Day ☒ If no, explain:

Diary:

Dispute

Work description.



INSTALLING THE FIRST PWS AT THE WEST LOOP

The ABF crew's activities at the West loop are as follows:

- After fixing the winch on the tower, the South side PWS was put under tension of its own weight and both the North and South Floating Arms were released.
- ABF crews welded a bracket close to the Trolley at the middle of the South Deviation saddle in order to prevent uplifting of the PWS during the hauling process.
- In general the wires at the South deviation saddle cross each other. The wire at the distance of six feet for the North Deviation saddle and two feet for the South deviation saddle are crossing each other and are much disorganized as shown in the pictures.
- All the wires checked for any damage and kink at the West loop and no problem was observed.
- ABF is planning to haul the second PWS tomorrow.

ABF Crews involved:

The Following crews worked 1.5 Hours at Pier W2, the rest at some other places.

-Jerry Kubala
-Rigoverto Garcia
-Ryan Nash
-Ryan Evanchick
-Joseph Stone

The Following crews worked at some other places.

-Mike portillo
-Mike Draper
-Tony Miranda
-Luis Plancarte
-Lance Carlson
-Kevin Karber
-Jim Benninghove
-Jonathan Canites



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 253 Date: 28-Dec-2011 Wednesday

Equipment:
Lincoln Welding Machine (ABF-000074)

ABF Crews involved:

- Jerry Kubala
- Rigoerto Garcia
- Ryan Nash
- Ryan Evanchick
- Joseph Stone

Equipment:
Lincoln Welding Machine (ABF-000074)

04-0120F4	Bid Item: 051	0-000-000.051	ERECT STRUCTURAL STEEL (BRIDGE)
-----------	---------------	---------------	---------------------------------

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4	Bid Item: 060	E-W2C-WDS.060	E Line W2 Cap West Deviation Saddle
-----------	---------------	---------------	-------------------------------------

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
-----------	---------------	---------------	-------------------------------------

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
-----------	---------------	---------------	---

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 253

Date: 28-Dec-2011

Wednesday

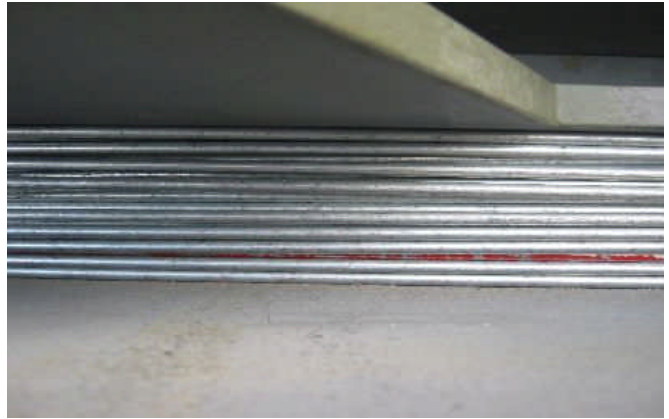

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 253

Date: 28-Dec-2011

Wednesday

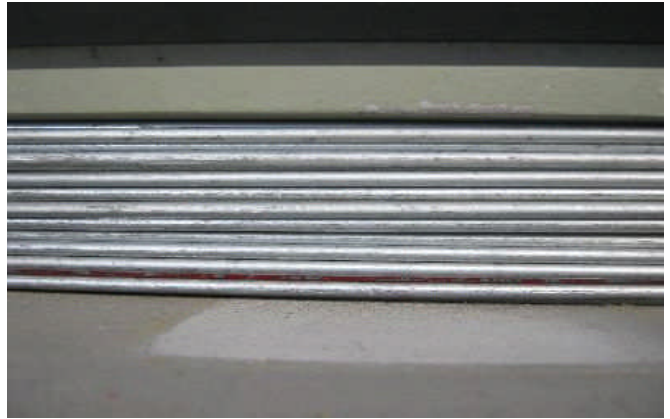

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 253

Date: 28-Dec-2011

Wednesday

