

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:17 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 254 Const Calendar Day: 842 Date: 29-Dec-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

29-Dec-11 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 40 - 50 12 PM 4PM 50 - 58**Precipitation** None**Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

THE WEST LOOP



The ABF crew's activities at the West loop are as follows:

- ABF crews welded a slotted plate in order to install a switch limit for stopping the Primary Hauling System Arm.
- ABF crews washed all the secondary hauling system and the West loop saddles by the pressured water to prevent damages due to sand blast particles to the Hauling System, Saddles, and PWS. MCM sand blasted the steel bars of YBI segment at the previous day without considering damage to the SAS Hauling system due to sand blast particles (CCO No.208).
- The ABF crews started replacing all the in-place cable clips with the CROSBY clips. It takes a few days to replace all the clips with the CROSBY type.

ABF Crews involved at the West Loop:

- Luis Plancarte (8 Hours)
- Lance Carlson (8 Hours)
- Kevin Karber (8 Hours)
- James Wilkerson (8 Hours)
- Earl Clayborn (1 Hour)
- Ian Murphy (1 Hour)
- Paul Fambrini (1 Hour)

ABF Crews Involved in CCO No. 208

- Rigoberto Campos (5 Hours+ 1 Hour OT)
- Jose Avila (5 Hours + 1 Hour OT)
- Carlos Montejano (5 Hours)
- Jesus Rodriguez (5 Hours)
- Christian Hernandez (5 Hours)

Equipment:

- Power Wash
- Manlift Genie S-125

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 254

Date: 29-Dec-2011


Thursday

04-0120F4	Bid Item: 060	E-W2C-WDS.060	E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			

Attachment

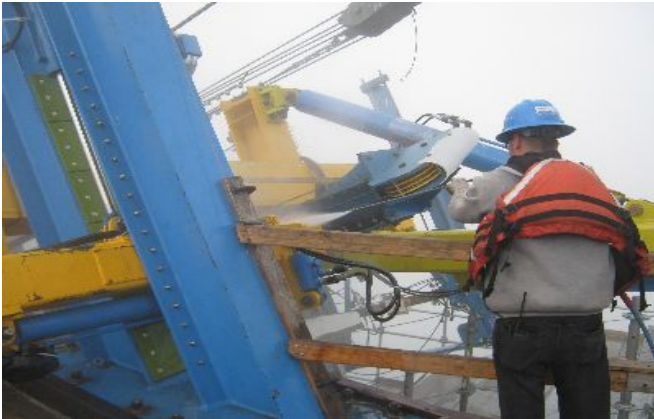

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 254

Date: 29-Dec-2011

Thursday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 254

Date: 29-Dec-2011

Thursday

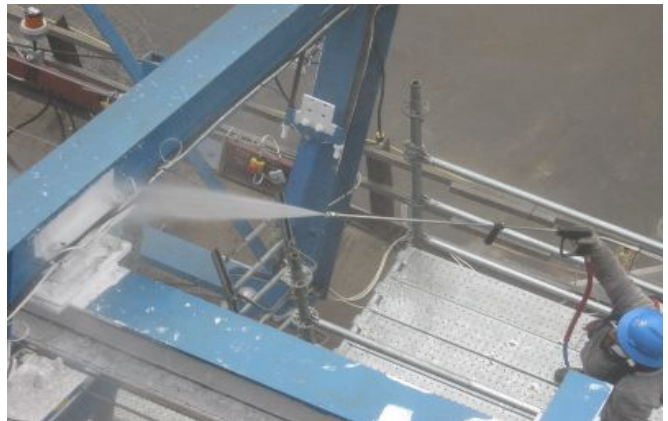

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 254

Date: 29-Dec-2011

Thursday

