

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 10:24 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 067 Const Calendar Day: 850 Date: 06-Jan-2012 Friday  
Inspector Name: Altamirano, Victor Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather**

Temperature 7 AM Below 40 12 PM 40 - 50 4PM 40 - 50

Precipitation Condition SUNNY

Working Day ☒ If no, explain:**Diary:**

Dispute

**Cable Hauling**

West End Field Work:

- Installing PWS restraint system on the north (NDS) & south Deviation Saddle (SDS).
- SDS: Removing twist and forming strand # 2. Equipment used - chainfalls, sling, rubber mallet and strand former.

- Jacking Saddle: Prepping to install strand # 2 into the saddle. Hex clamp @ centerline of jacking saddle removed. Circumferential mark for saddle is visible and near center of jacking saddle. Knife plates currently placed vertically in place before strand installation. Workers worked an 8 hour shift.

Hours Worked: 8 hours total.

**04-0120F4 Bid Item: 067 C-PWS-001.067 Install & Adjust PWS 1-5**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	MICHAEL DRAPER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL PORTILLO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	Tony Miranda	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	RYAN NASH	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	0.00	0.00	0.00	0.00		<input type="checkbox"/>

**Attachment**

ddrRptbyBidItem

Page 1 of 3

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Altamirano, Victor

Diary #: 067

Date: 06-Jan-2012

Friday




Damaged area of the trough @ bottom end of NDS



Forming @ SDS



Hex Clamp at Jacking Saddle circumferential mark

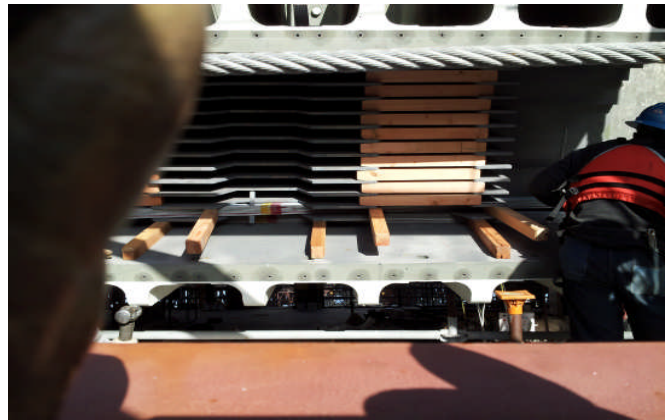

Strand # 2 installation @ Jacking Saddle



Strand # 2 floated @ NDS

Restraints attached prior to installation

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Altamirano, Victor

Diary #: 067

Date: 06-Jan-2012

Friday



Red wire at # 2 position near restraint bracket @ NDS



Strand # 2 installation at SDS
