

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:03 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 259 Const Calendar Day: 864 Date: 20-Jan-2012 Friday
Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer
Inspection Type: Intermittent
Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:
Federal ID:
Location:
Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 60
Precipitation 0.27in Condition Cloudy-Rain

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

ABF Crews activities at Pier W2:

1. The ABF crews floated PWS # 5, and completed installing the PWS at the West loop as follows:
 - At the Jacking Saddle at 7:30
 - At the South Deviation Saddle at 8:30
 - At the North Deviation saddle, the ABF continued installing until 10:45, the work was terminated because of the rain. The 7 feet remaining at the East end needs to be completed later on.
2. The quality of the work is as follows:
 - The position of the wires at the Jacking saddle and the North Deviation saddle is very good and acceptable.
 - The position of wires at the South Deviation Saddle is so that the bottom wire disappears in a 2 feet distance at the middle and 7 feet at the East end. Some pictures are attached for these locations.
 - The Hauling of the PWS # 6 started from the East end of the Deviation Saddle completed at 10:00 A.M., there is twisting on both North and South side catwalks that the ABF crews need to make the necessary action.
3. Still no adjustment on installed PWS # 3 and PWS # 4. The PWS # 3 has sag with 6 mm off from the expected value and PWS # 4 has sag which is much off from the expected value.
4. PWS # 5 requires some adjustment in order the center line of the hexagonal clamp matches the center line of the Jacking Saddle, the attached pictures shows the offset.

ABF Crews involved at Pier W2:

-Jerry Kubala
-Rigoverto Garci
-Joseph Stone
-Ryan Nash
-Ryan Evanchick
-Jonathan Canites
-Jim benninghove (10-10:45)
-Tony Miranda
-Mike Draper
-Mike portillo
-Johnathon Biskner
-Lonny Candelaria
-Matthew Holt
-Andy Zhen



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 259 Date: 20-Jan-2012 Friday

Equipment -Miller Welding Machine			
04-0120F4	Bid Item: 051	0-000-000.051	ERECT STRUCTURAL STEEL (BRIDGE)
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 060	E-W2C-WDS.060	E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-001.067	Install & Adjust PWS 1-5
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-006.067	Install & Adjust PWS 6-10
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-021.067	Install & Adjust PWS 21-25
AMERICAN BRIDGE/FLUOR, A JV			

Attachment

Daily Diary Report by Bid Item




Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 259

Date: 20-Jan-2012

Friday

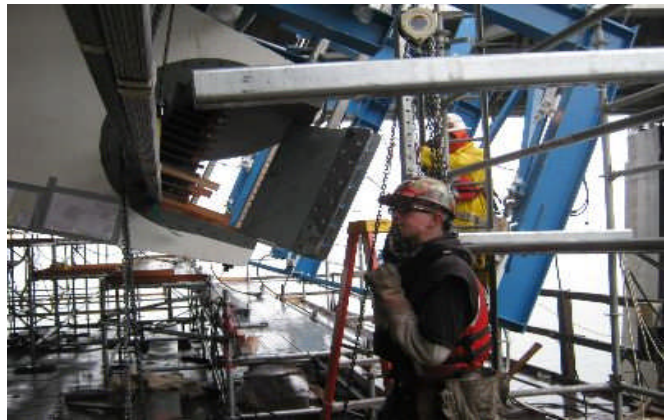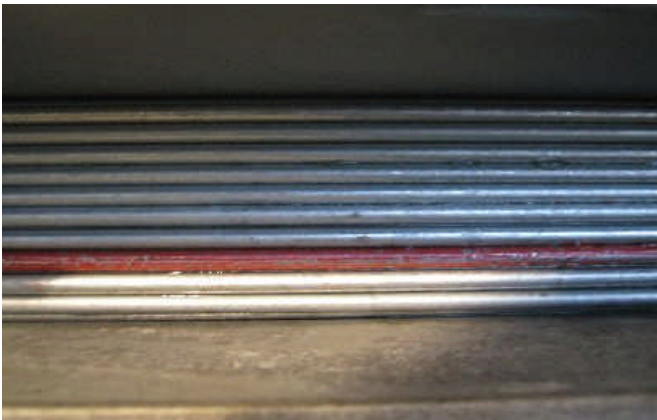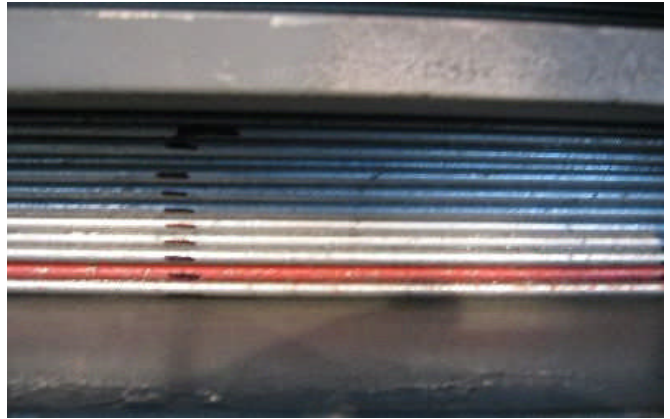

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 259

Date: 20-Jan-2012

Friday

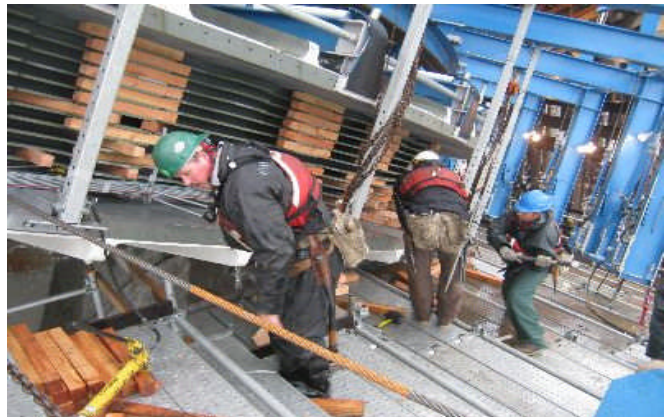

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 259

Date: 20-Jan-2012

Friday

