

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:15 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 150 Const Calendar Day: 910 Date: 06-Mar-2012 Tuesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 17:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 40 12 PM 56 4PM 52

Precipitation Condition Windy

Working Day ☒ If no, explain:**Diary:**

Dispute

Cable Hauling

East End – North Side area

Tai-Lin Liu; Diary on 03/06/12, Tuesday - Windy (37 – 54 F)

From 0700 AM to 1115 AM

- Arrived at office at 0700AM. Checked e-mail, reviewed Bob's Log sheet for strand operation, saw & talked to Daryoush & went to field. At the moment, the weather was cold and having strong wind.
 - Due to strong wind the hauling operation on strand #81 and strand # 79 installation were delay.
 - Jimmy installed coupler and extension rod for strand # 82 (Spare #S2) and checked by Eric Blue.
 - Strand # 80 was floated from main-span at 0725 AM and floated out for east saddle at 1040 AM.
 - At 0905 AM, crew connected strand #79 socket to anchor rod. I checked the screw length, but no mark at anchor rod. Asked Jimmy screwed in anchor rod all the way to the end of socket to obtain max. screw length.
 - Crew completed strand #79 installation from 0855 to 1030 AM, and completed strand hauling on strand # 81, from 0845 to 1105 AM. See Bob's log sheet for detail. Contractor called the hauling operation off at 1100 AM due to strong wind. Fish crew left job site at 1045 AM. Only 3 hauling IWS stay to finish hauling operation on strand # 81. Hauling #81 finished at 1115 AM, and IWS left job site.
 - I did measured the installed coupler and extension rod for # 82 that were:
 - * From center of coupler to end of extension rod = 575 mm = 22.638 in
 - * Coupler Length = 280 mm = 11.02 in
 - * Extension Rod Stick out length = 430 mm = 16.93 in
 - I left bridge at 1120 AM.
- From 1230 PM to 1730 PM
- Meeting to figure out the work time schedule on East End team members.
 - Performed paper works at office.
 - Refer to Bob's strand operation log sheet for tracking times of hauling operation. Labor worked hours were based on the information provided by all east end team members. OT = 2 hrs today.

☐**04-0120F4 Bid Item: 067 C-PWS-051.067 Install & Adjust PWS 51-55**

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	LANCE CARLSON	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	ROBERT RUSSELL	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	ROBERT MARTELL	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	JOSHUA JACKS	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	JAMES WILKERSON	4.00	0.00	0.00	4.00		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 150 **Date:** 06-Mar-2012 **Tuesday**

Ironworker	FOR	JAMES STURGEON	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	DANIEL MARTINEZ	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	GEN	DANIEL DUNN	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	DANIEL HUGHES	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	PATRICK OLEARY	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	APP	LUIS PLANCARTE	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	KEVIN KARBER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Engineer		ADAM REEVE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Engineer		ANKUR SINGH	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Engineer		ERIC BLUE	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Engineer		ADAM ROEBUCK	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	ANTHONY SMALER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Operator	APP	SCOTT ROSS	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JEREMY PERALTA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JUN PERALTA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	GREG WIEDER	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	RICHARD DAMBOISE	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Operator	OTH	THEODORE ROHR	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	JIMMY OSBURN	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	AARON KENT	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Operator	OTH	WILLIAM ALGER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Operator	OTH	RYAN OKU	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	BRADLEY WHITBURN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	MATTHEW CHAMBERLAIN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Electrician	GEN	RON KNARR	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Operator	JNM	JOHN GAGNON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment

Rental Company

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0150583						No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>

04-0120F4 Bid Item: 068 0-000-000.068 FURNISH SUSPENDER SYSTEM

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name Liu, Tai-Lin

Diary #: 150

Date: 06-Mar-2012 Tuesday



Strand dropped off from swift during hauling on strand # 81

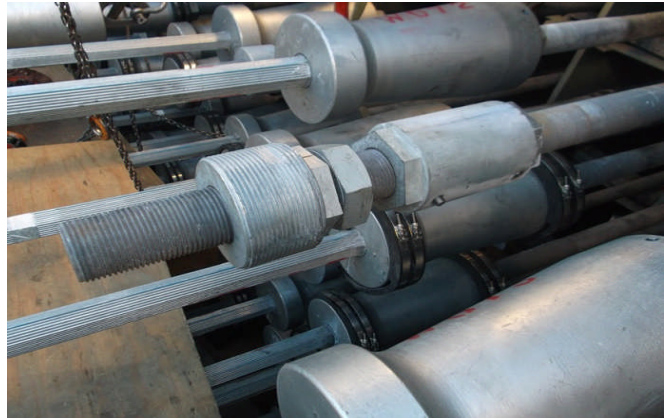

Installed Coupler & Extension Rod on strand # 82
