

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:42 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 300 Const Calendar Day: 941

Date: 06-Apr-2012 Friday

Inspector Name: Iranmanesh, Abbas

Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 11:00 am Break:

Over Time:

Federal ID:

Location:

Reviewer: Granados, Roman

Approved Date:

Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 45 - 50 12 PM 4PM 50 - 63**Precipitation** None **Condition** SunnyWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

APRIL 6, 2012 Diary

ABF Crews activities at the West Loop and West side Catwalks:

ABF crews started dismantling the hauling system and taken away the components as follows:

- 1- The ABF crews removed the Primary Hauling System hauling rope and the Hauling Arms.
- 2- The ABF crews started removing the Primary Hauling System Frames located at the West Catwalks.
- 3- The ABF crews started removing all the components of the Secondary Hauling System such as brackets, hydraulic jack hoses, cables and their extensions, sheaves, lights. Still the Secondary Hauling System Jacks are in place.
- 4- The ABF crews removed the Hydraulic arm of the North Transfer Arm and the connected hoses; however the steel frame holding it still is in place.
- 5- The power units of the Floating and the Transfer Arms were removed from the Pier W2.
- 6- The Crane Manitowoc (from 8:30A.M. to 11:00A.M.) and Crane TEREX RT160 (from 9:00A.M. to 10:30) were involved in the operation.

ABF Crews involved:

- Jerry Kubala (Foreman)
- Rigoverto Garcia
- Ryan Nash
- Jonathan Canites
- Joseph Stone
- Jim Benninghove (Foreman)
- Ryan Evanchick
- Mike Draper
- Mike Portillo
- Ronny Chamberlain
- Matthew Holt (Foreman)
- Lonny Candelaria
- Andy Zhen
- Eduardo Jimenez Padilla
- Jonathon Biskner
- Dario Loza
- Jun Peralta



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 300 **Date:** 06-Apr-2012 **Friday**

- Carlos Alvarado
- Scott Ross (Crane Op.)
- Jerry Kent (Superintendent)
- Aaron Kent (Foreman)

Equipments:

- Crane TEREX RT160
- Crane Manitowoc

04-0120F4 Bid Item: 067 C-PWS-096.067 Install & Adjust PWS 96-100
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-101.067 Install & Adjust PWS 101-105
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-106.067 Install & Adjust PWS 106-110
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-111.067 Install & Adjust PWS 111-115
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-125.067 Install & Adjust PWS 125-130
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-131.067 Install & Adjust PWS 131-135
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-136.067 Install & Adjust PWS 136-137
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 140 0-DMS-000.140 MOBILIZATION
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	MATTHEW HOLT	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	4.00	0.00	0.00	4.00		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 300 **Date:** 06-Apr-2012 **Friday**

Ironworker	APP	RYAN NASH	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	MICHAEL DRAPER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	RONNY Chamberlain	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	AARON KENT	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	LONNY CANDELARIA	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	SHAOFEI ZHEN	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	EDUARDO JIMENEZ-PADILLA	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	JONATHON BISKNER	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	DARIO LOZA	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	APP	JUN PERALTA	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	CARLOS ALVERADO	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Operator	APP	SCOTT ROSS	4.00	0.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	MICHAEL PORTILLO	4.00	0.00	0.00	4.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	
Contractor: AMERICAN BRIDGE/FLUOR, A JV						
*E0400406						
					No	
		2.50	0.00	0.00	0.00	<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton					
		2.00	0.00	0.00	0.00	<input type="checkbox"/>

Attachment



Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 300

Date: 06-Apr-2012

Friday

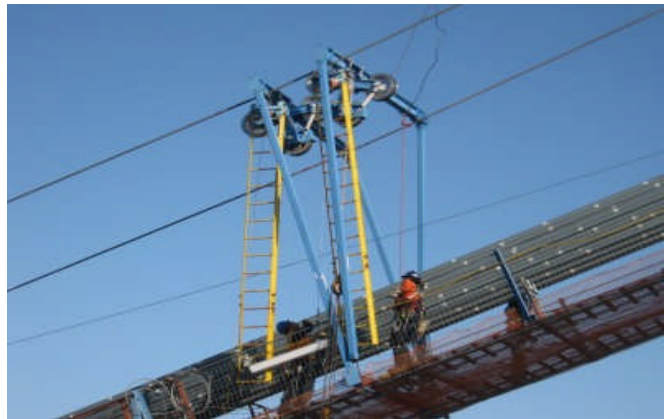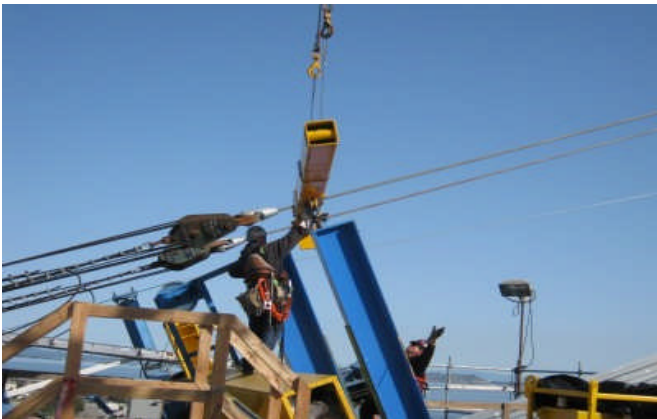

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 300

Date: 06-Apr-2012

Friday

