

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:36 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 307 Const Calendar Day: 952 Date: 17-Apr-2012 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Granados, Roman Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 68

Precipitation None Condition Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

APRIL 17, 2012 Diary

ABF Crews activities involved in the compaction of the strands at the North side of the West loop:

ABF crews continued compaction the strands of the North side of the West loop by the compacting equipment. The compaction stopped almost 6 meters from the North Deviation Saddle. Since the height at the initial points (Cable Band position) was high, about 787mm, the compacting machine was pulled back to this location and the strands were compacted again and the cable height reached an acceptable range. Point 1 is almost the edge of the first cable band (Almost 6 meters from the Jacking Saddle) and point 11 is almost the edge of the second cable band (Almost 6 meters from the North Deviation Saddle). The height, width and circumference of the cable at these locations were measure by both ABF Engineer and Caltrans and is written on the steel band at these location. The following table shows the result of these measurements.

Point Value	Measured Height (784mm+0/-8)	Measured Width (784mm+8/-0)	Circumference (2464mm+/- 12.5)	Height ABF Value	Width ABF
1	780	780	2465		
2	780	776	2470	780	
780					
3	776	781	2470	775	
784					
4	785	787	2487	783	
785					
5	786	787	2487	783	
785					
6	780	780	2466	774	
781					
7	780	781	2470	772	
780					
8	782	783	2475	783	
784					
9	778	784	2470	779	



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 307 Date: 17-Apr-2012 Tuesday

786				
10	779	779	2470	779
783				
11	784	777	2470	

The work was completed about 3:00PM and the ABF crews started disassembly of the compacting machine in order to transfer it to the tower for compaction the strands of the North side short span catwalk.
NOTE-1: ABF Engineer Mr. Levi Gatsos and ABF Superintendent Mr. Scott Smith were present.
NOTE-2: 2 hours OT

ABF Crews involved in the compaction of the strands:

- Rigoerto Garcia
- Ryan Nash
- Jonathan Canites
- James Benninghove (Foreman)
- Jerry Kubala
- Ryan Evanchick
- Mike Draper
- Mike Portilo
- Tony Miranda
- Michael Ford
- William Ager (Crane Op.)

Laborers

- Jesus Ruiz
- Jose Avalos
- Guillermo Limon

Equipments:

- Compacting equipment
- Crane Manitowoc (At Pier W2)

04-0120F4 Bid Item: 067 C-PWS-096.067 Install & Adjust PWS 96-100

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-101.067 Install & Adjust PWS 101-105

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-106.067 Install & Adjust PWS 106-110

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-111.067 Install & Adjust PWS 111-115

AMERICAN BRIDGE/FLUOR, A JV

Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 307 Date: 17-Apr-2012 Tuesday

04-0120F4 Bid Item: 067 C-PWS-125.067 Install & Adjust PWS 125-130
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-131.067 Install & Adjust PWS 131-135
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-136.067 Install & Adjust PWS 136-137
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-SUC.067 Compact Suspension Cables
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Operator	OTH	WILLIAM ALGER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Mechanic	JNM	MICHAEL FORD	0.00	0.50	0.00	0.50		<input type="checkbox"/>
Operator	OTH	WILLIAM ALGER	0.00	2.00	0.00	2.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	JOSE AVALOS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JESUS RUIZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN NASH	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	Tony Miranda	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL PORTILLO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL DRAPER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0430406							No	
		0.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0420406							No	
		8.00	0.00	0.00	0.00			<input type="checkbox"/>

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 307

Date: 17-Apr-2012

Tuesday

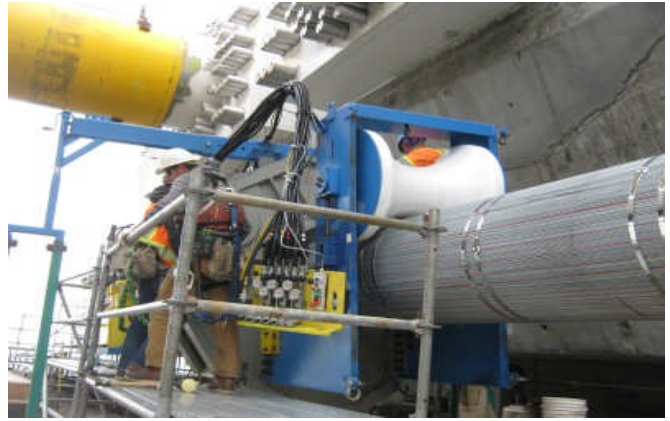

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 307

Date: 17-Apr-2012

Tuesday

