

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:31 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 189 Const Calendar Day: 283 Date: 14-Mar-2013 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 04:00 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Soheilifard, Saman Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 50 12 PM 64 4PM 63

Precipitation Condition Mostly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Paint Cable System03-14-13, Thursday, Mostly Cloudy, 46-70 F - Cable Suspender Rope Paint (North/South Main Span) ☐

- Arrived office around 07:15, checked e-mail and attending safety meeting from 08:00 - 08:35 AM. and went to field around 08:40 AM.
- At field, saw three painters performed pump & canisters cleaning at N56 area. QA/QC (Rex/Fred) were checking Gravel Grey paint at N50.
- Talked to QA Rex after he finished checking Gravel Grey on N50 - N60, he told me 7 out of 24 ropes have "holiday" on it needed to be re-painted for Gravel Grey - N56: SW, NE & NW ropes, N58: NE & NW and N60: SW & NE ropes. We talked to QC Fred and asked him to re-paint those 7 ropes for gravel grey. Warren passed the area also joined the conversation. Later on Brian was came by the area, myself & Rex talked to him about the status.
- I did measure the temperature conditions at 08:50 and 09:55, the condition did not pass at that time.
- At 10:35 AM, QC Fred measured the temperature: Humidity 74.4 %, T-Amb: 57.4F, Dew Point: 49.3F, Tw: 53F & T-Sur: 56.3, that the condition is OK to do the paint.
- At 11:25, crew performed DTM @ N50.
- Three painters cleaning suspender bracket.
- Went to NSS area to see the catwalk removal operation.
- Talk to Mahmoud and left field around 12:35 PM.
- Performed paper work after lunch.
- No OT today (03/14/13).

Attachment

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 189

Date: 14-Mar-2013

Thursday

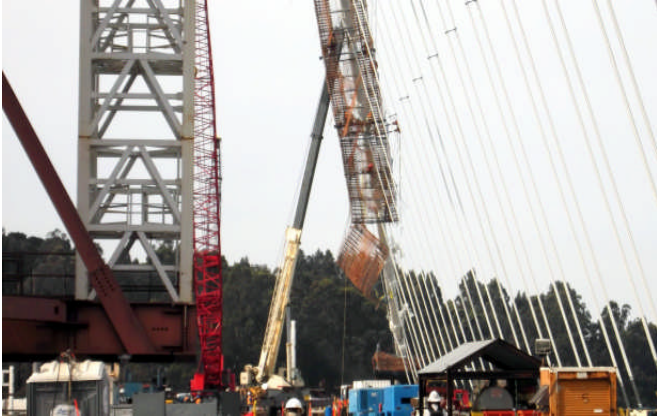

IRW's performed Catwalk removal operation at NSS



Three painters cleaned N44, 46 & 48 suspender brackets.



QA/QC checked Gravel Grey coating & 3 painters cleaned area & equipment at N50 area
