

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 8:17 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 024 Const Calendar Day: 380 Date: 19-Jun-2013 Wednesday

Inspector Name: Gagnier, Pamela Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: Over Time:

Federal ID:

Location:

Reviewer: Jefferson, Paul Approved Date: 11-Apr-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☒ If no, explain:**Diary:**

Dispute

E2 Shear Key Modifications

CCO 325 - Conco - Don McDowell (Carpenter FM - 8 hours), Ralph Gomez, Jorge Gomez, JD Freeman, Marcus McDowell, Sal Aldana, Jim Medina, Ricky Valenzuela, Danny McDowell all Carpenters. Everyone worked 8 regular hours unless otherwise noted.

Today Conco continues drilling #25 dowels.

Conco is also working on the E2 Soffit Beam mock-up. See photo below.

CCO 327 - ABF - Surveyors onsite. ABF is fabricating new access structure at pier 7. ABF is also supporting all sub-contractors on site. ABF has 2-3 engineers on site 10 to 12 hours plus safety for 2.5 hours. ABF has various equipment onsite difficult to verify all equipment in use for this CCO.

Equipment:

Total Station - 10 Hrs
Leica Level 2 each - 10 Hrs
220 KW Generator - 12 Hrs
W2 Elevator - 2.5 Hrs
6 pick up - various hrs
60 ton hydro crane - 12 Hrs
Extendable Fork Lift - 4 Hrs
4 Welders - 9 Hrs Ea
2 Grinders - 10 Hrs Ea
20 Radios - various Hrs
2 Torches - 10 Hrs Ea
Forklift Extendable - 4 Hrs

CCO 314 - ABF - See B. Wolcott's diary for ABF labor and equipment.

CCO 319 - In Place Machining (NPM) - 3 workers - T. Rouse (Tech), D. Odee (Tech), S. Mentovay (Tech) - 8 Reg Hrs and 4 OT Hrs. Finished machining angle west side at E2W - started drilling holes at this location. Moved milling machine to the south face of E2W.

Inspectors Remarks:

I worked 4 hours overtime covering field activities.



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Gagnier, Pamela Diary #: 024 Date: 19-Jun-2013 Wednesday

CCO-325 Bid Item: 001 0-CDM-EFA.325 Pier E2 Concrete Demolition

CONCO PUMPING

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: CONCO PUMPING								
Carpenter	APP	DAN MCDOWELL	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RICKY VALENZUELA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	FOR	Jim Medina	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	SAL ALDANA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	APP	Marcus McDowell	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	J.D. FREEMAN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	JORGE GOMEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RALPH GOMEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	DON MCDOWELL	8.00	0.00	0.00	8.00		<input type="checkbox"/>


CCO-327 Bid Item: 001 0-FIS-ELS.327 Pier E2 Falsework/Install Saddle

AMERICAN BRIDGE/FLUOR, A JV


Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	GEN	AARON KENT	0.00	0.00	2.50	2.50		<input type="checkbox"/>
Operator	OTH	NICOLAUS SHAFER	1.50	0.00	0.00	1.50		<input type="checkbox"/>
Ironworker	APP	REGINALD HUMPHREY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	EARL CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RICK CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RICHARD GARCIA	6.00	0.00	0.00	6.00		<input type="checkbox"/>
Operator	JNM	HOWARD SCHROYER	0.00	0.00	2.50	2.50		<input type="checkbox"/>
Ironworker	GEN	John Perine	4.00	1.00	0.00	5.00		<input type="checkbox"/>
		THOMAS FINNEGAN	8.00	0.50	0.00	8.50		<input type="checkbox"/>
Surveyor	APP	NICOLE ZBYCZIK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Surveyor	OTH	DAVID ADAMS	3.00	2.00	0.00	5.00		<input type="checkbox"/>

Attachment

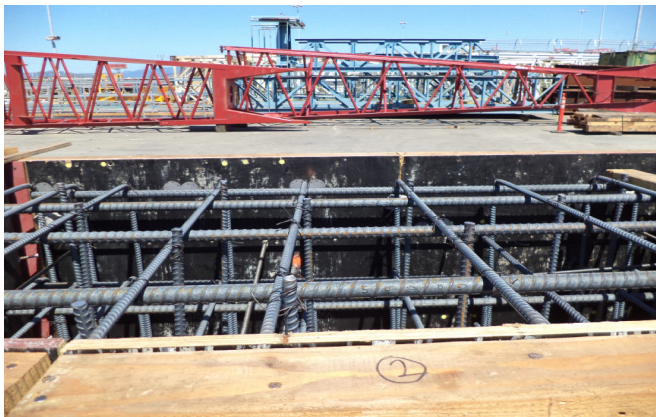

E2 Mock Up

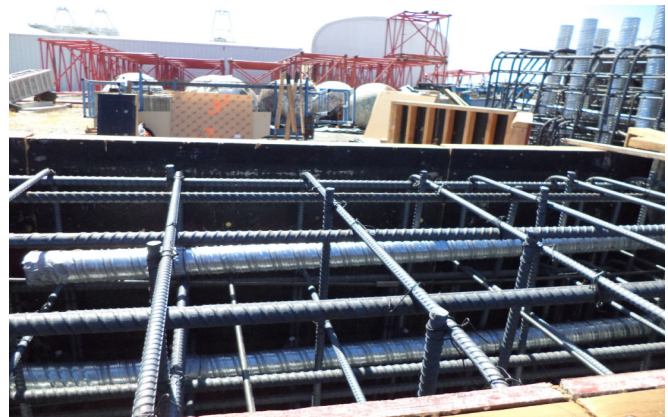

E2 Mock Up

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 024

Date: 19-Jun-2013

Wednesday

