

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 8:11 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 041 Const Calendar Day: 381 Date: 20-Jun-2013 Thursday

Inspector Name: Gagnier, Pamela Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: Over Time:

Federal ID:

Location:

Reviewer: Jefferson, Paul Approved Date: 11-Apr-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather**

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day ☒ If no, explain:**Diary:**

Dispute

**E2 Shear Key Modifications**

CCO 325 - Conco - Don McDowell (Carpenter FM - 8 hours), Ralph Gomez, JD Freeman, Marcus McDowell, Sal Aldana, Robert Garcia, Jim Medina, Ricky Valenzuela, Danny McDowell all Carpenters. Everyone worked 8 regular hours unless otherwise noted.

Today Conco continues drilling #25 dowels. Also laid out remaining dowels location for drilling around PT at E2E west. They are also drilling holes for vertical soffit dowels at E2W south side and started north side.

Conco is also working on the E2 Soffit Beam mock-up. See photo below.

CCO 327 - ABF - Surveyors onsite laying out vertical and draped tendons E2E west face. ABF is fabricating new access structure at pier 7. ABF is also supporting all sub-contractors on site. ABF is hooking up cooling system for E2 Soffit Beam mock up. ABF has 2-3 engineers on site 10 to 12 hours plus safety for 2.5 hours. ABF has various equipment onsite difficult to verify all equipment in use for this CCO.

**Equipment:**

Total Station - 10 Hrs  
Leica Level 2 each - 10 Hrs  
220 KW Generator - 12 Hrs  
W2 Elevator - 2 Hrs  
8 pick up - various hrs  
60 ton hydro crane - 12 Hrs  
Extendable Fork Lift - 8 Hrs  
3 Welders - 8.5 Hrs Ea  
2 Grinders - 10 Hrs Ea  
26 Radios - various Hrs

CCO 314 - ABF - See B. Brignano's diary for ABF labor and equipment.

CCO 319 - In Place Machining (NPM) - 3 workers - T. Rouse (Tech), D. Odee (Tech), S. Mentovay (Tech) - 8 Reg Hrs and 4 OT Hrs. Finished machining south side at E2W - continue drilling holes west side and started south side. Moved milling machine to the south face of E2W.

Inspectors Remarks:



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4

**Inspector Name:** Gagnier, Pamela

**Diary #:** 041

**Date:** 20-Jun-2013 Thursday

I worked 2 hours overtime covering field work.

**CCO-325 Bid Item: 001 0-CDM-EFA.325 Pier E2 Concrete Demolition**
**CONCO PUMPING**
**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> CONCO PUMPING								
Carpenter	APP	DAN MCDOWELL	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RICKY VALENZUELA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	FOR	Jim Medina	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	ROBERT GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	SAL ALDANA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	APP	Marcus McDowell	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	J.D. FREEMAN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RALPH GOMEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	DON MCDOWELL	8.00	0.00	0.00	8.00		<input type="checkbox"/>

**CCO-327 Bid Item: 001 0-FIS-ELS.327 Pier E2 Falsework/Install Saddle**
**AMERICAN BRIDGE/FLUOR, A JV**
**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	RICHARD CHOUINARD	4.00	1.00	0.00	5.00		<input type="checkbox"/>
Surveyor	APP	NICOLE ZBYCZIK	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		THOMAS FINNEGAN	8.00	0.50	0.00	8.50		<input type="checkbox"/>
Operator	JNM	HOWARD SCHROYER	0.00	0.00	2.50	2.50		<input type="checkbox"/>
Ironworker	JNM	RICHARD GARCIA	6.00	2.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	6.00	2.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	EARL CLAYBORN	7.00	2.00	0.00	9.00		<input type="checkbox"/>
Ironworker	APP	REGINALD HUMPHREY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Surveyor	OTH	DAVID ADAMS	5.00	1.00	0.00	6.00		<input type="checkbox"/>
Ironworker	APP	JAMES MIRANDA	0.00	0.00	2.50	2.50		<input type="checkbox"/>
Operator	JNM	JOE HERNANDEZ	1.00	2.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	MATTHEW MULLING	4.00	1.00	0.00	5.00		<input type="checkbox"/>
Ironworker	OTH	SCOTT SMITH	4.00	1.00	2.00	7.00		<input type="checkbox"/>
Operator	JNM	JEFFREY KELLER	0.00	2.00	2.50	4.50		<input type="checkbox"/>
Surveyor	APP	MICHAEL BONNICI	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Surveyor	APP	BRANDON LUBARSKY	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	RICHARD DAMBOISE	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JESUS RUIZ	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	6.00	2.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	0.00	0.00	2.50	2.50		<input type="checkbox"/>

**Attachment**


ddrRptbyBidItem

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 041


Date: 20-Jun-2013 Thursday



Machined E2W East Side



Prepared Concrete Suraced E2W East Face

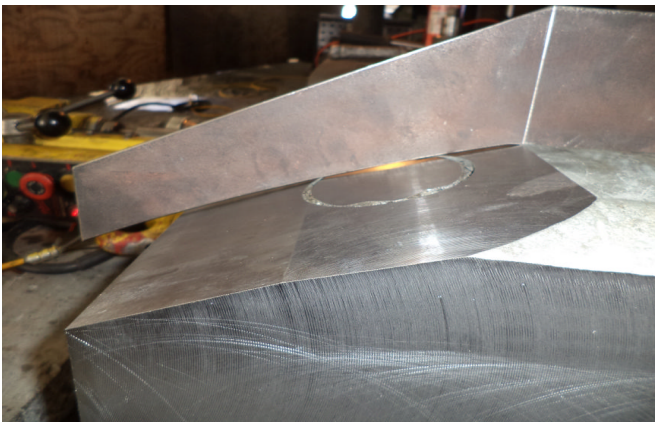

Machined E2W East Side



Prepared Concrete Surface E2W West Face



Prepared E2W North Side Soffit Surface - Drilled Dowel Holes Not Complete



Prepared E2W North Side Soffit Surface - Drilled Dowel Holes Not Complete
