

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 4:34 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 401 Const Calendar Day: 443 Date: 21-Aug-2013 Wednesday

Inspector Name: Soheilifard, Saman Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 07:30 pm Break: 00:30 Over Time: 04:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 30-May-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 60 - 70 4PM**Precipitation** none**Condition** Clear & SunnyWorking Day ☒ If no, explain:**Diary:**

Dispute

**Work description.**

Wednesday, August 21, 2013

- \* Bay Cities crew crew is on site grading and compacting soil for sidewalks;
- \* The Specialized carpenters continued with the building of the stairs and the seating in the plaza;
- \* A 3rd crew is forming the side walk;
- \* 15 Anchor Bolts for the fastening of the Light Standards arrived to the job site with the appropriate paper works and a Green Tag. The METS personnel removed the paper works and upon testing the assembly realized that the nuts for the 2" rod seized before running down.
- \* I mentioned to Rob Feather (CT engineer) and Jose Gonzalez that we need to arrange for the testing of compaction done for the soil compacted for the sidewalk. Robert indicated that he will call the lab but that he does not believe the lab personnel could make it to the site today. Jose on the other hand arranged for a compaction test to be conducted tomorrow at 7:00AM.
- \* The concrete pour for the sidewalk is scheduled for 12:00 to 13:30 tomorrow afternoon using the Mix Design: D110C5E1;
- \* Robert Wong (CT engineer in charge of SWPPP) issued a friendly warning to Don for him to remove the wood shavings off the ground at the conclusion of each shift;
- \* Two iron workers were constructing the the cages per Sections "C" & "M" of the plans for placement at the top of walls T3, T5, T6, TD, TE. They are Chris Verdon & Octavio Arciga, bith of whom are Journeymen;
- \* By 8:00 PM, the backfill for sidewalks were compacted and the 8 cages constructed, the layout line for the angles on CMU walls (for the placement of the Metal Decking) delineated. The stairs & the seats; however, are not complete, yet;
- \* Earlier today, Stanley Ku (my supervisor) spoke to Jose & labout the potential drainage problem at the podium. The drainage holes ere not necessarily located at the low points and there are 2 drainage holes which can not drain the water seeping through. This is particularly true as the surface has undulations and is rough, which obviates drainage of the intruding water further. Jose told us that he will core 4 drainage



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 401

Date: 21-Aug-2013 Wednesday

holes at the 4 corners and 4 additional ones at the low points.

More workers:

This crew was in charge of forming the side walk:

Alvarro Ibarra (Foreman); Francisco Lagarde; Doming Ibarra; Rafael Gomez; Robert Garcia;

The Bay Cities crew:

Bobby Motts (laborer); Raymon Marques; Manny Martinez; Brad Michaelson (oper);

Donny Babb (Foreman); Tony Thrush (Foreman)

Other Carpenters:

Jim Medina (Foreman); Sal Aldana; Phil Ritz; Carlos Gonzales; Eliazar Escobedo; Glen Kirkham;

Jesse Esquidel; Joseph (Jody) Freeman

|           |               |               |                              |
|-----------|---------------|---------------|------------------------------|
| 04-0120F4 | Bid Item: 081 | 0-000-000.081 | CLEAN AND PAINT CABLE SYSTEM |
|-----------|---------------|---------------|------------------------------|

CERTIFIED COATINGS COMPANY

|         |               |               |                       |
|---------|---------------|---------------|-----------------------|
| CCO-298 | Bid Item: 001 | 0-RHB-EFA.298 | IERBYS Rehabilitation |
|---------|---------------|---------------|-----------------------|

CERTIFIED COATINGS COMPANY

|         |               |               |                       |
|---------|---------------|---------------|-----------------------|
| CCO-298 | Bid Item: 001 | 0-RHB-EFA.298 | IERBYS Rehabilitation |
|---------|---------------|---------------|-----------------------|

CONCO PUMPING

|         |               |               |                      |
|---------|---------------|---------------|----------------------|
| CCO-321 | Bid Item: 001 | 0-BDW-EFA.321 | IERBYS Building Work |
|---------|---------------|---------------|----------------------|

CONCO PUMPING

### Attachment



Grading





## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 401

Date: 21-Aug-2013 Wednesday



The Bleachers




Grading/Compaction



Grading/Compaction (2)



Grading/Compaction (3)

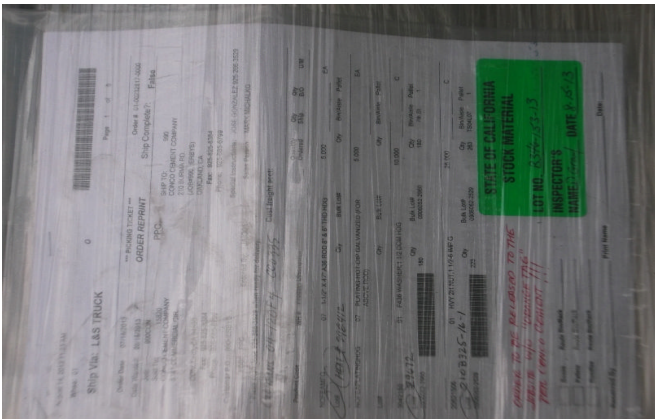

Green Tag for the Bolts used for the Light Standard



---

## ***Daily Diary Report by Bid Item***

**Job Name:** 04-0120F4

**Inspector Name:** Soheilifard, Saman

**Diary #:** 401

**Date:** 21-Aug-2013    **Wednesday**

---

