

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 5:32 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 172 Const Calendar Day: 465 Date: 12-Sep-2013 Thursday

Inspector Name: Woo, Laraine Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 05-Oct-13 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation

Condition overcast then clear, calm am, mod. Wind pm, mild

Working Day ☒ If no, explain:**Diary:**

Dispute

CCO # 98

Painting - Painters started setting up containment at the NW corner on the west side of the tower this morning at 0800 and finished at 1100. Painters started blasting area above ring beam and below elevation 19 and finished at 1400. Painters finished painting the area before end of shift at 1530.

Welding - welders continued welding the ringbeam connection on the east side of tower base and finished at around 1400. Welders then proceed to south side of tower base working on welding the ring beam to ring beam splice/connection.

See Sami Daouk's diary for other activities.

04-0120F4 Bid Item: 067 C-PWS-116.067 Install & Adjust PWS 116-120

AMERICAN BRIDGE/FLUOR, A JV

CCO-098 Bid Item: 001 T-TSD-ALS.098 Tower Skirt Details

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	LONNY CANDELARIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CARLOS ALVERADO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RENE ESQUIVEL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MATTHEW COCHRAN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JUAN HERNANDEZ	8.00	0.30	0.00	8.30		<input type="checkbox"/>
Ironworker	FOR	OBRA PAULK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	EARL CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Painter		ANTHONY KATRONES	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	JNM	JEFFREY SCOTT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	NEIL CALDWELL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Painter		RAFAEL SERRANO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Painter		LUIS PANYAQUA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Painter		RICARDO PERZILLA	4.00	0.00	0.00	4.00		<input type="checkbox"/>




Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Woo, Laraine **Diary #:** 172 **Date:** 12-Sep-2013 **Thursday**

Painter	ADILBERTO LEON	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Semi-Skilled Laborer JNM	CARLOS MONTEJANO	8.00	0.30	0.00	8.30		<input type="checkbox"/>
Equipment						Rental Company	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
000743	Marine, Barge, Flexifloat 1 EM1010					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
*E0010412	Ringer No. 1 Barge					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
CCO-321 Bid Item: 001 0-BDW-EFA.321 IERBYS Building Work							
AMERICAN BRIDGE/FLUOR, A JV							

Attachment

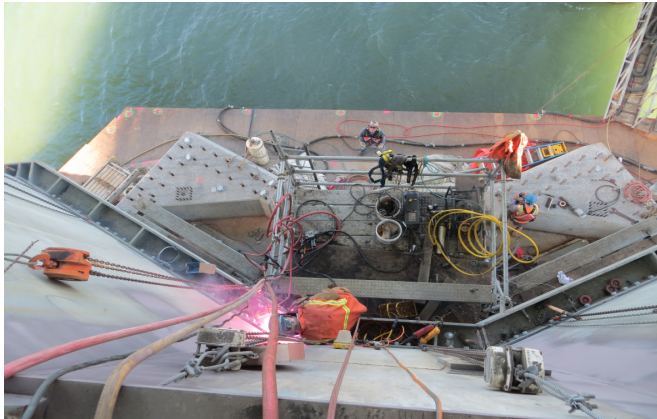

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Woo, Laraine

Diary #: 172

Date: 12-Sep-2013

Thursday

