

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 4:00 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 480 Const Calendar Day: 548 Date: 04-Dec-2013 Wednesday

Inspector Name: Soheilifard, Saman Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 05:00 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 30-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 50 - 60 12 PM 50 - 60 4PM

Precipitation none

Condition Rain

Working Day ☒ If no, explain:**Diary:**

Dispute

Work description.

Wednesday, December 4, 2013

The False work Assembly

- In the office searching for a new assignment up until 11:00 by virtue of calling and talking to managers from the OSC to the District;

- Painting the spots that were ground off rust on Monday in the South shaft continues today . The painting of these spots started yesterday. According to the Tower QA, Stuart Ross, CCC employees have worked their way down from elevation 71.0m to 65.0m as of 13:00;

- Jason Baragan is a new employee for Dutra who is starting today and Sam Tavake has returned ;

- The 3 piles numbered 7, 8, & 12 (numbering in accordance with the description provided in previous reports) were fresh-headed today- (#s 7 & 8 are on the N. W. corner of T1 and #12 on the S. E. corner);

- Pile #9 is not extended, yet;

- At about 13:00, Derrick, one of the Ballard divers, went in the water to place the top ring carrying the cable for the X-bracing of the piles to piles #6, #5, #2, and concluding with #4. Again, the numbering system is in accordance with the notes of previous reports. The cable has for pile #1 was completed this morning (see Sami Daouk's report);

- On Barge EM 1106, Walter, Allan & Gilbert are busy with the welding of stiffeners onto the false work beams;

- By 16:00, following a few trails & errors, the X-bracing for piles numbered 2, 4, , 5, & 6 was complete;

- At 16:00, the fit-up of pile #9 began and by 16:47 the welding of this 11-ft section was underway by Gilbert and Walter who were working off a bark;

- At 16:30, the 1st false work frame was being lowered in the water on the NW corner of the footing . The fit-up of this frame work continued until 17:20, during which time Walter continued with the welding of pile #9 and had it partially complete.

04-0120F4 Bid Item: 041 0-000-000.041 ERECT PRECAST CONCRETE FENDER MODULES

DUTRA MATERIALS



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 480

Date: 04-Dec-2013

Wednesday

Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: DUTRA MATERIALS								
Operator	OTH	STEVE FRIYER	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Operator	OTH	STEVE FRIYER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	WALTER QUINTERO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	ALLEN KURPIESKI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	JEFF SAINZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	GILBERT MAYA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	SAMI TAVAKE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	JNM	JON - PAUL CHENEY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	GEN	TREVER MURRAY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	APP	ROBERT UTLEY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Piledriver	APP	JAMES SAVAGE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	OTH	DAVE AVILAS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	OTH	STEVE FRIYER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Equipment								
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Rental Company	Dispute
Contractor: DUTRA MATERIALS								
*E0670562	MARINE, STEEL BARGE					No		<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0660562						No		<input type="checkbox"/>
		3.00	0.00	0.00	0.00			<input type="checkbox"/>
04-0120F4 Bid Item: 041 0-000-000.041 ERECT PRECAST CONCRETE FENDER MODULES								
BALLAD DIVING								
Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: BALLAD DIVING								
Marine Coordinator		DERDK CHASE	0.00	8.00	2.00	10.00		<input type="checkbox"/>
Marine Coordinator		TODD HORNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Underwater Diver		ALEX DOSS	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 480

Date: 04-Dec-2013

Wednesday

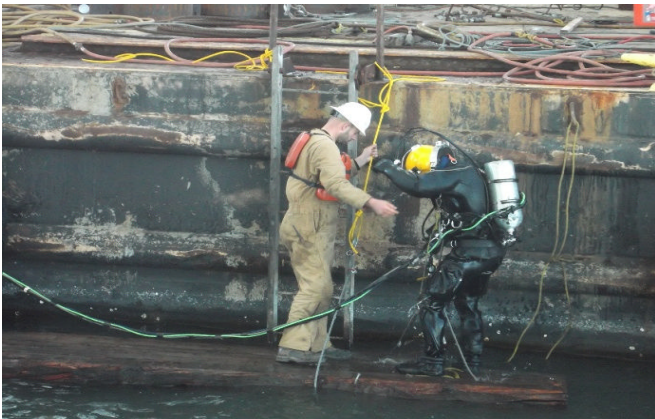

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 480

Date: 04-Dec-2013

Wednesday

