

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 3:55 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 483 Const Calendar Day: 553 Date: 09-Dec-2013 Monday

Inspector Name: Soheilifard, Saman Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 05:00 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 30-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 50 - 60 4PM**Precipitation** none**Condition** RainWorking Day ☒ If no, explain:**Diary:**

Dispute

Work description.

Mon, December 9, 2013

The CCC workers have opened a new front in the East Shaft today addressing the rust and areas of damaged or no paint. In our walk through of the East & South shafts with Mr. Ross Stuart, we came across the following items of interest:

- Working to land my next assignment;
- Loose clip on the grating at Elev. 53.0m;
- Missing Bolt on Skin "A" of the East shaft at El. 77.0m;
- @ El. 56.0m, Skin "C" of the East shaft, Bleyco need to address the abandoned & open drilled & tapped holes;
- CCC has assigned two painters in the South shaft to Power tool (SP@ &3) at Splice #1;
- CCC continued with leaving two painters in the East shaft who began their work of power tooling of the rusted steel at El. 74.0m through 71.0m;

I split my time between the paint & Fender operations, albeit not equally, and as such for more details on the paint operation or the summary of Dutra's work before I got to the Tower base, please refer to Ross Stuart and Sami Daouk's reports, respectively.

I was at the base of the Tower at about 13:30 relieving Sami who in my place was watching over Dutra's work up to this point. The following is the summary of events until the close of the business:

- I was told that Allan Karpieski got injured on Friday after he tripped over some stubs on the barge. The word was that he had not bothered to tell anyone but Gilbert about his injury/departure before leaving the site.
- At the close of the day, pile #11 is the only pile that remains without a collar and the associated bracing to the adjacent pile;
- The construction of built-up sections, welding of stiffeners to the false work beams, cutting angles, and in summary all work pertaining to the false work continues on Kelso and EM1106;
- I heard that Derek, a Ballard diver had to quickly surface from a depth of 70' due to the pinched hose line. He used his spare breathing device to ascend and no complications were reported;
- I spoke to Sam Patel about the abandoned holes left behind by Bleyco and he indicated that he will address that directly with them and that the items are now on the punch list;

04-0120F4 Bid Item: 041 0-000-000.041 ERECT PRECAST CONCRETE FENDER MODULES**DUTRA MATERIALS****Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
-------	-------	------	--------	--------	--------	-------	---------	---------

Contractor: DUTRA MATERIALS



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Soheilifard, Saman **Diary #:** 483 **Date:** 09-Dec-2013 **Monday**

Piledriver	JNM	Jason Baragan	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Supervisor		Dave Lumsden	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	JNM	LUKE HUDSON	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	JNM	WALTER QUINTERO	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	JNM	JEFF SAINZ	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	JNM	JON - PAUL CHENEY	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	APP	ROBERT UTLEY	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Piledriver	APP	JAMES SAVAGE	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	OTH	DAVE AVILAS	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	OTH	STEVE FRIYER	8.00	2.00	0.00	10.00	<input type="checkbox"/>

04-0120F4 Bid Item: 041 0-000-000.041 ERECT PRECAST CONCRETE FENDER MODULES

BALLAD DIVING

Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: BALLAD DIVING								
Marine Coordinator		DERDK CHASE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Marine Coordinator		TODD HORNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Underwater Diver		ALEX DOSS	8.00	2.00	0.00	10.00		<input type="checkbox"/>

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE

CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L02-ENE.078 Tower Lift 02 External Paint Tower NE

CERTIFIED COATINGS COMPANY

Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: CERTIFIED COATINGS COMPANY								
Painter	JNM	Hector pana	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Painter	JNM	ERNESTO SOLON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Painter	APP	RAFAEL SERANO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Painter	JNM	LUIS PANIAGUA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 483

Date: 09-Dec-2013

Monday



RustyElevator Connections (4)



RustyElevator Connections (3)



Abandoned Holes Left By Bleyco(1)



Various Fender Falsework tasks (1)



RustyElevator Connections (2)



EL.77.0m Paint Repair

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 483

Date: 09-Dec-2013

Monday



Various Fender Falsework tasks (2)



EL77.0m-Grinding



Various Fender Falsework tasks (4)



Abandoned Holes Left By Bleyco(2)



Various Fender Falsework tasks (6)



Various Fender Falsework tasks (5)

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Soheilifard, Saman

Diary #: 483

Date: 09-Dec-2013


Monday



Poor Lighting



Rusty Elevator Connections (1)

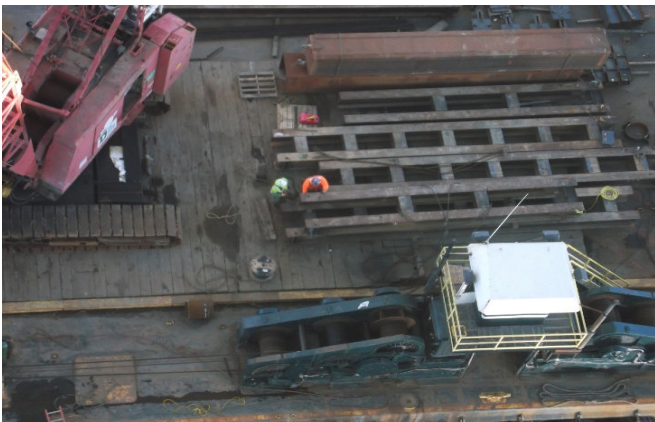

Various Fender Falsework tasks (3)
