

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:53 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 222 Const Calendar Day: 583 Date: 08-Jan-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 04:30 PM 02:30 AM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 18-Jan-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather**

Temperature	7 AM	12 PM	4 PM	50 - 60
Precipitation			Condition	Partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

**Tower Activities**

01-08-14, Wednesday, Night Shift: 4:30 PM – 2:30 AM, Partly Cloudy, 55/42 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

\* Arrived at Burma SAS office around 04:30 PM. Prepared paper work (including Spread Sheet from Laraine) & called Ed (METS) to find the field status. .

\* Obtained field status from QA (Ed & James) at field office & discussed the new spread sheet input data. QC Jesse Cayabyab is not in, new welder Reggie Humphrey started today.

\* Welder, Mike Jimenez (Forman), continued welding at location J / Face B through the whole shift..

\* At location N1/ Face A, welding (FCAW) was performed by Chris (in Process)..

\* New welder Reggie Humphrey performed excavation at location R / Face B @ Y = 710-810, Y = 1070 - 1770, & Y = 1860 - 2090 locations.

\* Jose performed excavation at location S / Face B @ Y = 915 - 1140 & Y = 1440 - 1920 through the whole shift.

\* Brendon worked on grinding at location P & T / Face A.

\* Jose worked grinding at location V / Face A & B.

\* Welder Ma performed grinding at location T / Face A.

\* There was no MT & UT test performed in today's shift.

\* QC Bonifacio worked 10 hours in this shift.

\* Shift ended at 02:30 AM.

**04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								




ddrRptbyBidItem

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Liu, Tai-Lin    **Diary #:** 222    **Date:** 08-Jan-2014    **Wednesday**

Welder	APP	Reggie Humphry	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Equipment			Rental Company				
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
2292	WELDER, 600 AMP					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>
2293	WELDER, 600 AMP					No	
		8.00	2.00	0.00	0.00		<input type="checkbox"/>

### Attachment

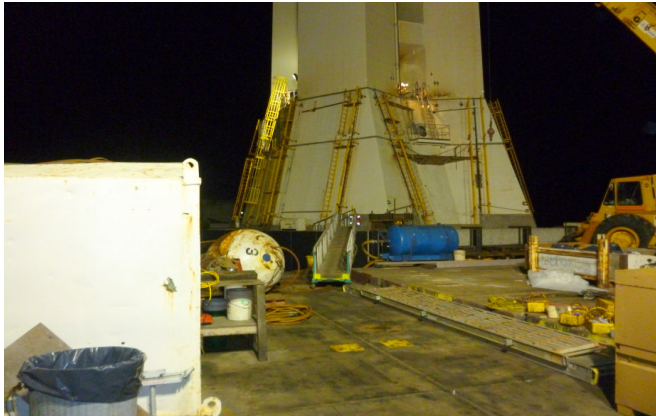

Tower Base at night



Welder Mike performed welding at location J / Face B with QA Ed
