

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:44 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 229 Const Calendar Day: 592 Date: 17-Jan-2014 Friday
Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 04:30 PM 02:30 AM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature	7 AM	12 PM	4PM	60 - 70
Precipitation			Condition	Mostly Clear

Working Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

01-17-14, Friday, Night Shift: 4:30 PM – 2:30 AM, Mostly Clear, 63/46 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

* Arrived at Burma SAS office around 04:30 PM. Saw Alex, Robert, Martin & Bob at office. Prepared paper work and went to field.

* At field, saw ABF safety officer Greg and boat operator Justin. At the field office, talked to QA-Ed Leach & James (METS) to find out the field status.

* QC (SE), Salvador Merino and Patrick Swain were on duty tonight.

* Welder Mike Jimenez (Forman) went back (from Brendon) & performed welding work on location J / Face B through the whole shift.

* Welder Chris Bowles continued last night welding work on W / Face A area through the whole shift.

* Brendon Chapman does not work this shift.

* Jose Torres performed excavating on N/Face A & B and grinding paint in weld P/Face B tonight. He also performed grinding on s / face B area tonight.

* Reggie Humphrey completed welding work on D/ Face A area (D7), and moved to F / Face B start welding. Excavating at weld F at Y = 2920 – 3300 has been VT / MT by QA / QC.

* Welder Man Chun Ma completed grinding on P2 / Face A area, and UT was performed at day shift. Welds P1/P2 Face B should be UT in this shift, but QC delayed this operation to next shift. QA (Ed) performed UT on P / Face A area & watched by QC Salvador. Ma also performed grinding on weld D / Face A & weld R / Face B through the whole shift.

QA James Doecame in at 12:00 PM & left field at 10:30 PM today.

* See QA's reports (Ed Leach and James Doe) for welder's detailed activities.

* QC Salvador Merino and Patrick Swain worked full 10 hours tonight.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
-----------	---------------	---------------	---



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 229

Date: 17-Jan-2014

Friday

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Safety Coordinator	OTH	GREG ANDERSON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No		<input type="checkbox"/>

Attachment



Chris performed welding on W / Face A area



Excavating on N / Face B area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 229

Date: 17-Jan-2014

Friday




Jose performed welding on S / Face B area



QA (Ed) performed UT on weld P / Face A area



Welding on S area

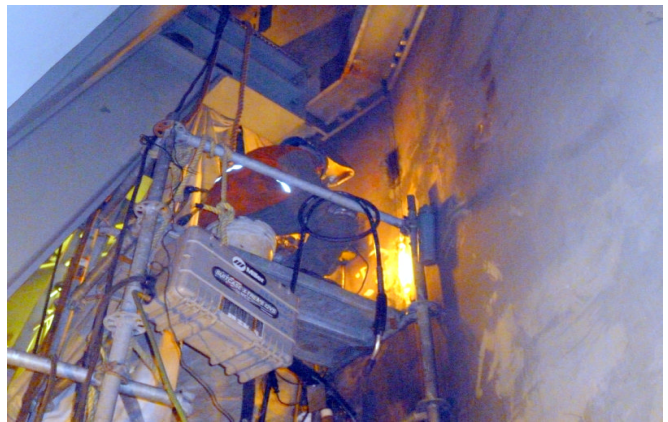

Ma performed grinding on R / Face B location
