

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:37 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 233 Const Calendar Day: 597 Date: 22-Jan-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 04:30 PM 02:30 AM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather**

Temperature	7 AM	12 PM	4 PM	60 - 70
Precipitation			Condition	Mostly Sunny

Working Day ☒ If no, explain:**Diary:**

Dispute

**Tower Activitie**

01-22-14, Wednesday, Night Shift: 4:30 PM – 2:30 AM, Mostly Sunny, 65/45 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

\* Arrived at Burma SAS office around 04:30 PM. Saw Bob & Mohammad at office, talked to Mohammad about work schedule & shift arrangement. Prepared paper work and went to field.

\* At field, saw ABF safety officer Greg and boat operator Justin. At the field office, talked to QA-Ed Leach & James (METS) to find out the field status.

\* QC (SE), Salvador Merino and Patrick Swain were on duty tonight.

\* Welder Mike Jimenez (Forman) performed Forman works tonight.

\* Welder Chris Bowles completed welding on N8 / Face B (Y = 4030 -40610) area, and performed welding work on K / Face B area through the whole night.

\* Brendon Chapman was not here today.

\* Jose Torres performed excavation on location H14 / Face B area tonight.

\* Reggie Humphrey completed welds D1 / Face B (Y = 595 – 815), D2 / Face B (Y = 1025 -1145) and N8 area. He also performed welding on location F and H tonight.

\* Welder Man Chun Ma performed grinding on location J / Face B area through the whole shift.

\* QA (Ed) performed UT on weld S / Face A, this weld has been rejected by QC (Patrick) – Ed agreed the results. Ed tried to perform UT on S / Face B area, but the paint need to be ground in order to perform UT, so it will be tomorrow. Ed went to QC office to sign off the UT report on weld S / Face A location.

\* QA (James) left office around 12:15 AM to cover another work at pike path area.

\* See QA's reports (Ed Leach and James Doe) for welder's detailed activities.

\* QC Salvador Merino and Patrick Swain worked 10 hours tonight.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
-----------	---------------	---------------	--



ddrRptbyBidItem

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4

**Inspector Name:** Liu, Tai-Lin

**Diary #:** 233

**Date:** 22-Jan-2014

**Wednesday**

### AMERICAN BRIDGE/FLUOR, A JV

#### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Safety Coordinator	OTH	GREG ANDERSON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>

#### Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2292	WELDER, 600 AMP						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2293	WELDER, 600 AMP						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>

#### Attachment



Welding on weld C / Face B



Welding on S / Face A

## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 233

Date: 22-Jan-2014

Wednesday

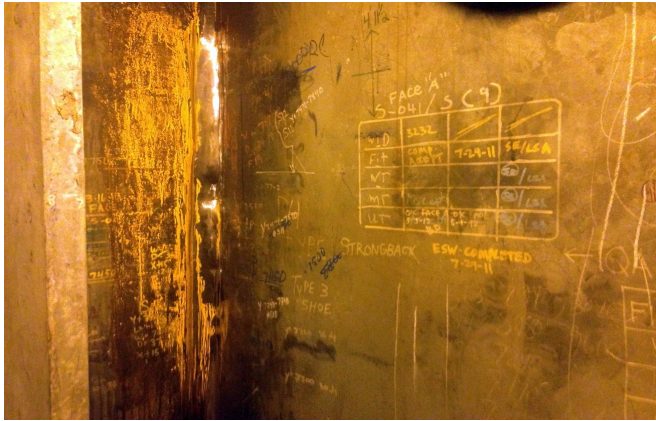

Welding on weld S4-S9 / Face A area



QA (Ed) performed UT on weld S / Face A location
