

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:30 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 236 Const Calendar Day: 600 Date: 25-Jan-2014 Saturday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 02:30 PM 10:30 PM Break: 00:30 Over Time: 08:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 06-Mar-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature	7 AM	12 PM	4 PM	60 - 70
Precipitation			Condition	Partly Cloudy

Working Day ☒ If no, explain:**Diary:**

Dispute

Tower Activities

01-25-14, Saturday, Night Shift: 2:30 PM – 10:30 PM, Partly Cloudy, 66/44 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transversal Indications.

* Arrived at Burma SAS office around 02:30 PM. Saw Bob at office. Prepared paper work and went to field.

* At field, saw ABF safety officer Greg and boat operator Justin. At the field office, talked to QA-Ed Leach & James (METS) to find out the field status.

* QC (SE), Salvador Merino and Patrick Swain were on duty tonight.

* Welder Mike Jimenez (Forman) performed Forman's duty and grinding to remove paint on R / Face A (for future MT testing) through the whole night.

* Welder Chris Bowles continued welding work on A3 / Face A area through the whole night.

* Brendon Chapman completed welding on F / Face A, and moved to K13 for welding through the whole shift.

* Jose Torres was not here tonight.

* Reggie Humphrey was not here tonight. .

* Welder Man Chun Ma performed grinding / excavating on location P / Face A area through the whole shift.

* No UT & MT performed in this shift.

* See QA's reports (Ed Leach and James Doe) for welder's detailed activities.

* QC Salvador Merino and Patrick Swain worked 8 hours tonight.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
-------	-------	------	--------	--------	--------	-------	---------	---------



ddrRptbyBidItem

Page 1 of 3

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 236 **Date:** 25-Jan-2014 **Saturday**

Contractor: AMERICAN BRIDGE/FLUOR, A JV							
Safety Coordinator	OTH	GREG ANDERSON	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	8.00	0.00	8.00	<input type="checkbox"/>
Equipment							
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT						
			0.00	8.00	0.00	0.00	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						
			0.00	8.00	0.00	0.00	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						
			0.00	8.00	0.00	0.00	<input type="checkbox"/>
2292	WELDER, 600 AMP						
			0.00	8.00	0.00	0.00	<input type="checkbox"/>
2293	WELDER, 600 AMP						
			0.00	8.00	0.00	0.00	<input type="checkbox"/>

Attachment



QA (Ed) checking welding on F / Face A area with Brendon



Welding on H14 area



Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name: Liu, Tai-Lin

Diary #: 236

Date: 25-Jan-2014

Saturday

Brendon performed welding on F / Face A area

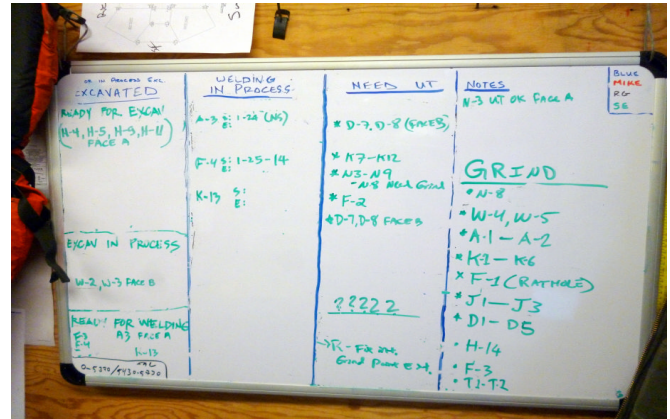

Today's work progress list
