

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:18 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 242 Const Calendar Day: 609 Date: 03-Feb-2014 Monday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60**Precipitation** **Condition** CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activities

02-03-14, Monday, Day Shift: 07:00 AM – 05:30 PM, Mostly Cloudy, 60/54 F

Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications.

* Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,

* Talked to QA - Joe Adame (METS) to find out the field status.

* QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today. JR worked on E2 instead of Tower Base today, QA Simiom have different shift time schedule - from 12:00 PM to 10:30 PM today. Saw ABF QC - Chris Chew today.

* Welder Richard Garcia (Forman) performed Forman's duty and setting up skirt operation. He also performed welding on L / Face A, Y = 500 - 700 area today .

* Welder Kyle Clowley was not here today.

* Welder Donald Plumb performed welding on F / Face A , Y = 4800 - 5800 area,

* Zachariah Macdonald performed grinding on A / Face B, Y = 1000 - 2000 area.

* Paul Fambrini performed misc. works (such as maintenance preheat pad installation or removing) as usual.

* Guowu Chen performed excavating / grinding on L / Face A at Y = 1500 - 1700 area. and G / Face A location as well.

* New guy Carlos Alvarado started after 3:30 PM. He performed grinding on H14 / Face B area.

* Welder Randy Clayborn was not in tower base today.

* Welder Ernest Connors was not here today.

* See QA's reports (Joe Adame) for welder's detailed activities.

* QC Bonifacio Daquinag (JR) worked 2 hours, and Bernie Docena worked 10 hours in ESW repair work today.



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 242

Date: 03-Feb-2014

Monday

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV


Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
2292	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	2.00	0.00	0.00	No	<input type="checkbox"/>

Attachment

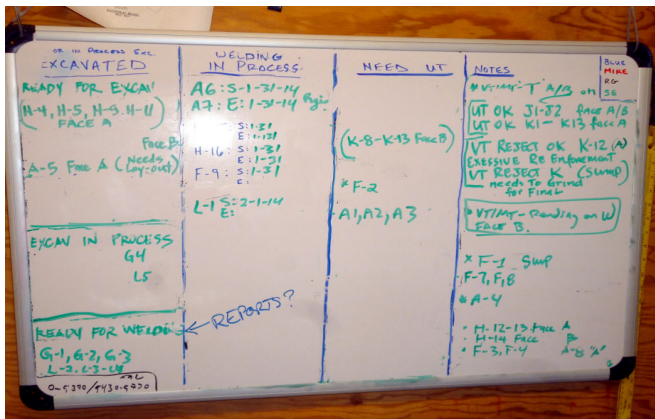

Work progress on the board



Chen performed grinding on G / Face A area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 242

Date: 03-Feb-2014

Monday



Donald performed welding on F / Face A area



Carlos will be grinding on H14 / Face B area
