

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 2:01 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 251 Const Calendar Day: 619 Date: 13-Feb-2014 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60**Precipitation** **Condition** CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activitie

02-13-14, Thursday Shift: 07:00 AM – 05:30 PM, Cloudy, 61/56 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

* Arrived at Burma SAS office around 07:00 AM. Attended safety meeting . Prepared paper work & went to field,

* Talked to QA - Simion Ramirez (METS) to find out the field status. QA - Joe Adam and QC - Bernie were not here today. Simion told me that Joe will be back next Tuesday.

* QC (SE), Bonifacio Daquinag (JR) was on duty today.

* Welder Kyle Clowley was helping Randy in welding on Skirt area.

* Welder Donald Plumb performed welding on M / Face B area and assisted by Zack & Paul.

* Zachariah Macdonald performed grinding / excavating on H / Face A area & helping Plumb on M / Face B area as well..

* Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing).

* Guowu Chen performed grinding on M / Face A & L / Face A area.

* Welder Randy Clayborn performed welding on Skirt area.

* Eric performed weld repair on F / Face A area.

* Welder Ernest Connors performed welding on L / Face A area and H / Face A area,

* QC (JR) performed MT on L9 / H4 / H5 today. No UT performed on this shift.

* See QA's reports (Simion Ramirez) for welder's detailed activities.

* QC Bonifacio Daquinag (JR) worked 10 hours, and Bernie Docena was not here today.

(2). CCO 366 - ESW Test Sample ***



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 251

Date: 13-Feb-2014 Thursday

* Julient Poulk continued drilling the bolt holts today and Arron Kent was helping him to perform the work. Doubler plate holes drilling was completed around 85% (See Pictures), will continue on tomorrow.

* Julient worked 10 hours on this CCO today. Arron worked around 8 hours on CCO today.

(3). Tower Fender System Cast-in-place concrete work

* See picture, total 8 people worked today, they left around 3:00PM today. Did not see CONCO crew here today, Per Dutra personnel & Mohammad, no work for Dutra & Conco on weekend & Presents Day.

* Crew worked on form works - temp. form installation, lost deck form work ,etc. (see pictures)

* Crew: Steve Friyer, Sami Tavake, Ron Torres, Robert Utley, Ben Unutoa, Luke Hudson, James Savage & Dan Wheeler (8) - worked 8 hours today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	6.00	2.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JULIENT POULK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JONATHON BISKNER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ETHAN KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2292	WELDER, 600 AMP						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2293	WELDER, 600 AMP						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 251

Date: 13-Feb-2014 Thursday

Attachment



Bolt hole drilling on V / Face B area by Julient



Pro-heat pad installed on H / Face B area




Bolt hole drilling on test sample area - V / Face B area



One of External Clourse Concrete pour



External Clouse Concrete pour performed on yesterday

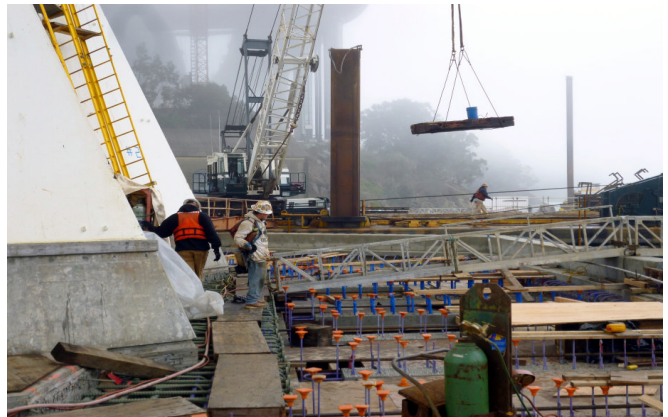

Dutra crew performed form works with crane operator

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 251

Date: 13-Feb-2014

Thursday



Dutra crew left from site around 3:00 PM



Julient performed drilling doubler plate bolt holes



Diver performed form work - Dutra



Dutra crew performed form work on fender system



Pro - Heat pad installed on M / Face A area



Form work on lost deck area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 251

Date: 13-Feb-2014

Thursday



Chen performed grinding on L / Face A area



Dutra perform wooden form works on lost deck area
