

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:56 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 252 Const Calendar Day: 620 Date: 14-Feb-2014 Friday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time: 00:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 50 - 60 4PM 50 - 60**Precipitation** **Condition** CloudyWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activities

02-14-14, Friday, Day Shift: 07:00 AM – 03:30 PM, Cloudy, 61/56 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

* Arrived at Burma SAS office around 07:00 AM. Prepared paper work & went to field,

* Talked to QA - Simion Ramirez (METS) to find out the field status. QA - Joe Adam and QC - Bernie were not here today (same as yesterday).

* QC (SE), Bonifacio Daquinag (JR) was on duty today.

* Welder Kyle Clowley was helping Randy in welding on Skirt area.

* Welder Donald Plumb performed excavating / welding on F / Face B area and assisted by Zack.

* Zachariah Macdonald performed grinding / excavating on F / Face B area helping Plumb (see pic.).

* Paul Fambrini performed misc. works (such as maintance proheat pad installation or removing - see pic.).

* Guowu Chen performed grinding / excavating on L / Face A area.

* Welder Randy Clayborn performed welding on Skirt area.

* Eric performed welding / repair on F / Face A area.

* Welder Ernest Connors performed excavating / welding on H / Face A area,

* QC (JR) performed MT on G / Face A area. No UT performed on this shift.

* See QA's reports (Simion Ramirez) for welder's detailed activities.

* Crew worked 8 hours today and no work on weekend & next Monday (Presents Day) as well.

* QC Bonifacio Daquinag (JR) worked 8 hours, and Bernie Docena was not here today.



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 252

Date: 14-Feb-2014 **Friday**

(2). CCO 366 - ESW Test Sample ***

* Bolt holts drilling was done late yesterday.

Aaron & Zach performed cleaning area today, worked 4 hours respectively.

(3). Tower Fender System Cast-in-place concrete work

* Talked to Dutra Engineer John, he told me that Conco will come in on 2/24/14, one week from now and Dutra will do the stay form clean work by themselves (may be next week).

* Dutra crew continued working on form works - temp. form installation, lost deck form work ,etc. (see pictures)

* Crew: Steve Friyer, Sami Tavake, Ron Torres, Robert Utley, Ben Unutoa, Luke Hudson, James Savage & Dan Wheeler (8) - worked 8 hours today.

*** Came back office around 3:40 PM. Finished diary & filled time sheet and car log left office around 4:30 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	CARLOS ALVARADO MATOS	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	JULIENT POULK	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JONATHON BISKNER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	ETHAN KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT	8.00	0.00	0.00	0.00	No		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	8.00	0.00	0.00	0.00	No		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	8.00	0.00	0.00	0.00	No		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Liu, Tai-Lin Diary #: 252 Date: 14-Feb-2014 Friday

2292	WELDER, 600 AMP	8.00	0.00	0.00	0.00	No	<input type="checkbox"/>
2293	WELDER, 600 AMP	8.00	0.00	0.00	0.00	No	<input type="checkbox"/>

Attachment



QC (JR) performed MT on L / Face A area




Chen performed grinding on L / Face A area



Doubler bolt hole drilling on V / Face A area



Dutra diver performed form work on fender system

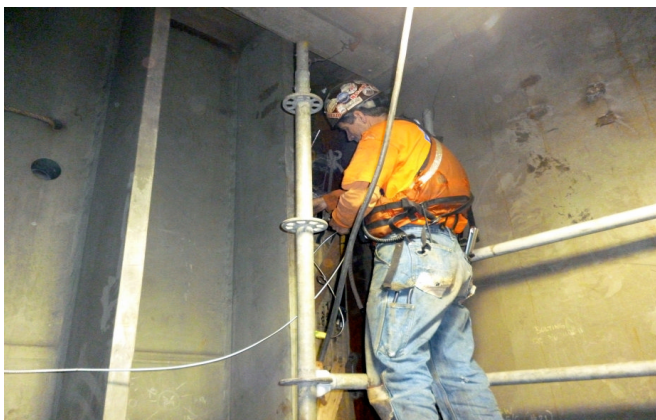

Paul installed pro-heat pad on L / Face B area



Pro-heat pad installed on L / Face B area

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 252 **Date:** 14-Feb-2014 **Friday**

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 252

Date: 14-Feb-2014

Friday



Zach performed grinding on G / Face B area



Dutra crew performed form work on fender system



New & old SFOBB



Donald performed welding on M / Face B area
