

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:31 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 259 Const Calendar Day: 632 Date: 26-Feb-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 31-May-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 50 - 60 12 PM 60 - 70 4PM 60 - 70**Precipitation** **Condition** ShowersWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activities

02-26-14, Wednesday, Day Shift: 07:00 AM – 05:30 PM, Showers, 62/58 F

(1). Electro Slag Weld (ESW) - Weld Repair on Tower Base Transverse Indications

* Arrived at Burma SAS office around 07:00 AM. Prepared paper work (CCO#366) & went to field,

* Welding was 100% completed, NDT was 85% completed per 2/26/14 ESW meeting status update.

* Talked to QA - Simion Ramirez (METS) and Joe Adame to find out field status. Saw Sami at field office. There were all grinding work today. There was no night shift work, 5 welders came back to day shift (Mike, Jose, Ma. Regie & Eric)

* QC (SE), Bonifacio Daquinag (JR) and Bernie Docena were on duty today.

* Welder Donald Plumb performed grinding the welds on F / Face A area today.

* Zachariah Macdonald performed grinding on G / Face A area today.

* Paul Fambrini was here today. .

* Guowu Chen performed grinding on F / Face B area today.

* Welder Ernest Connors continued welding / excavating on V / Face B area, later on Ma was helping him to grind the same area,

* QA Joe performed MT on H / Face A area. QC Bernie performed UT on G / Face A area.

* See QA's reports (Simion Ramirez & Joe Adame) for welder's detailed activities.

* QC Bonifacio Daquinag (JR) worked 10 hours today, and Bernie Docena also worked 10 hours today.

(2). CCO 366 - ESW Test Sample ***

* No work on this CCO today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 259

Date: 26-Feb-2014

Wednesday

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	ERNEST CONNER	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			

Attachment



Plumb performed grinding on H / Face B area



Pipe driving in near by area

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 259

Date: 26-Feb-2014

Wednesday

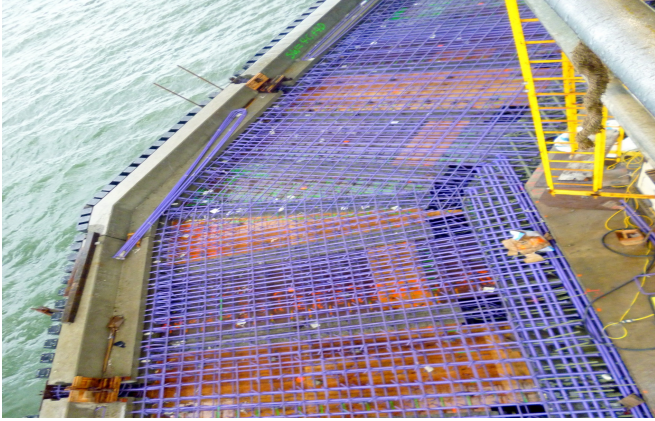

Rebar on east side of fender system



Grinding on V / Face B area by Ma



Wet floor on bottom of Tower Base due to rain



Two more skirt area left (E/W entrance) on Tower Base area



Grinding on F / Face A area



Chen performed grinding on F / Face B area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 259

Date: 26-Feb-2014

Wednesday



Ma performed grinding on V / Face B area



QC (Bernie) performed UT on G / Face A area
