

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:48 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 279 Const Calendar Day: 687 Date: 22-Apr-2014 Tuesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 07-Jun-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather**

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation

Condition Clear and strong Wind

Working Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

04-22-14, Tuesday, Clear / Strong Wind at Tower

- * Performed Paper work this morning
- * At 1:05 PM, went to job site (bottom of W2) with Mohammad to meet METS personnel - Arron and Stuart Ross.
- * Talked to Stuart regarding Tower Cleaning work performed by ABF.
- * Stuart provided the crew's name as the follows:

Dale Harris, John La Rosa, Joseph Ruiz and Danny Schwartz - Four Labors.

Work Schedule: 7:00 AM - 3:30 PM

Work Location: Elevation 123 to 139 m

- * We all went to Tower through elevator. Saw ABF's Engineer (Levi Gatsis) & Forman @ Elev. 53.
- * Mohammad, METS' ponsonnel & ABF's Engineer went to Top of the Tower to check the cleaning work performed by ABF last week. Per Mohammad, the area is still need further clean in order to sign off.
- * I left Tower area earlier and back to office around 3:00 PM. Checked e-mail and did some paper work & left office around 3:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	CHRISTOPHER BOWLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MAN CHUN MA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	BRENDON CHAPMAN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Welder	APP	Reggie Humphry	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Operator	JNM	JUSTIN GARRETT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Safety Coordinator	OTH	GREG ANDERSON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JOHN ROSAS	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	GUOWU CHEN	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	RANDY CLAYBORN	0.00	0.00	0.00	0.00		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 279 **Date:** 22-Apr-2014 **Tuesday**

Ironworker	JNM	ERNEST CONNER	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	KYLE CROWLEY	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	STANLEY DALIE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	Tony Miranda	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSEPH RUIZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	RICHARD GARCIA	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment						Rental Company	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

Attachment




Old bridge demolition - view from Tower



Up-view tower from Elev. 68



View west (W2) from tower

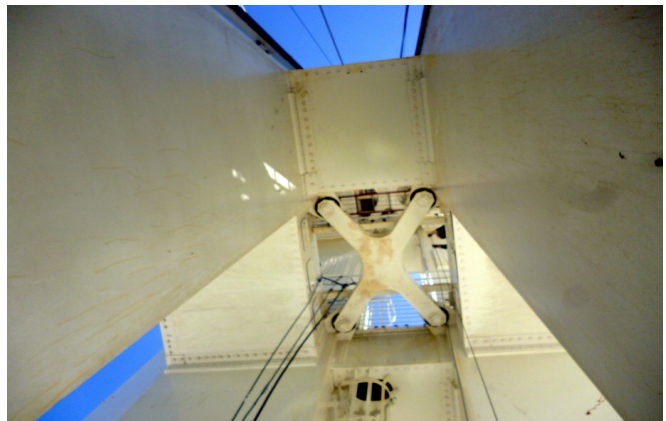

Another view from Elev. 68 up to Tower top
