

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:02 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 324 Const Calendar Day: 770 Date: 14-Jul-2014 Monday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

**Tower Activites**

Tower Base Works (7/14/14, Monday - Clear day):

\* CCC painting works:

- Attended staff meeting this morning.

- No METS paint inspector in the field yet. CCC Tony was in pier 7 for paint testing, not in the field today.

- CCC two painters continued painting in elevation 18 tower façade area. They will move to elevation 23 to paint the the façade inside area.

- Two CCC painters performed preparation work at elevation 28 &amp; 33 façade area.

- CCC 6 painters worked 10 hours today.

- CCC painter Billy was painting the elevator door today at the fender concrete area.

Paint Crew: Billy Gatewood, Joege Fones, Javier Alvag, Recardo Pasalla, Manuel &amp; Eric - 10 hours.

\* Saw ABF cleaning crew at tower base area (above 53 meter exterior of shaft, See pictures) - Refer to Laraine's diary for detail.

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

\* Saw IRWs Paul &amp; Donald Plumb at job site.

\* Saw 3 electrician worked on elevator area.

\* Crane operator Neil Caldwell &amp; helper Justin at barge stand by for any lifting work needed.

\* Performed paper work including RFI/Submittal PMIV works at the office. Left office around 03:40 P

**04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
-------	-------	------	--------	--------	--------	-------	---------	---------



ddrRptbyBidItem

Page 1 of 4

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Liu, Tai-Lin    **Diary #:** 324    **Date:** 14-Jul-2014    **Monday**

<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
Ironworker	JNM	DONALD PLUMB	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

<b>Equipment</b>						<b>Rental Company</b>	
<b>Equipment ID</b>	<b>Description</b>	<b>RT Hrs</b>	<b>OT Hrs</b>	<b>ST Hrs</b>	<b>IT Hrs</b>	<b>Remarks</b>	<b>Dispute</b>
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>
2292	WELDER, 600 AMP					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>
2293	WELDER, 600 AMP					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>

<b>04-0120F4</b>	<b>Bid Item:</b> 078	<b>T-L01-ENE.078</b>	<b>Tower Lift 01 External Paint Tower NE</b>
CERTIFIED COATINGS COMPANY			

<b>04-0120F4</b>	<b>Bid Item:</b> 078	<b>T-L05-ENE.078</b>	<b>Tower Lift 05 External Paint Tower NE</b>
CERTIFIED COATINGS COMPANY			

<b>04-0120F4</b>	<b>Bid Item:</b> 078	<b>T-HEA-ENE.078</b>	<b>Tower Head External Paint Tower NE</b>
CERTIFIED COATINGS COMPANY			

<b>CCO-355</b>	<b>Bid Item:</b> 001	<b>0-CIC-EFA.355</b>	<b>CIC - Elevator Impacts - USA Hoist</b>
AMERICAN BRIDGE/FLUOR, A JV			

**Attachment**



ddrRptbyBidItem

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 324

Date: 14-Jul-2014

Monday



Three electricians worked on electric line on tower elevator



Electrician worked on electric line at el. 13 area




CCC painter Joge performed painting on inside façade area elevation 18



Painting inside the façade area



ABF labors performed cleaning exterior of tower on east side area near 53 meter area

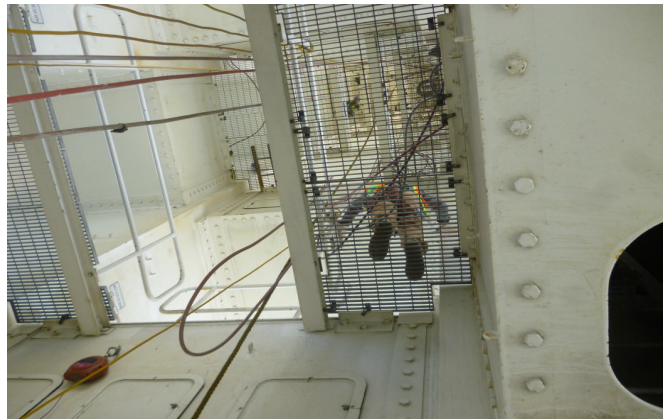

CCC painters (2) performed prep. Works on Elev. 28 & 33 area



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 324

Date: 14-Jul-2014

Monday



CCC transported tool to el. 28 façade area



CCC Billy performed painting on elevator door at fender concrete area
