

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 11:58 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 325 Const Calendar Day: 771 Date: 15-Jul-2014 Tuesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

Tower Base Works (7/15/14, Tuesday - Clear):

* CCC painting works:

- Still No METS paint inspector in the field yet. CCC Tony also not in the field when I was there.

- CCC completed painting in elevation 18 tower façade area. All 7 painters worked on prep work at El. 28 & 33 meter façade area.

- Forman Recado told me that they worked 8 hours yesterday and today as well.

- Went inside tower base area with Grady, no painter working in that area (see pictures)

Paint Crew: Billy Gatewood, Joege Flones, Javier Alvag, Recardo Pasalla, Manuel Ramirer, Marco Oruno & Eric Garza.

* Saw ABF cleaning crew at tower around 33 meter exterior of shaft (See pictures) - Refer to Laraine's diary for detail.

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

* Saw IRWs Paul & Donald Plumb at job site.

* Saw 3 electrician worked on elevator area.

* Crane operator Neil Caldwell & helper Justin at barge stand by for any lifting work needed.

* Took safety office Grady Hart to tower inside skirt & inside base area (see pictures)

* Performed paper work including RFI/Submittal PMIV works at the office. Left office around 03:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
-------	-------	------	--------	--------	--------	-------	---------	---------

Contractor: AMERICAN BRIDGE/FLUOR, A JV



ddrRptbyBidItem

Page 1 of 4

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 325 **Date:** 15-Jul-2014 **Tuesday**

Ironworker	JNM	DONALD PLUMB	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment

Rental Company

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
AMERICAN BRIDGE/FLUOR, A JV

Attachment



ddrRptbyBidItem

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 325

Date: 15-Jul-2014

Tuesday




Tower skirt area view



Tower base area water pump outlet pipe



Tower base in north shagt area

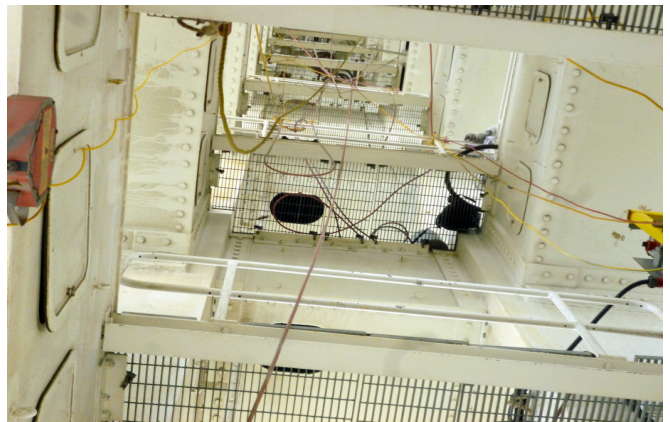

CCC performed prep work at El.33 façade area



Dehumidifier at inside tower cell # 6 area



ABF's labres performed tower exterior cleaning at el. 33 meter area west side

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 325

Date: 15-Jul-2014

Tuesday



Safety office Grady was checking area inside the tower base area
