

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 11:54 AM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 327 Const Calendar Day: 773 Date: 17-Jul-2014 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

**04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

**Tower Activites**

Tower Base Works (7/17/14, Thursday - Overcast/Clear):

\* Attended safety meeting this morning. Finalized a CCO letter and actioned 5 RFI to the individual group this morning as well.

\* CCC painting works:

- CCC crew (7) continued performing prep & painting work on tower facad area between elevation 23 meter to 33 meter area.

- Met Forman Recado at pier, he told me that they finished façade painting on El. 23 will continue to higher elevation same as prep work, also mentioned that the painter Edllberto came back for work at field today.

Paint Crew: Billy Gatewood, Joege Flones, Javier Alvag, Recardo Pasalla, Manuel Ramirer, Marco Ornuño, Edllberto Leon & Eric Garza.

\* Saw ABF cleaning crew at tower around 33 meter exterior of shaft (See pictures).

\* ABF labores (7) performed tower shaft exterior cleaning works, at shaft W face b, shaft E face c & d and shaft N face b area at various elevations (see pictures).

\* Saw 3 electricians worked on elevator area.

\* Crane operator Neil Caldwell & helper Justin at barge stand by for any lifting work needed.

\* ABF IRWs James Miranda & Jim Benninghove at tower base area performed ropes arrangement that ties to tower cleaning support card at air (see pictures).

\* Performed paper work including RFI/Submittal PMIV works at the office. Left office around 03:40 PM.

**04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	AMERICAN BRIDGE/FLUOR, A JV							
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Liu, Tai-Lin    **Diary #:** 327    **Date:** 17-Jul-2014    **Thursday**

Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
<b>Equipment</b>			<b>Rental Company</b>				
<b>Equipment ID</b>	<b>Description</b>		<b>RT Hrs</b>	<b>OT Hrs</b>	<b>ST Hrs</b>	<b>IT Hrs</b>	<b>Dispute</b>
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No	
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No	
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
2292	WELDER, 600 AMP					No	
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
2293	WELDER, 600 AMP					No	
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
<b>04-0120F4      Bid Item: 078      T-L01-ENE.078      Tower Lift 01 External Paint Tower NE</b>							
CERTIFIED COATINGS COMPANY							
<b>04-0120F4      Bid Item: 078      T-L05-ENE.078      Tower Lift 05 External Paint Tower NE</b>							
CERTIFIED COATINGS COMPANY							
<b>04-0120F4      Bid Item: 078      T-HEA-ENE.078      Tower Head External Paint Tower NE</b>							
CERTIFIED COATINGS COMPANY							
<b>CCO-355      Bid Item: 001      0-CIC-EFA.355      CIC - Elevator Impacts - USA Hoist</b>							
AMERICAN BRIDGE/FLUOR, A JV							

**Attachment**



ddrRptbyBidItem

## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 327

Date: 17-Jul-2014

Thursday

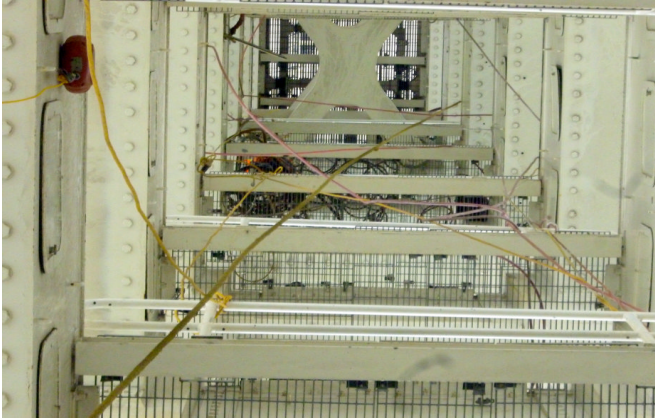

View from center of tower looking from bottom - CCC crew performed façade cleaning & painting works




Another labores performed cleaning at Shaft E face d & c area




ABF IRW's James & Jim performed cleaning car ropes arrangement



ABF IRW's James & Jim performed arrangement for cleaning car supporting ropes

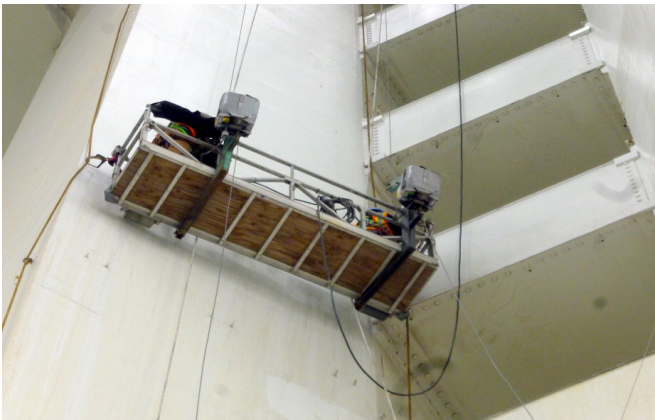

ABF labores performed tower shaft exterior cleaning at shaft W face b El. 28 m

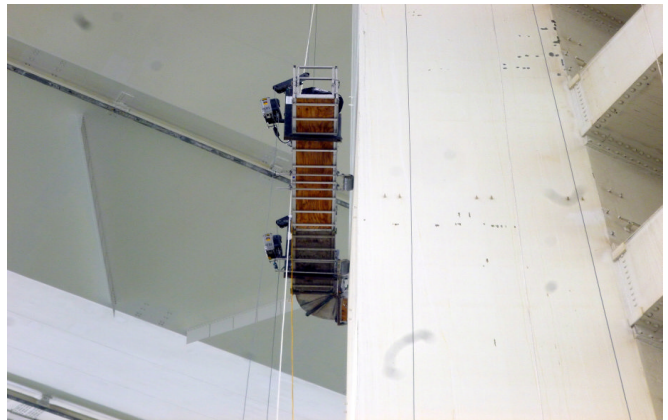

ABF labors performed cleaning at shaft N face b area
