

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:24 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 331 Const Calendar Day: 780 Date: 24-Jul-2014 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (Below 53 m area) (7/24/14, Thursday - Clear):



* Attended safety meeting from 08:00 - 0920 AM.

* Went to T1 with Grady and Robert Wong. Saw METS SMR and paint inspector going to inside tower base to check skirt, façade & shaft cleaning /paint repair works (see picture)

* CCC painting works:

- Saw Tony at field, he told me that two painters Billy & Marco performed touch-up on interior of skirt. Two painters were in façade area continued performing prep & painting work (El. 47.6 meter).

- Two painters: Billy, Marco continued working in tower base cell area for touch-up paint repair work.

Paint Crew: Billy Gatewood, Joege Flores, Recardo Pasalla, Marco Ornuno, E Leon and Tony Katrones.

*** Noted that E Leon and Billy Gatewood worked 8 hours on CCO # 314 works today.

* ABF cleaning work (below 53 m area):

- Did not see ABF labores work on tower shaft exterior cleaning (below 53 m) today.

- CCC crew continued performing paint repair on shaft S face B, shaft N face B and shaft E face C & D today (see pictures).

- ABF's crew: Victor Hernandez, Jose Jr. Avila, Fabian Rodriguez, Aurelio Rodriguez, Juan Gutiores, Guillermo Limon,

- CCC crew: see Larian's diary.

* Other works:

- Saw 1 electrician worked on installing PVC pipe for electric lines around exterior of skirt area.

- Did not see crane operator Neil Caldwell & helper Justin at barge today.



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 331 **Date:** 24-Jul-2014 **Thursday**

- Saw Mahmoud performed inspection on tower elevator installation with 2 workers (US Hoist).

- ABF IRWs Paul & Plumb were in tower as well.

Safety office Grady and Sweep Robert /Melidar were in T1 today.

Performed paper work and RFI/Submittal PMIV process work at office.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
CERTIFIED COATINGS COMPANY



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 331

Date: 24-Jul-2014

Thursday

CCO-355	Bid Item: 001	0-CIC-EFA.355	CIC - Elevator Impacts - USA Hoist
AMERICAN BRIDGE/FLUOR, A JV			

Attachment



CCC crew performed paint repair on shaft S face B area



CCC performed paint repair work on shaft S face B exterior area



CCC crew performed paint repair on shaft E face C & D, façade area El. 33m, and IRW's at opening area



Again, CCC crew performed paint repair work on shaft S face B, no ABF labor on shaft S face C area



Viewed from boat on T1 paint repair work and tower elevator works



Saw two METS personnel at site checking paint work

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 331

Date: 24-Jul-2014

Thursday

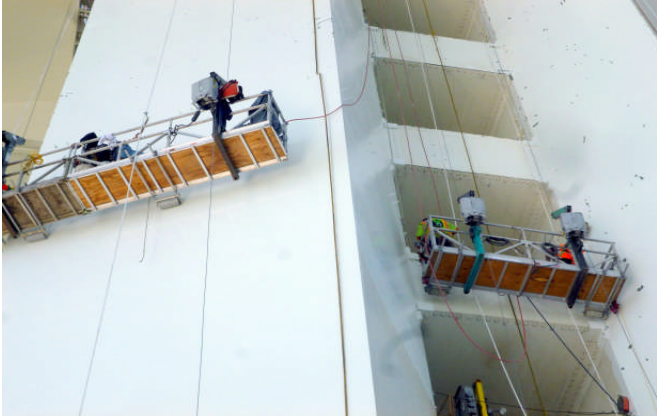

CCC crew performed paint repair work at Shaft E & N



Two US Hoist personnel wrked on elevator work
