

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 11:42 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 344 Const Calendar Day: 800 Date: 13-Aug-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 06:30 AM 04:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (8/13/14, Wednesday - Clear):



- * Performed paper work, and checked e-mail. Went to job site (T1 base by boat) with Grady & Martin.
- * At tower base, saw ABF's labor Jose Jr. Avila at tower base El. 13 meter area performed housekeeping work. He moved the garbage from inside tower base to barge. He told me Victor will joint him this afternoon. Tower elevator crew performed checking the elevator this morning and ran into a little bit problem on the system, Martine planed to take elevator to top of the top by elevator has been canceled. Saw Feather with another guy went into tower base cell to check dehumidifier.
- * No CCC painter worked in the area below El. 53m this morning.
- * After lunch, drove to W2 and walked to Tower entance El.53 with Grady. Saw CCC forman Sage Ray at tower entrance area. Also saw James & Ray (ABF paint inspector, he was on the way back to pier 7 for attending the meeting). From the pictures, there were two L shape swing stages on the N/W shaft C/B faces area at El. 114m, total 6 painters continued performing paint repair in that area. There was a painter performed paint repair at cross bracing at El. 89m, two painters also performed paint repair at El. 71m area as well. Sage (Forman) told me that total 11 painters worked today for 12 hours shift. And no painter worked below El.53 area at the time I was there. Later on, I met another forman Francisco at El.53, he told me he will take another 3 guys (Cory Reese, Mike Woodnancy & Jonny Fagunders) to the area below 53m to perform housekeeping about 1 hour (these five guys worked on OBG area today).
- * Paint Crew: Sage Ray, Armado Avitia, Manuel Ramirez, Cory Reese, Alberto Serrano, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Edilberto Leno (worked 8 hours), Daniel Rosales, Abraham Ventura. Crew worked from 6AM to 6PM, 12 hours shift.

Rafael Ventura, Mike Woodnancy, Johanny Fagundes and, Franciso Serano - Four painters worked one hour at area below El. 53m for cleaning the area - housekeeping work.

- * At 2:30 PM, saw James & Ray at tower entrance El. 53. Four labors worked in tower today, mainly for hourskeeping and moving swing stages for painter.

- * Four labores: Victor Hernandez, Jose Jr. Avila, Aurelio Rodriguez and Danny Schwartz worked 8 hours shift today (6 AM to 2:30PM).

- * Other works:



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 344 **Date:** 13-Aug-2014 **Wednesday**

- Saw crane operator Neil Caldwell & helper Justin on the barge moving garbage container from tower base to barge & on the boat.
- Saw Mahmoud performed inspection on tower elevator installation with 4 workers (US Hoist), Martine was in site as well.

Performed paper work and RFI/Submittal PMIV process work at office, left office around 5:10 PM. OT 2 hours today.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
CERTIFIED COATINGS COMPANY

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 344

Date: 13-Aug-2014 Wednesday

CCO-355	Bid Item: 001	0-CIC-EFA.355	CIC - Elevator Impacts - USA Hoist
AMERICAN BRIDGE/FLUOR, A JV			


Attachment



ABF labor Jose took garbage from inside tower cell to barge



ABF put cover on the drain holes (half of them) on the tower base footing

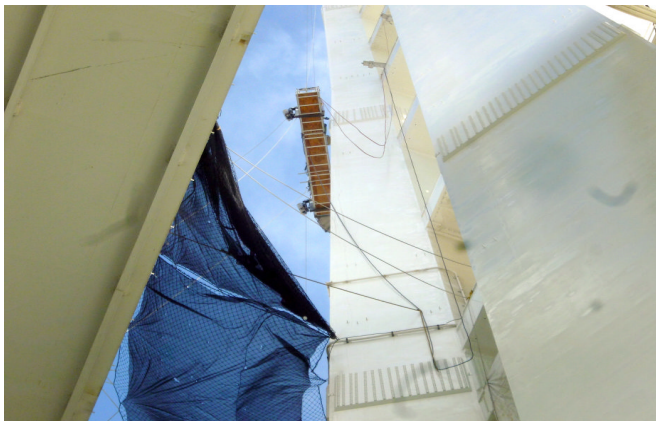

Swing stage on the W shaft C/D faces El. 71m



Saw CCC forman Sage Ray on the tower entrance El. 53m



CCC painter performed paint repair on piping at El. 53m tower entrance area



Painter performed paint repair on cross bracing El. 71m area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 344

Date: 13-Aug-2014 Wednesday



CCC performed paint repair on swing stage at N shaft C/D faces
El.114m area



Two L shape swing stage on N/W shafts D/C faces used for paint
repair usage



Picture for single swing stage used by CCC
