

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:21 AM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 352 Const Calendar Day: 816 Date: 29-Aug-2014 Friday  
Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge**Weather**

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day ☒ If no, explain:**Diary:**

Dispute

**Tower Activities**

CCO # 382 - Tower Painting and Cleaning works (8/29/14, Friday - Clear):

\* Performed paper work, and studied Tower cleaning &amp; paint repair tracking sheets. Went to job site (T1 by driving to W2 with Robert) around 10:00 AM.

- At W2 near elevator, saw ABF's labor forman - James & elevator operator Howard.
- There was no CCC's painter work in tower today due to Labor Day long weekend (Holiday for CCC), did not see METS personnel in field as well. No field work on three day long weekend.
- Total 5 labores at the tower performed house keeping work.
- ABF's labores left tower around 10:45 AM, W2 Elevator also shot down later.

\* Labores: James Sturgeon, Jose Jr. Avila, Victor Hernandez, Rogelio Rodriguez and Danny Schwartz worked today

\* Performed paper work at office.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

**Equipment**

Rental Company

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							



ddrRptbyBidItem

## Daily Diary Report by Bid Item


**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 352    **Date:** 29-Aug-2014    **Friday**

*E0020562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
2292	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
2293	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
<b>04-0120F4      Bid Item: 078      T-L01-ENE.078      Tower Lift 01 External Paint Tower NE</b> CERTIFIED COATINGS COMPANY							
<b>04-0120F4      Bid Item: 078      T-L05-ENE.078      Tower Lift 05 External Paint Tower NE</b> CERTIFIED COATINGS COMPANY							
<b>04-0120F4      Bid Item: 078      T-HEA-ENE.078      Tower Head External Paint Tower NE</b> CERTIFIED COATINGS COMPANY							
<b>CCO-355      Bid Item: 001      0-CIC-EFA.355      CIC - Elevator Impacts - USA Hoist</b> AMERICAN BRIDGE/FLUOR, A JV							

### Attachment



Tower base viewed from W2 area

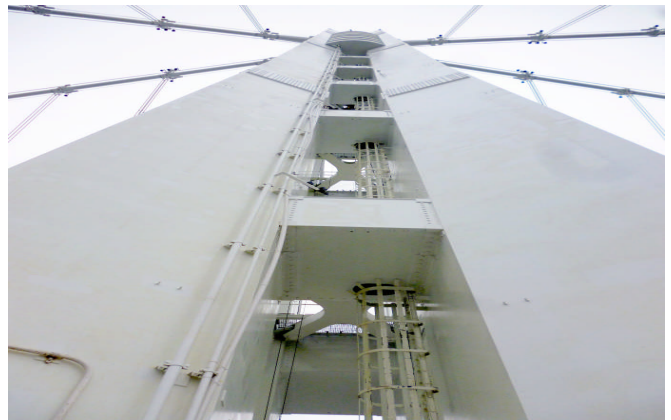

No painter work today


## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 352

Date: 29-Aug-2014 Friday

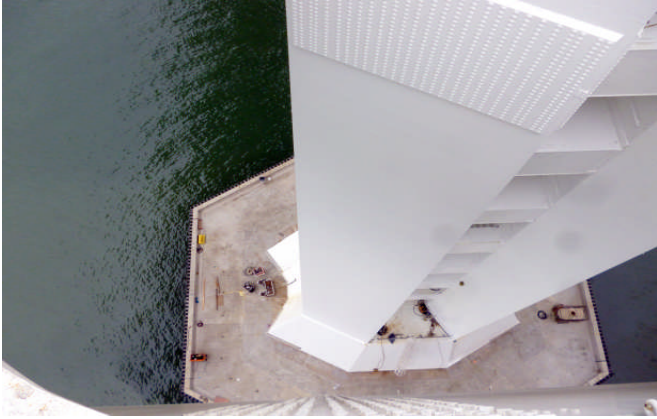

Tower viewed from El. 53 M deck area



ABF's laborers (Fish, Victor & Danny) and Robert were in El. 53 m tower-deck area



Smoke came from old bridge demo job next to the tower area



Piping has been power tooling near the tower area
