

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:19 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 355 Const Calendar Day: 823 Date: 05-Sep-2014 Friday
Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
Inspection Type: Continuous
Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
Federal ID:
Location:
Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
Precipitation Condition Clear

Working Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (9/5/14, Friday - Clear):

* Went to job site (T1 by driving to W2) with Grady this afternoon.

- Saw METS paint inspector Justing at the W2 parking lot, he was on the way to tower traver inspecting paint repair.

- There were 6 CCC's painters working in tower from EL. 143 m down to the EL. 127m for floor paint repair works. CCC will work in coming weekend for N/W shafts D and E faces paint repair (Tower elevator area).

* Paint Crew: Sage Ray, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Daniel Rosales, Abraham Ventura. Crew worked from 6AM to 2:30 PM, 8 hours shift.

* Labores: James Sturgeon, Jose Jr. Avila, Victor Hernandez, and Danny Schwartz worked today (8 hours shift) performing hours keeping works.

- Left T1 around 2:20PM,

* Performed paper work at office, and left office around 4:05 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 355 **Date:** 05-Sep-2014 **Friday**

Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Equipment							Rental Company	
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2292	WELDER, 600 AMP						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2293	WELDER, 600 AMP						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE								
CERTIFIED COATINGS COMPANY								
04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE								
CERTIFIED COATINGS COMPANY								
04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE								
CERTIFIED COATINGS COMPANY								
CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist								
AMERICAN BRIDGE/FLUOR, A JV								

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Liu, Tai-Lin

Diary #: 355 Date: 05-Sep-2014 Friday


Tower north elevator side, area still need paint repair



Traver near W2 elevator area



Elevator side of tower

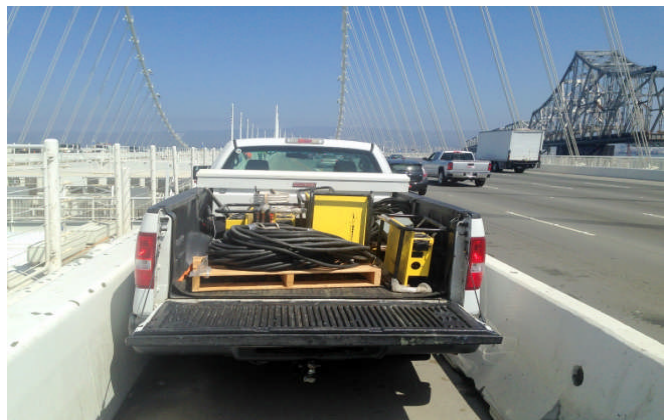

Labor's forman James's truck with unloaded equipment



CCC painters performed paint repair on barrier & piping near tower (North side)



METS paint inspector - Justing went down to traver for inspection - Tower El. 53
