

**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:18 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 356 Const Calendar Day: 826 Date: 08-Sep-2014 Monday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

**04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge****Weather****Temperature** 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80**Precipitation** **Condition** ClearWorking Day ☒ If no, explain:**Diary:**

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (9/8/14, Monday - Clear):

* Attended staff meeting this morning 8:00 - 9:10AM.

* Awal told me that CONCO labor will be in tower base tomorrow around 6:40AM for repairing the concrete crack on tower footing area. Looked into the diaries, spreadsheet & drawings for the unrepaired concrete crack area on tower base footing area.

* Performed paper work, and studied Tower cleaning & paint repair tracking sheets.
Went to job site (T1 by driving to W2 with Grady) around 1:00 PM.

* Took elevator to the deck, and walked to tower El. 53 m area. I saw dozen of CCC painters continued worked on barrier and piping paint repair works near tower area (see pictures).

* At El. 53 m deck area, saw ABF labor forman Victor, James was not in today. There were 3 labores working in tower performing hours keeping work today.

* Saw METS paint inspector Stuart, he told me that there were 6 CCC's painters working in tower in various floor elevations. He checked and bought out the paint repair on floor façade EL. 143 m floor area. Stuart also inspected paint repair on El. 89m, 127m, 135m & 155m steel grating / floor area - some of the area need more work to complete. METS paint inspector Justing came to tower last weekend (9/6 & 9/7) to inspect CCC paint repair works on face D of shafts N/W elevator area.

* Paint Crew: Sage Ray, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez & Abraham Ventura (6) worked from 6AM to 2:30 PM, 8 hours shift.

* Labores: Jose Jr. Avila, Victor Hernandez, and Danny Schwartz (3) worked today (8 hours shift).

* Left T1 around 2:30PM, Performed paper work at office, and left office around 4:05 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 356 **Date:** 08-Sep-2014 **Monday**

Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment

Rental Company

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 356

Date: 08-Sep-2014

Monday

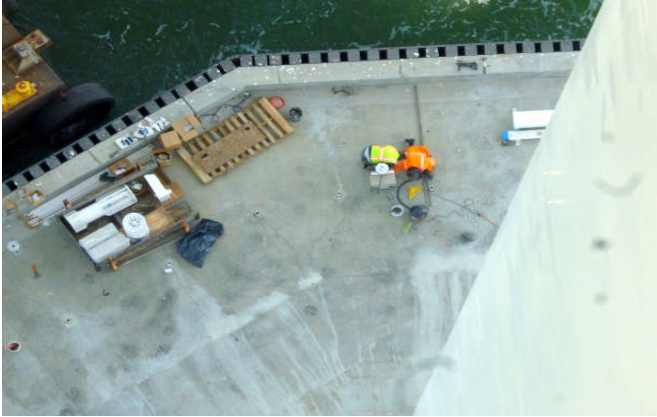

Saw contractor install light fixtures on tower footing area



Painters performed paint repair on cross beam & piping next to tower



METS paint inspector Stuart at tower El. 53m area



Safety engineer Grady & painter on cross-beam next to Tower
