

DEPARTMENT OF TRANSPORTATION**DIVISION OF ENGINEERING SERVICES**

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch

690 Walnut Ave. St. 150

Vallejo, CA 94592-1133

(707) 649-5453

(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-002463**Date Inspected:** 19-Apr-2008**Project Name:** SAS Superstructure**OSM Arrival Time:** 1400**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 2330**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China

CWI Name:	N/A			CWI Present:	Yes	No	
Inspected CWI report:	Yes	No	N/A	Rod Oven in Use:	Yes	No	N/A
Electrode to specification:	Yes	No	N/A	Weld Procedures Followed:	Yes	No	N/A
Qualified Welders:	Yes	No	N/A	Verified Joint Fit-up:	Yes	No	N/A
Approved Drawings:	Yes	No	N/A	Approved WPS:	Yes	No	N/A
				Delayed / Cancelled:	Yes	No	N/A
Bridge No:	34-0006			Component:	OBG/Tower		

Summary of Items Observed:

CALTRANS Quality Assurance (QA) Inspector, Erik Prue was present for the fabrication scheduled for this project at the ZPMC facility in Shanghai, China for the San Francisco Oakland Bay Self Anchored Suspension Bridge.


Tower Bay 1: QA Inspector performed ultrasonic verification testing of the skin plate Complete Joint Penetration (CJP) butt joint after ZPMC QC UT acceptance. QA UT tested plates ESD1 SA216 A/K 16B side "B" and SSD1 SA173 A/K 18B. QA Ultrasonic Testing (UT) was performed to verify that a minimum of 10% of the weld meets the requirements of the contract documents and AWS D1.5-2002. The weld and base metal were scanned utilizing a Krautkramer Branson USN 60 #01RN5T. QA Inspector performed a base metal lamination check using a 25mm diameter 2.25 MHz transducer and a shear wave scan using a 20mm x 15mm 2.25 MHz transducer on a 70 and 45 degree angle wedges from face A. For details please see the ultrasonic testing report TL-6027 dated April 19, 2008. QA Inspector found the welds inspected to be in compliance with AWS D1.5- 2002 Table 6.3 and the contract documents.

Tower Bay 3- QA Inspector performed ultrasonic (UT) verification testing of Deck Panel Complete Joint Penetration (CJP) welds at joints DP491-001-117, DP329-002-153, DP084-001-117, and DP111-001-153 after ZPMC QC acceptable UT inspection. The Ultrasonic Testing (UT) was performed to verify that 10% of the weld meets the requirements of the contract documents and AWS D1.5-2002. The weld and base metal were scanned utilizing a Krautkramer Branson USN 60 #01RN5T. QA Inspector performed a base metal lamination check using a 25mm diameter 2.25 MHz transducer and a shear wave scan using a 20mm x 15mm 2.25 MHz transducer on a 70 degree angle wedge from face A. For details please see the ultrasonic testing report TL-6027 dated April 19,

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

2008. QA Inspector found the welds inspected to be in compliance with AWS D1.5- 2002 Table 6.3 and the contract documents.

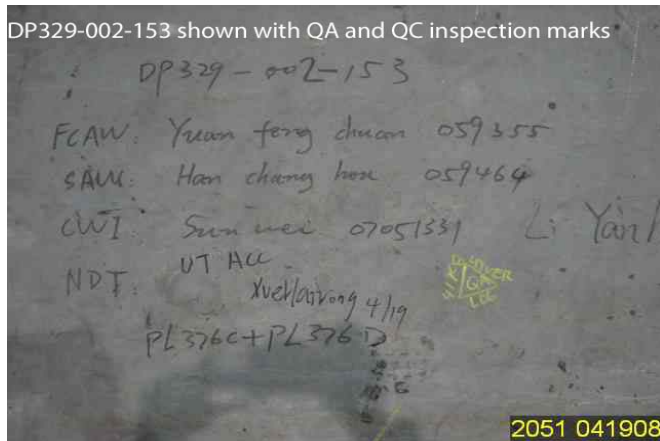

Summary of Conversations:

No significant conversations this day.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Patrick Lowry, 858 344-2712, who represents the Office of Structural Materials for your project.

Inspected By:	Prue,Erik	Quality Assurance Inspector
Reviewed By:	Hager,Craig	QA Reviewer
