

DEPARTMENT OF TRANSPORTATION

DIVISION OF ENGINEERING SERVICES

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493


Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 69.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-002598**Date Inspected:** 11-Apr-2008**Project Name:** SAS Superstructure**OSM Arrival Time:** 630**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1730**Contractor:** Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island **Location:** Shanghai, China**CWI Name:** Chen Xi**CWI Present:** Yes No**Inspected CWI report:** Yes No N/A**Rod Oven in Use:** Yes No N/A**Electrode to specification:** Yes No N/A**Weld Procedures Followed:** Yes No N/A**Qualified Welders:** Yes No N/A**Verified Joint Fit-up:** Yes No N/A**Approved Drawings:** Yes No N/A**Approved WPS:** Yes No N/A**Delayed / Cancelled:** Yes No N/A**Bridge No:** 34-0006**Component:** OBG**Summary of Items Observed:**

Caltrans Quality Assurance (QA) Inspector Sherri Brannon arrived on site at the Zhenhua Port Machinery Company (ZPMC) facility at Changxing Island, in Shanghai, China to periodically monitor welding and Quality Control (QC) functions. While on site the QA Inspector observed and/or discovered the following.

QA Inspector Brannon observed welding utilizing the dual process WPS-B-T-2342-U1 (U-rib)-3 welding procedure specification for closed rib welding of the Production Monitoring Test (PMT) #1 for Production Panel DP353-001 and DP052-001 on closed U-rib Partial Joint Penetration (PJP) welds in Bay #1. ZPMC welding personnel performed Gantry Machine, Gas Metal Arc Welding (GMAW) for the root pass and immediately performed Gantry Machine, Submerged Arc Welding (SAW) for the cover/final pass on PMT #1, using gantry machine #1. Upon completion of the SAW pass on U-rib PJP welds on PMT #1 Visual Testing (VT) was performed on weld #1 through #6 by ZPMC personnel and was accepted then VT was verified by the Caltrans QA inspector. Ultrasonic Testing (UT) was then performed by ZPMC inspector and PMT #1 was determined to be acceptable. Macro etch samples were selected by the Caltrans QA inspector on PMT #1.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

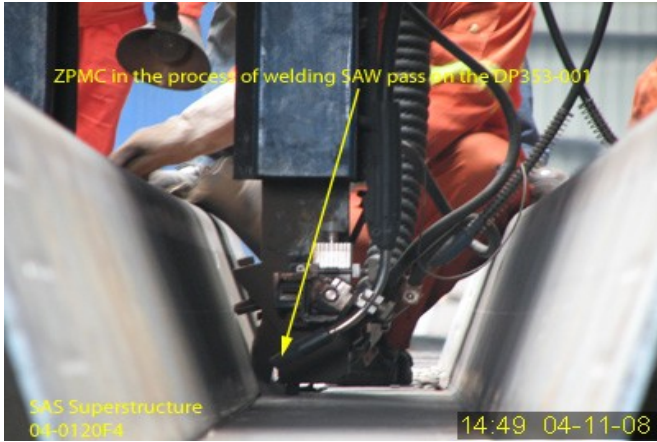

Summary of Conversations:

No relevant conversations to report.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Patrick Lowry, (858) 344-2712, who represents the Office of Structural Materials for your project.

Inspected By:	Brannon,Sherri	Quality Assurance Inspector
Reviewed By:	Cuellar,Robert	QA Reviewer
